



**Bureau of Environmental Health**  
 8930 Stanford Boulevard, Columbia, MD 21045  
 Main: 410-313-2640 | Fax: 410-313-2648  
 TDD 410-313-2323 | Toll Free 1-866-313-6300  
[www.hchealth.org](http://www.hchealth.org)  
 Facebook: [www.facebook.com/hocohealth](http://www.facebook.com/hocohealth)

**Maura J. Rossman, M.D., Health Officer**

RECEIPT DATE: 6/18/2024      **ONSITE SEWAGE DISPOSAL SYSTEM**      P 586719

APPROVAL DATE: 8/13/24      **PERMIT: REPAIR**      A Repair

PROPERTY ADDRESS: 7416 Cherry Tree Drive

SUBDIVISION: Hopkins Meade      LOT: 3      TAX ID: 05-349591

CONTRACTOR: Fogle's      EMAIL: Jeff@foglesinc.com

CONTRACTOR ADDRESS: 580 Obrecht Road, Sykesville 21784      PHONE: 410-795-5670

---

PROPERTY OWNER: Seth Gersuk      EMAIL: Obasic92@hotmail.com

OWNER ADDRESS: Same as above      PHONE: 443-742-4199

SEPTIC TANK SIZE: Existing      PUMP SIZE: n/a      PUMP TANK CAPACITY: n/a


DISTRIBUTION SYSTEM:     GRAVITY     LPD    BEDROOMS: 5    APPLICATION RATE: 1.2gpd/ft

TRENCHES:	LINEAR FEET REQUIRED: <u>155</u>	INLET DEPTH: <u>4</u>
	TRENCH WIDTH: <u>2</u>	MAXIMUM BOTTOM DEPTH: <u>10</u>
	MINIMUM SPACE BETWEEN TRENCHES: <u>12</u>	EFFECTIVE AREA BEGINNING DEPTH: <u>5.5</u>
LOCATION:	<b>SYSTEM STAKED BY INSTALLER/DESIGNER AND VERIFIED BY APPROVING AUTHORITY DURING PRE-CONSTRUCTION INSPECTION.</b>	
NOTES:	Install system per approved design plans.	

ISSUED BY: Kevin M. Wolf, L.E.H.S.      ISSUE DATE: 7/5/2024      EXPIRATION DATE: 7/5/2025

- NOTE: CONTRACTOR MUST SCHEDULE A PRE-CONSTRUCTION INSPECTION PRIOR TO BEGINNING ANY INSTALLATION
- NOTE: CONTRACTOR REGISTERED WITH THE STATE OF MD ON-SITE WASTEWATER PROFESSIONALS BOARD: CONFIRMED
- NOTE: CONTRACTOR MUST SCHEDULE AN INSPECTION AND GAIN APPROVAL OF ALL COMPONENTS PRIOR TO COVERING
- NOTE: STONE MUST BE APPROVED BY HEALTH DEPARTMENT AND GRAVEL TICKET MUST BE AVAILABLE FOR REVIEW.
- NOTE: WATERTIGHT SEPTIC TANKS REQUIRED
- NOTE: ALL PARTS OF SEPTIC SYSTEM SHALL BE AT LEAST 100 FEET DOWNGRADE FROM ANY WATER WELL
- NOTE: MANHOLE RISERS REQUIRED ON ALL SEPTIC TANKS AND PUMP CHAMBERS
- NOTE: AN ELECTRICAL PERMIT IS REQUIRED FOR INSTALLATION OF ANY ELECTRICAL COMPONENTS OF THE SYSTEM  
 ELECTRICAL PERMIT ISSUED    E n/a
- NOTE: THE HCHD DOES NOT WARRANT ANY SYSTEM AND CANNOT GUARANTEE THE PERFORMANCE OF THIS SYSTEM AS DESIGNED. BY ACCEPTING THIS PERMIT, THE OWNER AND/OR APPLICANT ACKNOWLEDGE THAT THE SPECIFICATIONS DETAILED IN THIS DESIGN ARE ONE POSSIBLE OPTION AND THAT THE HCHD WILL REVIEW OTHER PROPOSALS. YOU HAVE THE OPTION TO SEEK THE ADVICE OF A QUALIFIED DESIGN CONSULTANT OR PROFESSIONAL ENGINEER FOR FURTHER GUIDANCE.
- NOTE: AN INDIVIDUAL CERTIFIED BY MDE AND THE MANUFACTURER FOR BAT INSTALLATION MUST BE PRESENT AT ALL TIMES DURING BAT INSTALLATION.
- NOTE: MDE RECOMMENDS SEPTIC TANKS, BAT, AND OTHER PRETREATMENT UNITS BE PUMPED AT A FREQUENCY ADEQUATE TO ENSURE THAT SOLIDS ARE NOT DISCHARGED TO THE DISPOSAL AREA

**NEITHER THE HOWARD COUNTY COUNCIL NOR THE HEALTH DEPARTMENT IS RESPONSIBLE FOR THE SUCCESSFUL OPERATION OF ANY SYSTEM.**  
**PERMITTEE RESPONSIBLE FOR OBTAINING FINAL APPROVAL ON THIS PERMIT.**  
**CALL 410-313-1771 TO SCHEDULE INSPECTIONS.**

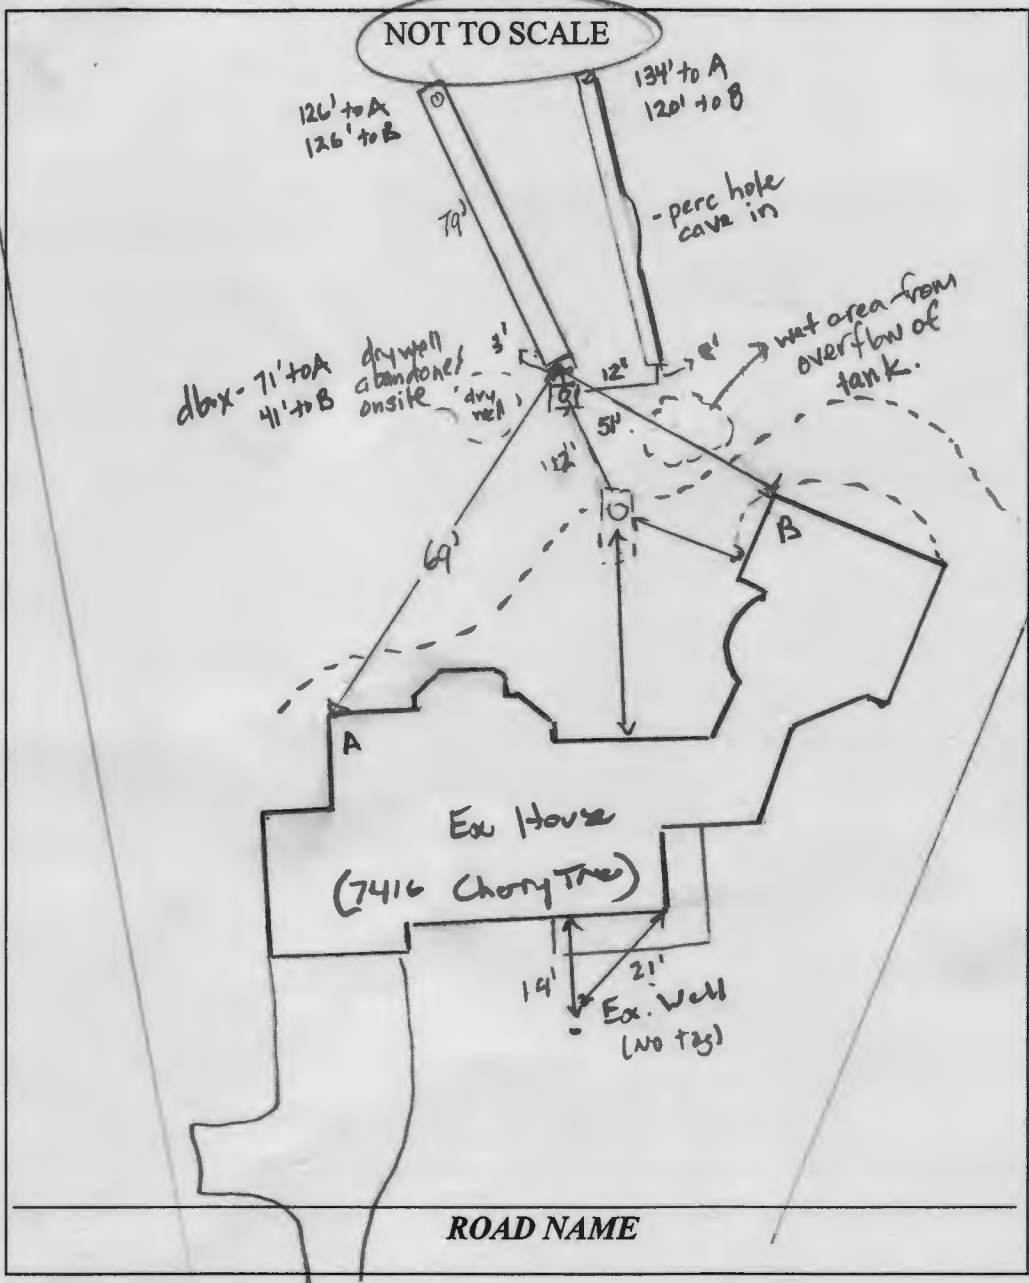

TRENCH/DRAINFIELD DATA		
WIDTH	INLET	BOTTOM
2'	4'	10'
NUMBER OF TRENCHES		2
TOTAL LENGTH		158'
ABSORPTION AREA		316 sq ft + Siderail
DISTRIBUTION BOX LEVEL		Yes
DISTRIBUTION BOX BAFFLE		Yes
DISTRIBUTION BOX PORT		Yes

SEPTIC TANK DATA	
SEPTIC TANK 1 LEVEL	Existing
MANUFACTURER	
CAPACITY	GAL
SEAM LOC	
TANK LID DEPTH	
BAFFLES	
BAFFLE FILTER	
MANHOLE LOC	
6" PORT LOC	
WATERTIGHT TEST	
SLOTTED	
DATE ON LID	
PUMP/SEPTIC TANK LEVEL N/A	
MANUFACTURER	
CAPACITY	GAL
SEAM LOC	
TANK LID DEPTH	
BAFFLES	
BAFFLE FILTER	
MANHOLE LOC	
6" PORT LOC	
WATERTIGHT TEST	
SLOTTED	
DATE ON LID	

SEPTIC CONTRACTOR ONSITE INSTALLING SYTEM: Mike  
 SEPTIC CONTRACTOR ONSITE LICENSED WITH THE STATE OF MD: YES/NO

PRE-CONSTRUCTION NOTES:  
7/5/2024 Design plan approved (KRM)

8/6/2024 - installer onsite. trench closest to drywell on contour. Homeowner wanted to move trench closer to perc to avoid getting perc down, moved trench 6'-8", straggled off. Siderail & pipe line both trenches lengths @ 80', on contour by 4"-3". Distance between trenches 20' - OK to stragg (SPMB?)

INSTALLATION NOTES:  
 8/17/2024 - installer onsite. Upper trench finished, stone & fabric OK. inlet @ 4", length @ 79' OK to backfill (SPMB) 8/13/24 - contractor onsite working on the demo of the drywell it's being filled in w/ small #2 stone and clean fill from the site. The 2nd trench was completed w/ geotextile fabric & small #2 stone (double washed), 2nd trench moved on contour a bit further away from the 1st trench, dbx levels OK, 2nd trench ran through the perc hole so it was wider than 2 feet; wet spot in yard was where the sewage overflow was pooling (see as built)

CONTROL PANEL DATA	
CONTROL PANEL HEIGHT	
(MIN 30")	
INSPECTION DATE	
INSPECTION: PASS/FAIL (CIRCLE ONE)	

FINAL INSPECTOR R. Rappaport DATE OF APPROVAL 8/13/24  
 Contractor stated that the septic tank already had a plastic 4" baffle in the back. Contractor sealed riser w/ hydraulic cement, inlet ok, observation pipes in place OK to backfill (KRM)



# HOWARD COUNTY HEALTH DEPARTMENT

86718

CODES

DATE

6/18/24

25

CASH

CHECK

NO.

86420

Received From

torles Septic Clean Inc

For

Per Rep - 7/10/24 (very recent)

Two hundred sixty five

Dollars

\$

26500

Received By

*[Handwritten Signature]*



# HOWARD COUNTY HEALTH DEPARTMENT

86719

CODES

DATE

6/18/24

CASH

CHECK

Received From

Taylor Joseph (1) Health Inc

NO.

For

Books - HHA (1) Health Inc

50420

Two hundred eighty five Dollars

\$

2500

Received By

*[Signature]*

# Repair System Design Plan

No wells within 100'  
 5 Bedrooms  
 Trench Detail  
 160'- Total length  
 2 - 80' Each  
 2'- wide  
 10'- Trench depth  
 6'- Stone below pip  
 3 1/2'- cover

Drop off to HCHD on 7-2-24

**FOGLE'S**

**Installer Information**  
 Fogle's Septic Clean, Inc.  
 580 Obrecht Rd  
 Sykesville, MD 21784  
 Phone: 410-795-5670  
 Email: john@foglesinc.com

**Homeowner Information**  
 Name: Seth Gersuk  
 Phone: 443-742-4199  
 Email: qbasic92@hotmail.com

**Property Information**  
 7416 Cherry Tree Dr  
 Clarksville, MD 21029  
 Bedrooms: 5  
 HCHD Permit: P586718/P586719  
 Perc Date: 06/27/2024

Approved Septic System Plan  
 Howard County Health Department

*K. P. Hoff* 7/5/2024  
 Signature Date

