

Approved
MRE 9/16/25

Record Detail * (This section is required.)

Permit Type	Permit Number	Opened Date
Building/Residential/Misc/Pool Spa	B25003143	08/08/2025
Description of Work		
SFD/ construct 15' x 35' inground pool W/ 6 X 8 spa, 4' aluminum fence TO CODE, 3,000 SQ FT pool patio**SUBJECT TO FIELD INSPECTION**		

Online BP.
g8 8/13/25

[check spelling](#)

Address * (This section is required.)

Search Reset Clear Get Parcel & Owner

Street #	Street Name	Street Type	
5018	TEN OAKS	RD	
Unit Type	Unit #	X Coordinate	Y Coordinate
--Select--		-76.98043	39.23169
City	State	Zip Code	Primary
CLARKSVILLE	MD	21029	Yes

Parcel * (This section is required.)

Search Reset Clear Get Address & Owner

GIS ID *	Parcel	Parcel Area	Land Value	Improved Value	Exemption Value	Plan Area
11059187	140	3.03	296300	1742900	1446600	RURAL
Legal Description						
IMPSLOT 5 3.025 A.[]5018 TEN OAKS RD[]TEN OAKS FARM						

[check spelling](#)

Block	Lot	Census Tract	Council Dist	Inspection Dist	Supervisor Dist	Map #	DAP Zone
	5	605101	5				
Plan Area	State Tax Id	Subdivision Name					
	1405601265	Ten Oaks Farm					
Section	Area	Tax Map					
		28					
Grid	Zoning District	ADC Map					
28-14	RR-DEO	4933-D3					
SDP No.	Final Plan No.	WP File No.					
	ECP-16-013						
Record Plat No.	WS Contract No.	FDP No.		Primary			
24785-2478				Yes			
Owner Occupied	Year Built	Historic District					
<input type="radio"/> Yes <input type="radio"/> No	2024	<input type="radio"/> Yes <input checked="" type="radio"/> No					
Historic District Registry No.	Stat Area	Flood Plain					
	5-04A	<input type="radio"/> Yes <input checked="" type="radio"/> No					
Building No							

Owner * (This section is required.)

Search Reset Clear

Name *
ADJAP

Address Line 1
5018 TEN OAKS RD

Address Line 2

Address Line 3

Mail City
CLARKSVILLE

Mail State
MD

Mail Zip Code
21029

Phone
443-535-2193
Primary
Yes
E-mail

Cell Number Fax Number

Professionals (This section is not required.)

License # * Business Name
08010118655 OASIS LANDSCAPE GROUP LLC
License Type * First Name Middle Name Last Name
MHIC Ind ALEX MEWSHAW
Primary Address Line 1
Yes 2444 SOLOMON'S ISLAND RD STE216
Address Line 2

City State ZIP Code
ANNAPOLIS MD 21401-0000
Phone 1 Phone 2 Fax
4439261442
E-mail
ALEX@OASISLANDSCAPE.COM

Applicant (This section is not required.)

Search As Owner As Lic. Prof As Contact

Type * First Name MI Last Name
Applicant Victor Skinner
Relationship Full Name
Applicant Victor Skinner
Primary Organization Name
Yes Scorpion Designs
Street Address
7808 Beddington Ct
Address Line 2

City State Zip Code
Clinton MD 20735
Phone Cell Fax
240-804-7350
E-mail *
designingscorpion@gmail.com

Addtl Info

Est Construction Cost * Housing Units * Number of Buildings * Public Owned
40000 0 0 No
Construction Type
649 - All Other Buildings and Structures

POOL INFORMATION

MISCELLANEOUS POOL INFORMATION


Capital Project-No Fee * Capital Project Number Fee Exempt * Water Supply * Sewage Disposal *
 Yes No (Text) Yes No Private Private
Existing Use * Type of Pool or Spa * Pool Safety Device * Electrical Permit Number Expiration Date
SFD In Ground Pool and Hot Tub Fence (Text) 2/7/2026

Submit Cancel


2406.5382
LOCATION DRAWING
HOWARD COUNTY

PLEASE NOTE
Per Maryland State Code, Sec. 09.13.06.06, this House Location Drawing is not to be relied upon to determine property boundaries or the establishment or location of existing or future improvements.

SCALE: 1"=60'

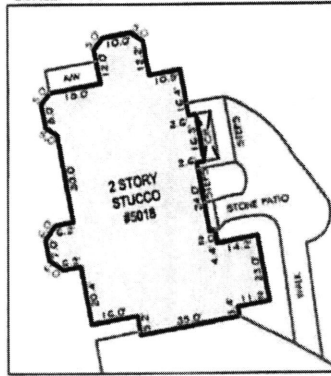

LOT 6

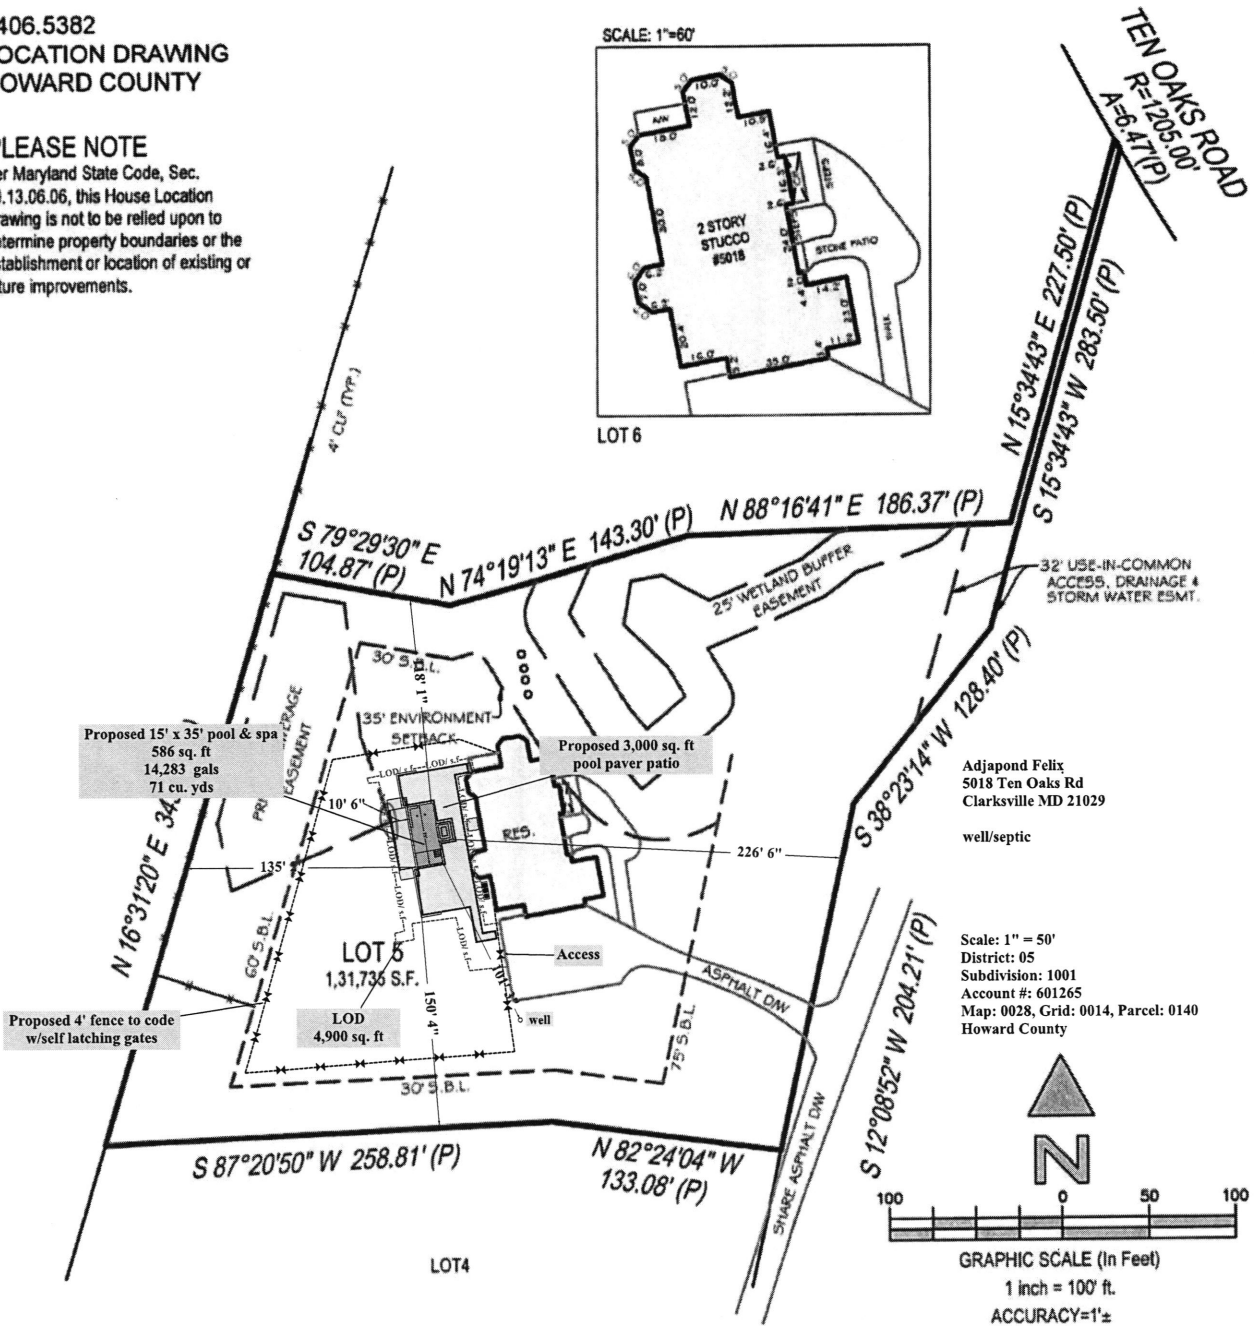

Matthew Nigel Brien
State of Maryland Professional Land Surveyor
License Number 21406

SURVEYORS CERTIFICATION:
THE INFORMATION SHOWN HEREON HAS BEEN BASED UPON THE RESULTS OF A FIELD INSPECTION PURSUANT TO THE DEED OR PLAT OF RECORD. THIS PLAT WAS PREPARED UNDER MY DIRECT SUPERVISION IN ACCORDANCE WITH C.O.M.A.R. SECTION 09.13.06.06 AS NOW ADOPTED BY THE MARYLAND BOARD FOR PROFESSIONAL LAND SURVEYORS AND IS OF BENEFIT TO A CONSUMER ONLY INsofar AS IT IS REQUIRED BY A LENDER OR A TITLE COMPANY IN CONNECTION WITH CONTEMPLATED TRANSFER, FINANCING OR REFINANCING THE PROPERTY DEPICTED HEREON.

POINTS OF INTEREST:
NONE VISIBLE



Exacta Land Surveyors, LLC
LN#21937
office: 443.819.3994
4424 Ventura Way, Apt L | Aberdeen, MD 2100



DATE SIGNED: 06/28/24
FIELD WORK DATE: 6/27/2024
REVISION DATE(S): (REV.1 6/28/2024)

SEE PAGE 2 OF 2 FOR LEGAL DESCRIPTION
PAGE 1 OF 2 - NOT VALID WITHOUT ALL PAGES

BACKYARD RENOVATION


5018 Ten Oaks Road,
Clarksville, MD 21029




FRONT SIDE (STREET VIEW)




RETAINING WALL - PROPOSED

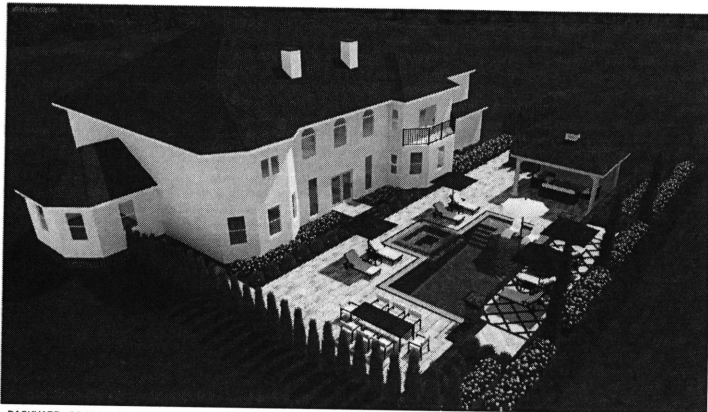

BACKYARD - PROPOSED



CITY MAP



VICINITY MAP

Drawing Issue

CONSTRUCTION SET

Applicable Codes

2021 International Residential Code (IRC)
2021 International Building Code (IBC)
2021 International Energy Conservation Code (IECC)
2021 International Mechanical Code (IMC)
2021 International Fuel Gas Code (IFGC)
2021 International Plumbing Code (IPC)
2021 International Green Construction Code (IgCC)
2021 International Private Sewage Disposal Code (IPSDC)
2021 International Property Maintenance Code (IPMC)
2021 International Existing Building Code (IEBC)
2020 National Electric Code (NEC, NFPA 70)
2018 NFPA 101 Life Safety Code

Building Data

	EXISTING	PROPOSED
BASEMENT	SF	0 SF
1ST FLOOR	SF	0 SF
2ND FLOOR	SF	0 SF
TOTAL	12 000 SF	0 SF

STORIES: 2

Index of drawings

G01 COVER SHEET
G02 SITE PLAN

S01 DIMENSIONS
S02 FOUNDATION PLAN
S03 STRUCTURE PLAN
S04 POOL SECTIONS
S05 POOL SECTIONS
S06 RETAINING WALL DETAILS

Project Description

- Structural drawings of the pool and material specifications.
- Structural drawings for retaining wall and material specifications.

General Notes

- The drawings and specifications herein provide graphic and written requirements for the execution of The Work by The Contractor. They are intended to be used together and shall have equal force. Any discrepancies between them shall be reported to The Owner or Owner's Representative before commencing work.
- All dimensions are to face of finished wall, unless noted otherwise.
- The Contractor shall be responsible for executing The Work as drawn and specified in The Contract Documents and shall be liable for any unapproved deviation from the drawings and specifications therein. Any planned deviation from The Contract Documents shall be brought to the attention of The Owner prior to implementation and shall be undertaken only with the written consent of The Owner.
- The Contractor shall have sole responsibility and control over construction means, methods, techniques, sequences and coordination of all portions of The Work.
- The Contractor shall visit site prior to commencing Work to take field measurements and verify field dimensions for horizontal and vertical control, and shall report any discrepancies to the owner.
- The Contractor shall continue operations at The Site to the limits of the project site as described on the drawings and shall protect adjoining property from damage.
- All materials and workmanship shall comply with applicable building codes.
- The building and grounds shall be kept clean at all times. After completion of The Contract and before receiving final payment, The Contractor shall remove from the premises trash rubbish, tools, equipment and excess materials. The building and grounds shall be left in perfectly clean condition.
- The Contractor shall store materials in a safe and dry location and shall be responsible for protecting equipment, materials and partially or fully completed work of all trades.
- The Contractor shall be responsible for verifying field measurements before ordering materials and prefabricated items. Any necessary adjustments between field measurements and drawings shall be coordinated with The Owner or Owner's Representative.
- All specified products and systems shall be installed according to manufacturer's written instruction; including, but not limited to instructions regarding preparation of substrates and adjoining construction, weather conditions and protection after installation.
- The Contractor shall furnish and install all necessary materials, labor and equipment for a complete mechanical and electrical system.
- The Contractor shall coordinate with The Owner & Architect the final selection of hardware, fixtures, finishes and accessories not specified.
- The Contractor shall guarantee, for the period of one year after the date of completion and final acceptance by The Owner, all workmanship and materials, and shall repair or replace at no additional cost The Owner any part thereof which may become defective.
- All equipment warranties and maintenance manuals shall be given to The Owner. Warranty periods shall begin upon completion of Work.
- The Owner shall obtain and pay for the building permit, The Contractor shall be responsible for obtaining and paying for all other permits and shall obtain all required building department inspections.
- The Contractor is responsible for all temporary shoring design and construction.



12001 Golden Twig Ct.
North Potomac, MD 20679
Contact: Aaron Jassat, MS, PE
web: www.triplejconsulting.com
e-mail: aaron@triplejconsulting.com
phone: 240 854 2811

OWNER:
Adjapong Feix
5018 Ten Oaks Road
Clarksville, MD 21029

STRUCTURAL ENGINEER:
Aaron Jassat, MS, PE
web: www.triplejconsulting.com
e-mail: aaron@triplejconsulting.com
phone: 240 854 2811

BACKYARD RENOVATION
5018 Ten Oaks Road,
Clarksville, MD 21029

PROJECT NORTH


SCALE:
PROJECT NO.: 25-000
DATE: 07/28/2025



I hereby declare these documents were prepared or approved by me, and that I am a duly licensed engineer under the laws of the state of Maryland. License number 14787, expiration date 8/30/27

COVER SHEET

G01

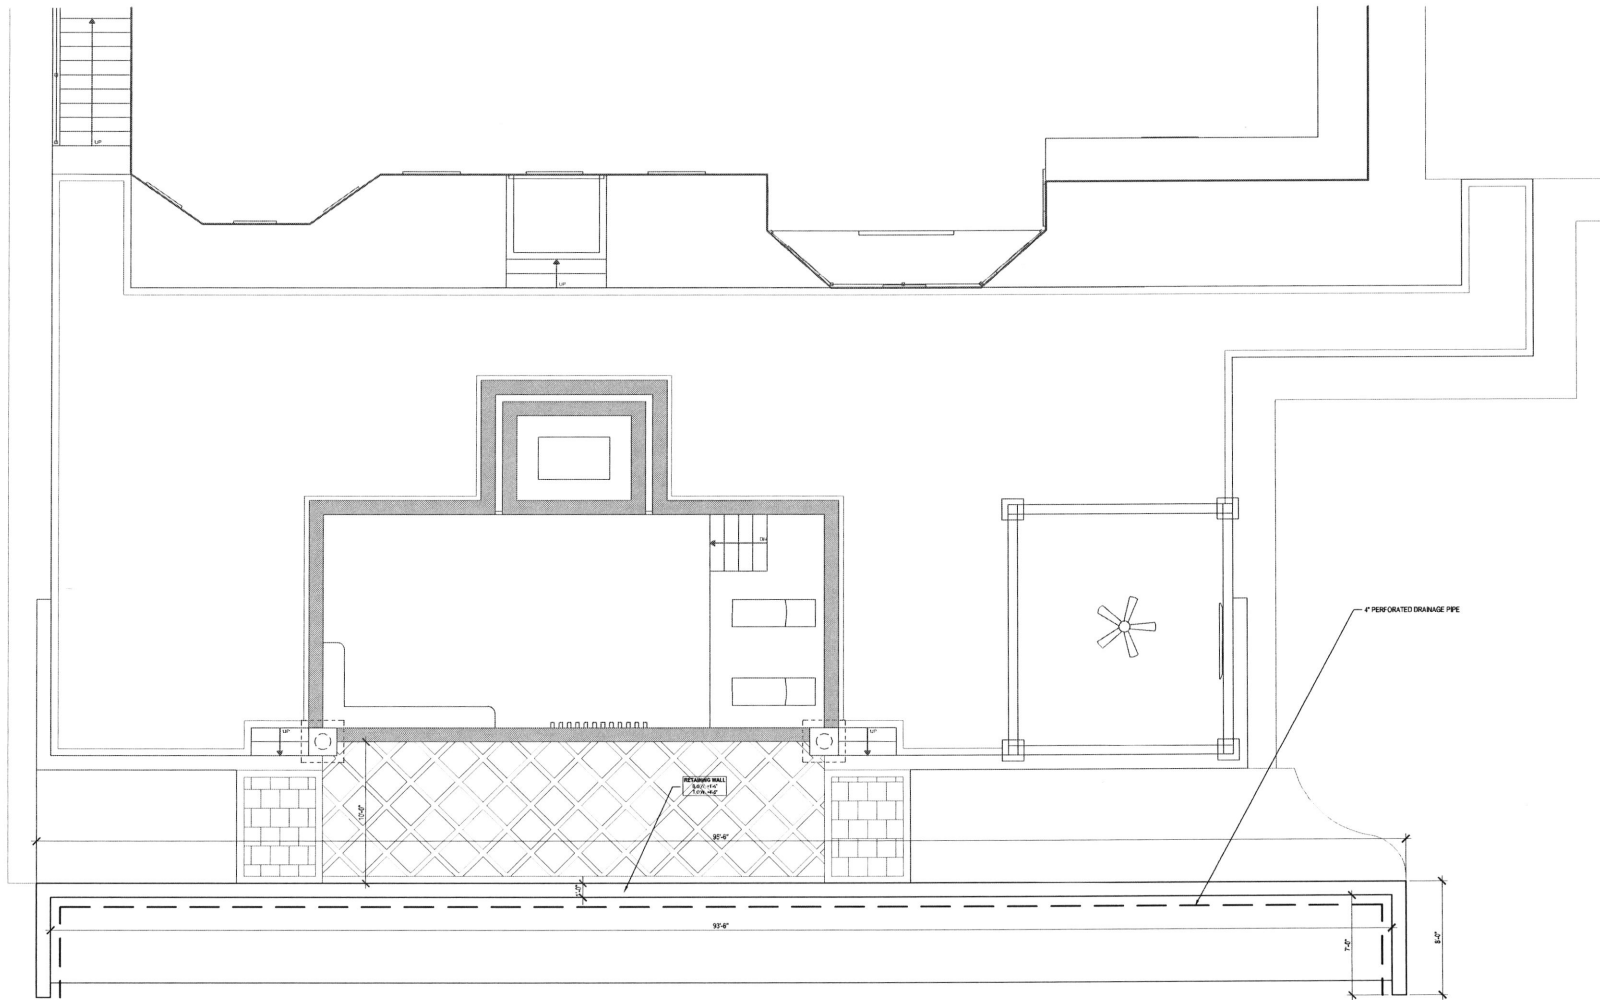

1 FOUNDATION PLAN - PROPOSED
 302 SCALE: 1/4" = 1'-0"



12021 Golden Twig Ct.
 Hunt Valley, MD 20939
 Contact: Azam Javed, MS, PE
 web: www.triplejconsulting.com
 e-mail: ajaved@triplejconsulting.com
 phone: 240 604 2821

OWNER:
 Kippang Park
 5018 Ten Oaks Road
 Clarksville, MD 21029

STRUCTURAL ENGINEER:
 Azam Javed, MS, PE
 web: www.triplejconsulting.com
 e-mail: ajaved@triplejconsulting.com
 phone: 240 604 2821

BACKYARD RENOVATION
 5018 Ten Oaks Road,
 Clarksville, MD 21029

PROJECT NORTH: 
 SCALE: AS MENTIONED
 PROJECT NO.: 25 - 000
 DATE: 07/26/2025



I certify that these documents were prepared or approved by me, and that I am a duly licensed engineer under the laws of the state of Maryland. License number 84707, expiration date 04/30/2027.

FOUNDATION PLAN

S02



2025 Columbia, MD 21046
 Contact: Apple V Consulting, LLC
 Address: 5015 Ten Oaks Road, Clarksville, MD 21029
 Phone: 410.326.8251

PROJECT NO: 2025-001
 DATE: 02/28/2025
 SCALE: AS SHOWN
 PROJECT NO: 25-006
 DATE: 02/28/2025

BACKYARD RENOVATION

5018 Ten Oaks Road,
 Clarksville, MD 21029


PROJECT NO: 25-006
 DATE: 02/28/2025



Professional Engineer
 License No. 14787
 State of Maryland
 Adam J. Sells
 02/28/2025


STRUCTURE PLAN

S03

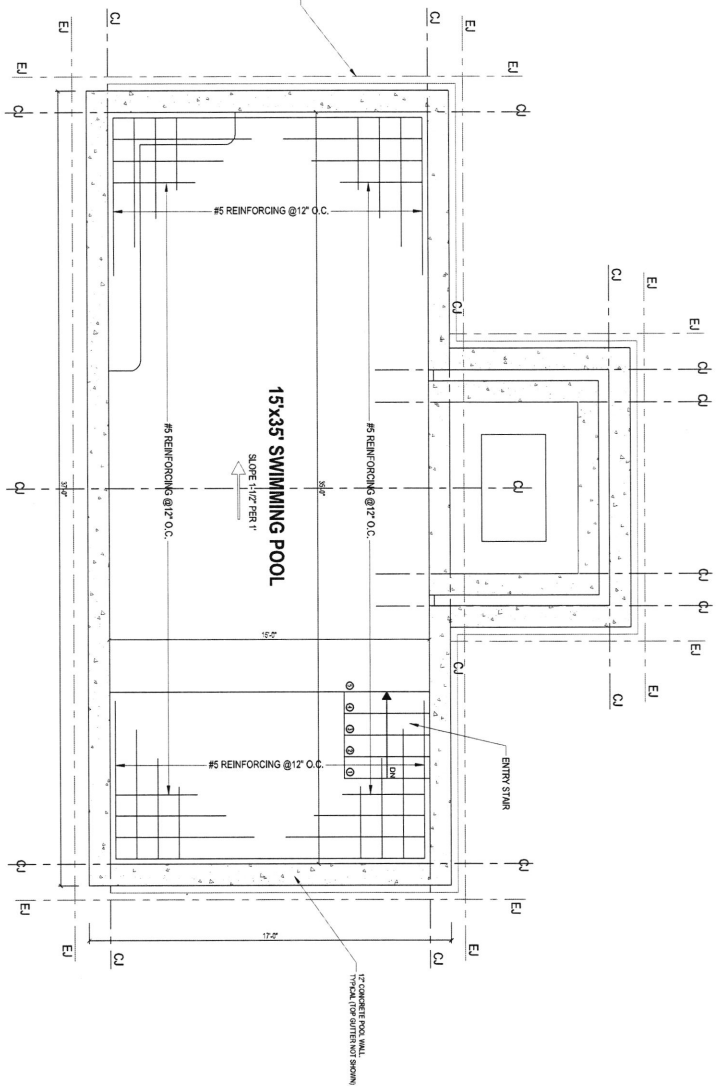

NOTE:
 ALL SHOWN POOL WALLS &
 REINFORCING SHALL BE
 CONCRETE. SEE SECTION
 05100 FOR CONCRETE
 REINFORCING DETAILS.
 REINFORCING SHALL BE
 #5 BARS @ 12\"/>

1 POOL STRUCTURE PLAN
 SCALE: 3/8" = 1'-0"



Bureau of Environmental Health
 8930 Stanford Boulevard, Columbia, MD 21045
 Main: 410-313-2640 | Fax: 410-313-2648
 TDD 410-313-2323 | Toll Free 1-866-313-6300
 www.hchealth.org
 Facebook: www.facebook.com/hocohealth

Maura J. Rossman, M.D., Health Officer

RECEIPT DATE: 10-31-22 **ONSITE SEWAGE DISPOSAL SYSTEM** P 572673
 APPROVAL DATE: 7/17/2024 **PERMIT: CONSTRUCTION** A _____
 PROPERTY ADDRESS: 5018 Ten Oaks Road
 SUBDIVISION: Ten Oaks Farm LOT: 5 TAX ID: _____
 CONTRACTOR: Allright Plumber Heating EMAIL: _____
 CONTRACTOR ADDRESS: 3rd Kings Park Rd, Randallstown, MD 21133 PHONE: 443-622-1842
 PROPERTY OWNER: Villa Building Group EMAIL: Vince
 OWNER ADDRESS: 6822 Green Hollow Way, Highland, MD 20777 PHONE: 443-832-8168
 SEPTIC TANK SIZE (GALLONS): 2000 TANK MANUFACTURER: Babylon
 PUMP MODEL: Zoeller PUMP SIZE: 0.4 PUMP TANK CAPACITY: 2000

DISTRIBUTION SYSTEM: GRAVITY PRESSURE DOSED BEDROOMS: 6 APPLICATION RATE: 1.2

TRENCHES:	LINEAR FEET REQUIRED: <u>95'</u>	INLET DEPTH: <u>3.5</u>
	TRENCH WIDTH: <u>3</u>	MAXIMUM BOTTOM DEPTH: <u>8</u>
	MINIMUM SPACE BETWEEN TRENCHES: <u>10</u>	EFFECTIVE AREA BEGINNING DEPTH: <u>3.5</u>
LOCATION:	PER APPROVED SITE PLAN. SEWAGE DISPOSAL AREA AND TANK LOCATIONS MUST BE STAKED BY LICENSED SURVEYOR PRIOR TO PRE-CONSTRUCTION INSPECTION.	
NOTES:	Install 2 trenches @47.50 LF	

ISSUED BY: Hank Oswald ISSUE DATE: 10-31-22 EXPIRATION DATE: 10-31-23

- NOTE: CONTRACTOR MUST SCHEDULE A PRE-CONSTRUCTION INSPECTION PRIOR TO BEGINNING ANY INSTALLATION
- NOTE: CONTRACTOR MUST SCHEDULE AN INSPECTION AND GAIN APPROVAL OF ALL COMPONENTS PRIOR TO COVERING
- NOTE: STONE MUST BE APPROVED BY HEALTH DEPARTMENT AND GRAVEL TICKET MUST BE AVAILABLE FOR REVIEW.
- NOTE: WATERTIGHT TANKS REQUIRED
- NOTE: ALL PARTS OF SEPTIC SYSTEM SHALL BE AT LEAST 100 FEET DOWNGRADIENT FROM ANY WATER WELL
- NOTE: MANHOLE RISERS REQUIRED ON ALL SEPTIC TANKS AND PUMP CHAMBERS
- NOTE: AN ELECTRICAL PERMIT IS REQUIRED FOR INSTALLATION OF ANY ELECTRICAL COMPONENTS OF THE SYSTEM
 ELECTRICAL PERMIT ISSUED E 22004566
- NOTE: MDE RECOMMENDS SEPTIC TANKS, BAT, AND OTHER PRETREATMENT UNITS BE PUMPED AT A FREQUENCY ADEQUATE TO ENSURE THAT SOLIDS ARE NOT DISCHARGED TO THE DISPOSAL AREA

NEITHER THE HOWARD COUNTY COUNCIL NOR THE HEALTH DEPARTMENT IS RESPONSIBLE FOR THE SUCCESSFUL OPERATION OF ANY SYSTEM.
 PERMITTEE RESPONSIBLE FOR OBTAINING FINAL APPROVAL ON THIS PERMIT.
 CALL 410-313-1771 TO SCHEDULE INSPECTIONS.

NOT TO SCALE

TRENCH/DRAINFIELD DATA

WIDTH	INLET	BOTTOM
<u>3.0'</u>	<u>3.5'</u>	<u>8.0'</u>
NUMBER OF TRENCHES		<u>2</u>
TOTAL LENGTH		<u>94</u>
ABSORPTION AREA		<u>282 ft²</u>
DISTRIBUTION BOX LEVEL		<u>—</u>
DISTRIBUTION BOX BAFFLE		<u>—</u>
DISTRIBUTION BOX PORT		<u>yes</u>

TBC.

SEPTIC TANK DATA

SEPTIC TANK 1 LEVEL	<u>yes</u>
MANUFACTURER	<u>Babylon</u>
CAPACITY	<u>2,000</u> GAL
SEAM LOC	<u>Top</u>
TANK LID DEPTH	<u>12-24"</u>
BAFFLES	<u>yes</u>
BAFFLE FILTER	<u>NA</u>
MANHOLE LOC	<u>Front/Rear</u>
6" PORT LOC	<u>None</u>
WATERTIGHT TEST	<u>N/A</u>
SLOTTED	<u>yes</u>
DATE ON LID	<u>9/23/2022</u>
PUMP/SEPTIC TANK LEVEL	<u>yes</u>
MANUFACTURER	<u>Babylon</u>
CAPACITY	<u>2,000</u> GAL
SEAM LOC	<u>Top</u>
TANK LID DEPTH	<u>16"</u>
BAFFLES	<u>N/A</u>
BAFFLE FILTER	<u>N/A</u>
MANHOLE LOC	<u>Front/Rear</u>
6" PORT LOC	<u>None</u>
WATERTIGHT TEST	<u>N/A</u>
SLOTTED	<u>No</u>
DATE ON LID	<u>9/30/2022</u>

See separate sheet
for As-Built

ROAD NAME

PRE-CONSTRUCTION:

11/10/2022 called contractor - do yard work for layout. He said the system was already installed, will just turn on site to access. done

INSTALLATION:

11/10/2022 Contractor on site. trenches completed & stoned. Traps set in 10" box has to be changed. Force main needs to be installed correctly. 2" force main should be installed instead of the 4". Pump not set. Call in for reinspection. SP/MLW

11/15/2022 - 2" FM installed. Pump was set. Alarm not wired. mentioned to contractor about installing floats on float tree. OK to cover all with. (Call for P & A test - SP/MLW) 7/17/2024 - Electrician onsite for P&A. Audible & visual high water alarm successful. Pump to do box wires (SP)

FINAL INSPECTOR S. Page / M. Burns

DATE OF APPROVAL 7/17/2024

Maura J. Rossman, M.D., Health Officer

APPLICATION FOR WAIVER

To Howard Co Code Subtitle 8: Onsite Sewage Disposal Systems and Subtitle 9: Individual Potable Water Supply Systems

Date Submitted: 8/18/25
 Property Address: 5018 Ten Oaks Road, Clarksville MD 21029
Ten Oaks Farm 5 28 14 140 601265
 Subdivision Lot Tax Map Grid Parcel Tax Account #

Provide a brief site history including previously submitted and active plans with the Health Department or the County (subdivision plans, perc test applications, Building Permit applications):

See attached letter

In the area below, list the specific section of the Howard Co Code to which a waiver is being requested and provide a brief summary of the regulation and an explanation of why the waiver is being requested (Attach a separate sheet if necessary).

Regulation Section	Summary and Explanation
1. <u>See 3.808(c)</u>	<u>Requesting a 10' setback reduction from septic area to pool.</u>
2. _____	_____

Property Owner's Signature

Health Department Use Only

Reviewed by Melanie Kshenbaum 8/20/25
 HCHD Staff Date

Comments/Conditions: approved - SDA must be fenced off prior to BP sign off. OSDS free main will be close to pool + patio. If it is hit during construction, contractor must pull a minor septic repair permit to fix

Approved by: [Signature] 8/25/25
 BEH Deputy Director Date

Felix Adjapong
5018 Ten Oaks Rd, Clarksville MD 21029
(443) 535 2193
Jun 13, 2025

Jeff Williams
Howard County Health Department

Request for 10' Setback Waiver for Pool Installation

Dear Mr. Williams,

I am writing to formally request a waiver for a reduced setback distance of 10 feet between the pool installation and the septic area on my property. Currently, the requirement is for a 20-foot setback, but due to certain constraints on my property, I am seeking permission for a reduced setback as stated.


I understand the importance of maintaining proper distances between pools and septic systems to ensure safety and compliance with health regulations. However, I would like to provide specific reasons and assurances regarding this request:

1. **Property Layout:** The layout of my septic reserve area limits the available space for the pool installation. A 10-foot setback would significantly enhance the feasibility of this project without compromising the functionality and safety of the septic system.
2. **Professional Evaluation:** I have consulted with a licensed contractor who has assessed the site and confirmed that a 10-foot setback would be sufficient for the pool installation without posing any risks to the septic system.
3. **Safety Measures:** I am committed to implementing additional safety measures, such as reinforced barriers or fencing, to ensure the protection and integrity of the septic system during and after the pool installation.
4. **Compliance with Other Standards:** The pool installation will fully comply with all other relevant health and safety standards, including those related to water quality and drainage.

I kindly request that you review this waiver request with consideration of the outlined reasons. I am prepared to provide any additional information or documentation that may assist in the evaluation process.

Thank you for considering my request. I am eager to proceed with this project and am committed to adhering to all necessary regulations and guidelines. Please feel free to contact me at (443) 535 2193 / felix_adjapong2002@yahoo.com or my pool builder (443) 926 1442 / agreen@liveoasis.com if you require further information or clarification.


I look forward to your favorable response.
Warm regards,
Felix Adjapong



SITE INSPECTION SHEET

OWNER: Felix Adjapang PHONE #: _____
ADDRESS: 5018 Ten Oaks CONTRACTOR: _____
WELL TAG #: _____
SUBDIVISION: _____ LOT: 5 COUNTY #: Howard
PROPOSAL: Pool, retaining wall & Pavillia

LOCATION DIAGRAM



COMMENTS: well cap not secured / water tight!
well cap will need belts to secure to casing
missing a couple bolts. No concerns with
septic. As built drawing measurements are off
a little bit.

DATE: 8/18/25 INSPECTOR: Melanie Fishback

Eshenbaugh, Melanie

From: Abby Green <agreen@liveoasis.com>
Sent: Tuesday, September 16, 2025 10:55 AM
To: Eshenbaugh, Melanie
Subject: Re: B25003143

WARNING!!!

This email originated from someone outside of Howard County
*****DO NOT CLICK LINKS OR OPEN ATTACHMENTS*****
unless you recognize the sender and know for sure that the content is safe

Good Morning Melanie,

The safety fence is along the approved SDA based on the siteplan.

On Tue, Sep 16, 2025 at 10:52 AM Eshenbaugh, Melanie <MEshenbaugh@howardcountymd.gov> wrote:

Good Abby,

Thank you for sending these photos to me and the well photo looks good. I wanted to confirm whether the fencing was the approved SDA area or just the existing septic system. Is it difficult to determine based on the other orange fencing photo provided. Please let me know so that I can schedule a site visit if necessary. Hope you have a wonderful day.

Melanie Eshenbaugh

Bureau of Environmental Health

Howard County Health Dept.

8930 Stanford Blvd. Columbia, MD 21045

www.hchealth.org



CONFIDENTIALITY NOTICE

This message and the accompanying documents are intended only for the use of the individual or entity to which they are addressed and may contain information that is privileged, confidential, or exempt from disclosure under applicable law. If the reader of this email is not the intended recipient, you are hereby notified that you are strictly prohibited from reading, disseminating, distributing, or copying this communication. If you have received this email in error, please notify the sender immediately and destroy the original transmission.

From: Abby Green <agreen@liveoasis.com>
Sent: Friday, September 12, 2025 1:08 PM
To: Eshenbaugh, Melanie <MEshenbaugh@howardcountymd.gov>
Cc: Victor Skinner <designingscorpion@gmail.com>
Subject: Re: B25003143

WARNING!!!

This email originated from someone outside of Howard County
*****DO NOT CLICK LINKS OR OPEN ATTACHMENTS*****
unless you recognize the sender and know for sure that the content is safe

Good Afternoon Melanie,

Attached are the photos of the well cap (secured by a licensed plumber) along with the orange safety fence installed around the SDA, which will remain completely avoided during construction.


Please let me know if you need anything further in order to move forward with approval.

Thanks,

Abby

 Adjapong.zip



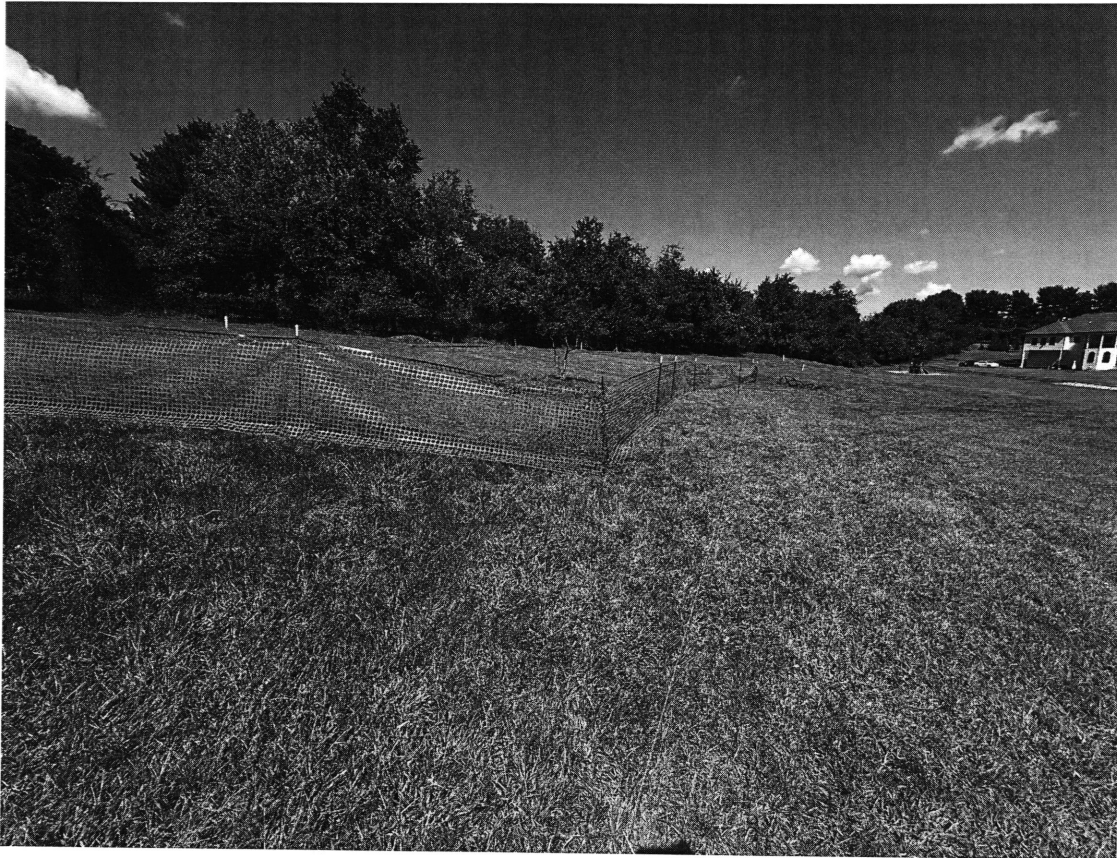

On Fri, Sep 5, 2025 at 9:02 AM Eshenbaugh, Melanie <MEshenbaugh@howardcountymd.gov> wrote:

Good morning Abby,

It was nice speaking with you yesterday afternoon, please email me the pictures as discussed yesterday regarding the fencing to protect the Sewage Disposal Area (SDA) and images showing the new bolts to secure the well cap. Hope you have a nice weekend and thank you kindly.

Melanie Eshenbaugh

Bureau of Environmental Health

Howard County Health Dept.

8930 Stanford Blvd. Columbia, MD 21045

www.hchealth.org
