

APPLICATION

PERCOLATION TESTING

A _____

P _____

HOWARD COUNTY HEALTH DEPARTMENT
BUREAU OF ENVIRONMENTAL HEALTH
3525-H ELLICOTT MILLS DRIVE/ELLICOTT CITY, MARYLAND 21043
TELEPHONE: 313-2640

DISTRICT 5th

DATE _____

TO: THE COUNTY HEALTH OFFICER
ELLICOTT CITY, MARYLAND

I HEREBY APPLY FOR THE NECESSARY TEST PRIOR TO APPLICATION FOR PERMIT TO CONSTRUCT (OR RECONSTRUCT) A SEWAGE DISPOSAL SYSTEM.

PROPERTY OWNER H Y Real Estate Joint Venture, c/o Robert B. Canter, Esquire

ADDRESS 11921 Rockville Pike, Suite 300 PHONE (301) 230-5220
Rockville, MD. 20852-2737

AGENT OR PROSPECTIVE BUYER Mount View, LLC. Attention: Paul M. Revelle

ADDRESS 6258 Cardinal La, Columbia Md. 21044 PHONE (410) 992 5805

PROPERTY LOCATION:

SUBDIVISION Pindell Woods LOT NO. ①

ROAD AND DESCRIPTION "B"

TAX MAP 41 PARCEL # 274 & 275

SIZE OF LOT 1-Acre Lot TYPE BLDG. Single Family Dwelling
(SINGLE FAMILY DWELLING OR COMMERCIAL)

THE SYSTEM INSTALLED UNDER THIS APPLICATION IS ACCEPTABLE ONLY UNTIL PUBLIC FACILITIES BECOME AVAILABLE. I FULLY UNDERSTAND THE FEE CONNECTED WITH THE FILING OF THIS PERC TEST APPLICATION IS NON-REFUNDABLE UNDER ANY CIRCUMSTANCES. I ALSO AGREE TO COMPLY WITH ALL M.O.S.H.A. REQUIREMENTS IN TESTING THIS LOT. _____
(SIGNATURE OF APPLICANT)

APPROVED BY _____ FOR _____ DATE _____

DISAPPROVED BY _____ FOR _____ DATE _____

HOLD PENDING FURTHER TESTS _____

REASONS FOR REJECTION OR HOLDING _____

PERCOLATION TEST PLAT/PRELIMINARY PLAT - TITLE OR I.D. # _____ DATE _____

SITE DEVELOPMENT PLAN/FINAL PLAT - TITLE OR I.D. # _____ DATE _____

THIS IS NOT A PERMIT

COUNTY #

SOIL PROFILE

573

0' topsoil
 1' br org red brn cl Lm
 3.5' 4' pale org beige sa mica Lm
 12' 15-20% sapr sh

574

0' topsoil
 1' br red brn cl Lm
 3' 4' med org brn sa mica Lm
 12' 15%+ sapr sh


575

0' topsoil
 1' red brn sa cl Lm
 3.5' 4' med red brn sa mica Lm
 12' 20%+ sapr sh

SOIL PROFILE

576

0' topsoil
 1' org brn cl Lm
 4.5' 5' med org brn sa mica Lm
 11.5' 15%+ sapr sh
 0' 643 topsoil
 1' org brn cl Lm
 4' med red brn sa mica Lm
 11.5' 20%+ sapr sh

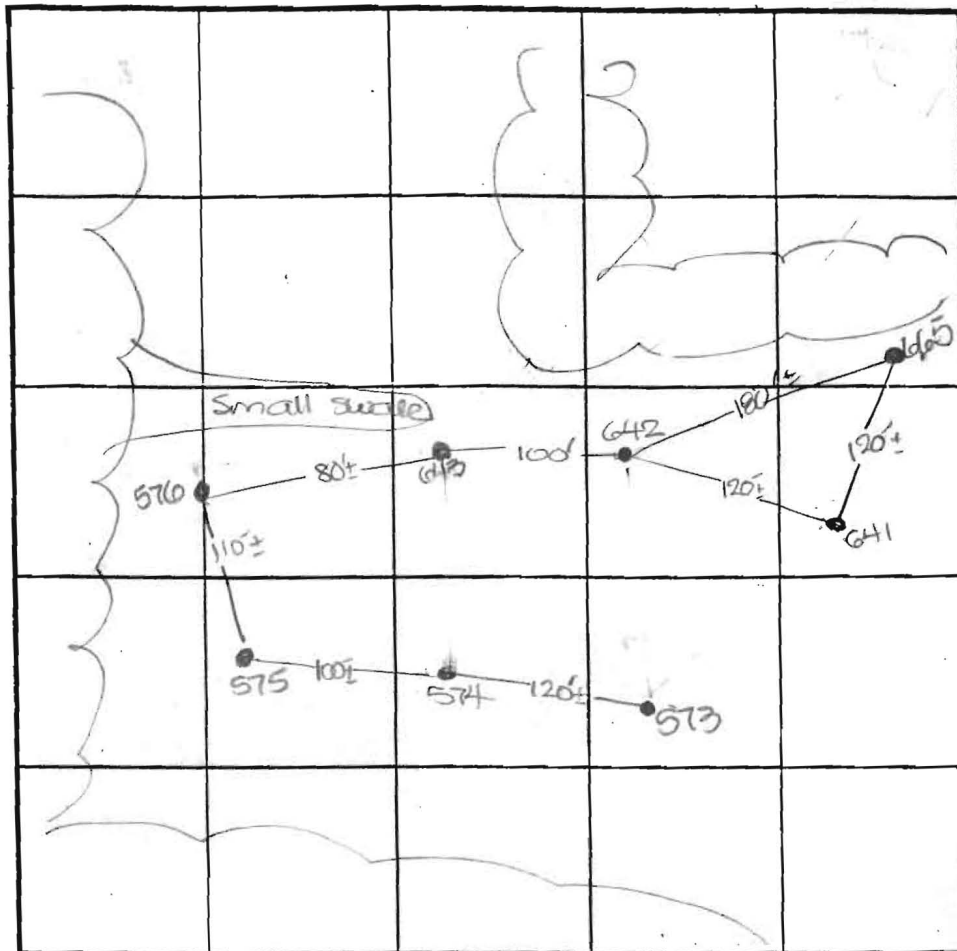

INDICATE NORTH - NAME ADJOINING ROADWAY AS BASE LINE.

Pindell School Road

DATE	TEST NO.	DEPTH	PRE-WET		TEST - 1" DROP		TIME
			START	STOP	START	STOP	
6-30-00	✓573	12.0'D	visual	- see	profile		OK
	✓574	3.5'S	11:24	11:26 ₃	11:26 ₂	11:30	4
		12.0'D	visual	- see	profile		OK
	575	12.0'D	visual	- see	profile		OK
	576	4.0'S	11:32	11:56	11:56	11:56	LOW
		11.5'D	visual	- see	profile		OK
		4'10"m	12:06	12:17	12:17	12:32	15
	643	11.5'D	visual	- see	profile		OK

REMARKS holes tested as stacked

TYPE OF SOIL _____

TESTED BY DKS ALSO PRESENT C. Zepp, R. Colson

TRENCH DESIGN DATA: AVERAGE PERCOLATION TIME _____ TRENCH WIDTH _____

INLET DEPTH _____ MAXIMUM BOTTOM DEPTH _____ SQ. FT./BEDROOM _____

COUNTY #

SOIL PROFILE

642

topsoil

org brn
cl Lm

4'

br
org red
tan
sa mica
Lm

12.5'

10-15%
sap
sh

641

topsoil

org brn
cl Lm

4'

med
red tan
sa mica
Lm

20%
sap
sh

18.5'

665

topsoil


br
org brn
sa cl Lm

4'


br
org brn
to
org beige
sa mica
Lm

15%
sap
sh

12.5'

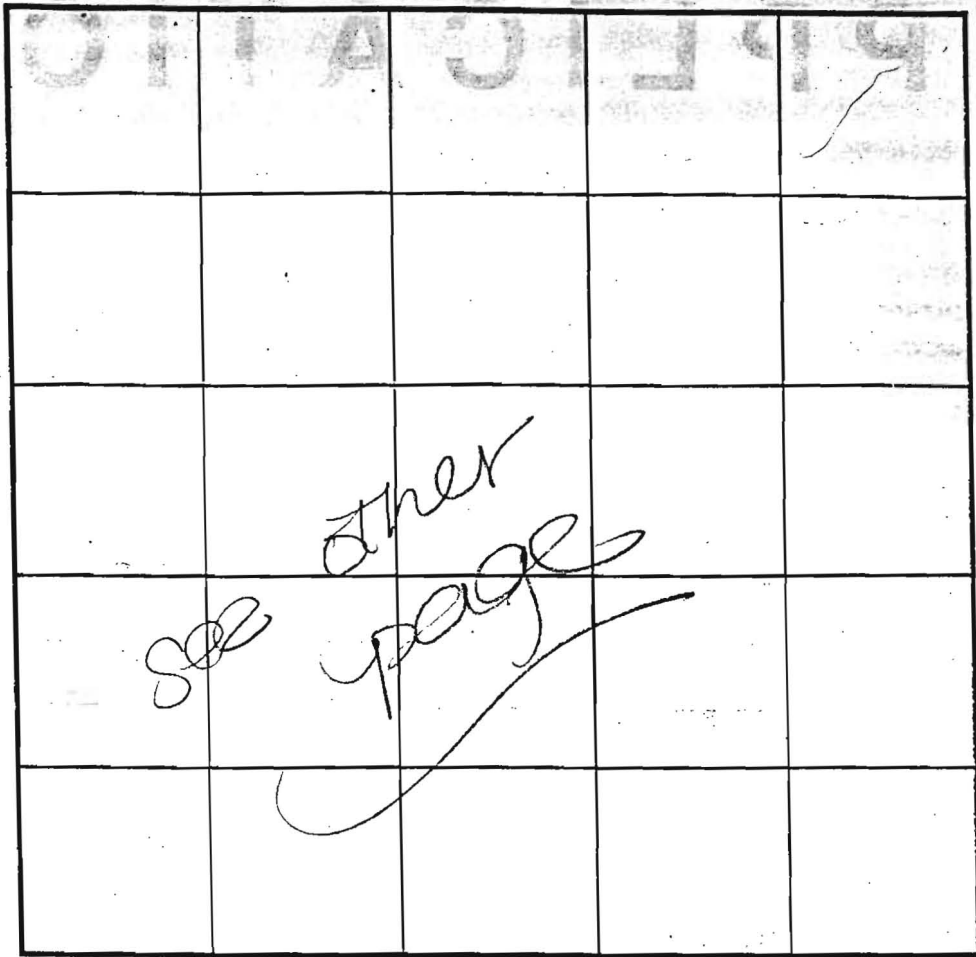

SOIL PROFILE



INDICATE NORTH - NAME ADJOINING ROADWAY AS BASE LINE.

DATE	TEST NO.	DEPTH	PRE-WET		TEST - 1" DROP		TIME
			START	STOP	START	STOP	
6-30-00	642	4.5' S	12:21	12:24 ₃	12:24 ₂	12:28 ₃	4
		12.5' D	Visual	- see	profile		OK
	665	4.0' S	12:44	12:48 ₂	12:48 ₂	12:57	9
		12.5' D	Visual	- see	profile		OK
	641	18.5' D	Visual	- see	profile		OK

REMARKS holes tested as stated

TYPE OF SOIL _____

TESTED BY DKS ALSO PRESENT C. Zepp, R. Colson

TRENCH DESIGN DATA: AVERAGE PERCOLATION TIME _____ TRENCH WIDTH _____

INLET DEPTH _____ MAXIMUM BOTTOM DEPTH _____ SQ. FT./BEDROOM _____

APPLICATION

PERCOLATION TESTING

A _____

P _____

HOWARD COUNTY HEALTH DEPARTMENT
BUREAU OF ENVIRONMENTAL HEALTH
3525-H ELLICOTT MILLS DRIVE/ELLICOTT CITY, MARYLAND 21043
TELEPHONE: 313-2640

DISTRICT 5th

DATE _____

TO: THE COUNTY HEALTH OFFICER
ELLICOTT CITY, MARYLAND

I HEREBY APPLY FOR THE NECESSARY TEST PRIOR TO APPLICATION FOR PERMIT TO CONSTRUCT (OR RECONSTRUCT) A SEWAGE DISPOSAL SYSTEM.

PROPERTY OWNER H Y Real Estate Joint Venture, c/o Robert B. Canter, Esquire

ADDRESS 11921 Rockville Pike, Suite 300 PHONE (301) 230-5220
Rockville, MD. 20852-2737

AGENT OR PROSPECTIVE BUYER Mount View, LLC. Attention: Paul M. Revelle

ADDRESS 6258 Cardinal La, Columbia Md. 21044 PHONE (410) 992 5805

PROPERTY LOCATION:


SUBDIVISION Pindell Woods LOT NO. ①

ROAD AND DESCRIPTION "B"

TAX MAP 41 PARCEL # 274 & 275

SIZE OF LOT 1-Acre Lot TYPE BLDG. Single Family Dwelling
(SINGLE FAMILY DWELLING OR COMMERCIAL)

THE SYSTEM INSTALLED UNDER THIS APPLICATION IS ACCEPTABLE ONLY UNTIL PUBLIC FACILITIES BECOME AVAILABLE. I FULLY UNDERSTAND THE FEE CONNECTED WITH THE FILING OF THIS PERC TEST APPLICATION IS NON-REFUNDABLE UNDER ANY CIRCUMSTANCES. I ALSO AGREE TO COMPLY WITH ALL M.O.S.H.A. REQUIREMENTS IN TESTING THIS LOT.



(SIGNATURE OF APPLICANT)

APPROVED BY _____ FOR _____ DATE _____

DISAPPROVED BY _____ FOR _____ DATE _____

HOLD PENDING FURTHER TESTS _____

REASONS FOR REJECTION OR HOLDING _____

PERCOLATION TEST PLAT/PRELIMINARY PLAT - TITLE OR I.D. # _____ DATE _____

SITE DEVELOPMENT PLAN/FINAL PLAT - TITLE OR I.D. # _____ DATE _____

THIS IS NOT A PERMIT


COUNTY #

SOIL PROFILE

573
 0' topsoil
 1' br org red brn cl Lm
 3.5' 4' pale org beige sa mica Lm
 12' 15-20% sapr sh

574
 0' topsoil
 1' br red brn cl Lm
 3' 4' med org brn sa mica Lm
 12' 15%+ sapr sh

575
 0' topsoil
 1' red brn sa cl Lm
 3.5' 4' med red brn sa mica Lm
 12' 20%+ sapr sh

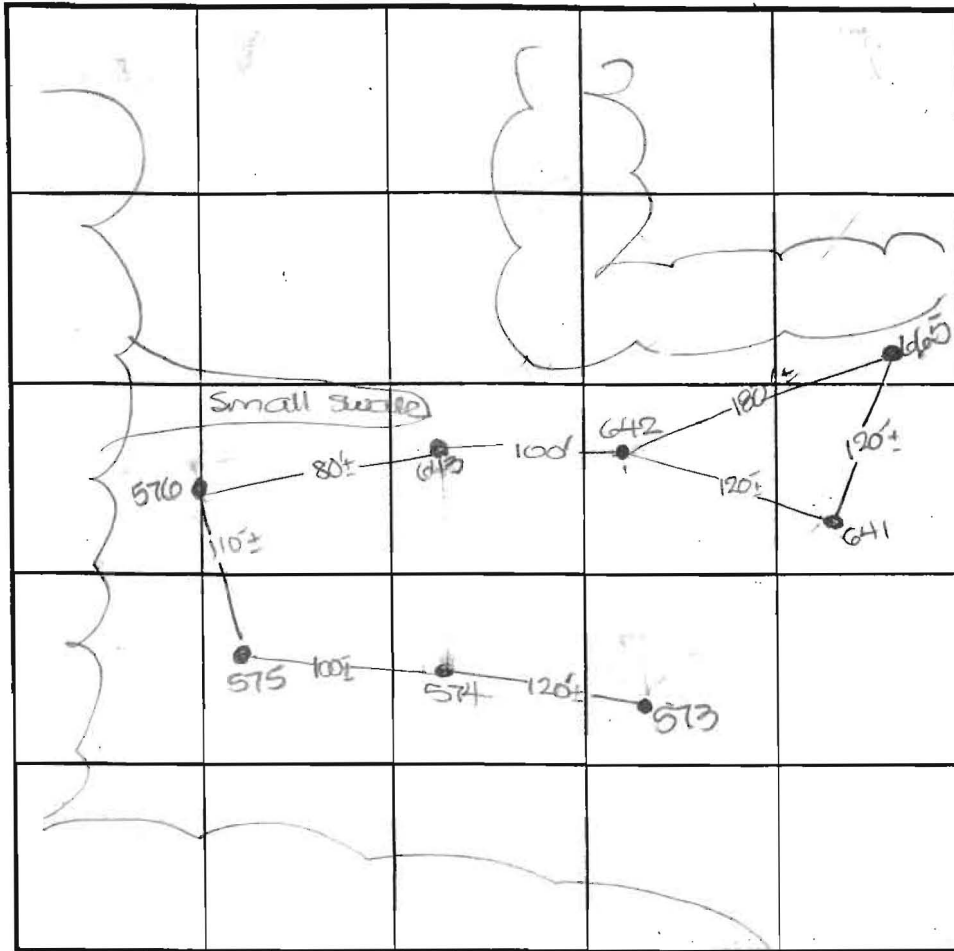

SOIL PROFILE

576
 0' topsoil
 1' org brn cl Lm
 4.5' 5' med org brn sa mica Lm
 11.5' 15%+ sapr sh
 643
 0' topsoil
 1' org brn cl Lm
 4' med red brn sa mica Lm
 u.s. 20%+ sapr sh

INDICATE NORTH - NAME ADJOINING ROADWAY AS BASE LINE.
 Pindell School Road

DATE	TEST NO.	DEPTH	PRE-WET		TEST - 1" DROP		TIME
			START	STOP	START	STOP	
6-30-00	✓ 573	12.0' D	visual	- see	profile		OK
	✓ 574	3.5' S	11:24	11:26 ³	11:26 ³	11:30	4
		12.0' D	visual	- see	profile		OK
	575	12.0' D	visual	- see	profile		OK
	576	4.0' S	11:32	11:56	11:56	little slow	-
		11.5' D	visual	- see	profile		OK
		4' 10" M	12:06	12:17	12:17	12:32	15
	643	11.5' D	visual	- see	profile		OK

REMARKS holes tested as stacked

TYPE OF SOIL _____

TESTED BY DKS ALSO PRESENT C. Zepp, R. Colson

TRENCH DESIGN DATA: AVERAGE PERCOLATION TIME _____ TRENCH WIDTH _____

INLET DEPTH _____ MAXIMUM BOTTOM DEPTH _____ SQ. FT./BEDROOM _____

COUNTY #

SOIL PROFILE

642

topsoil

org brn
cl Lm

br
org red
brn
sa mica
Lm

10-15%
sapr
sh

4'

12.5'

641

topsoil

org brn
cl Lm

med
red brn
sa mica
Lm

20%
sapr
sh

4'

18.5'

665

topsoil


br
org brn
sa cl Lm

br
org brn
to
org ledge
sa mica
Lm


15%
sapr
sh

4'

12.5'

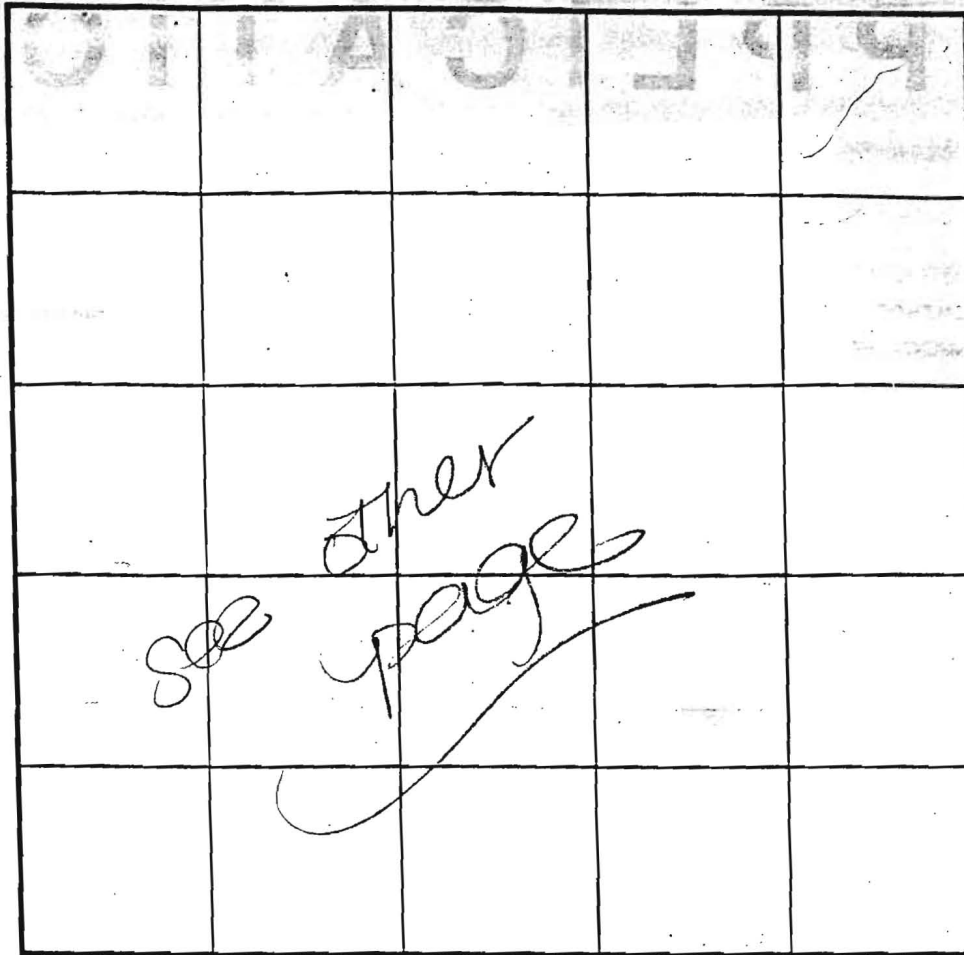

SOIL PROFILE



INDICATE NORTH - NAME ADJOINING ROADWAY AS BASE LINE.

DATE	TEST NO.	DEPTH	PRE-WET		TEST - 1" DROP		TIME
			START	STOP	START	STOP	
6-30-00	642	4.5' S	12:21	12:24 ₃	12:24 ₃	12:28 ₃	4
		12.5' D	Visual	- see	profile		OK
	665	4.0' S	12:44	12:48 ₂	12:48 ₃	12:57	9
		12.5' D	Visual	- see	profile		OK
	641	18.5' D	Visual	- see	profile		OK

REMARKS holes tested as stated

TYPE OF SOIL

TESTED BY DK5

ALSO PRESENT C. Zepp, B. Colson


TRENCH DESIGN DATA: AVERAGE PERCOLATION TIME

TRENCH WIDTH


INLET DEPTH

MAXIMUM BOTTOM DEPTH

SQ. FT./BEDROOM

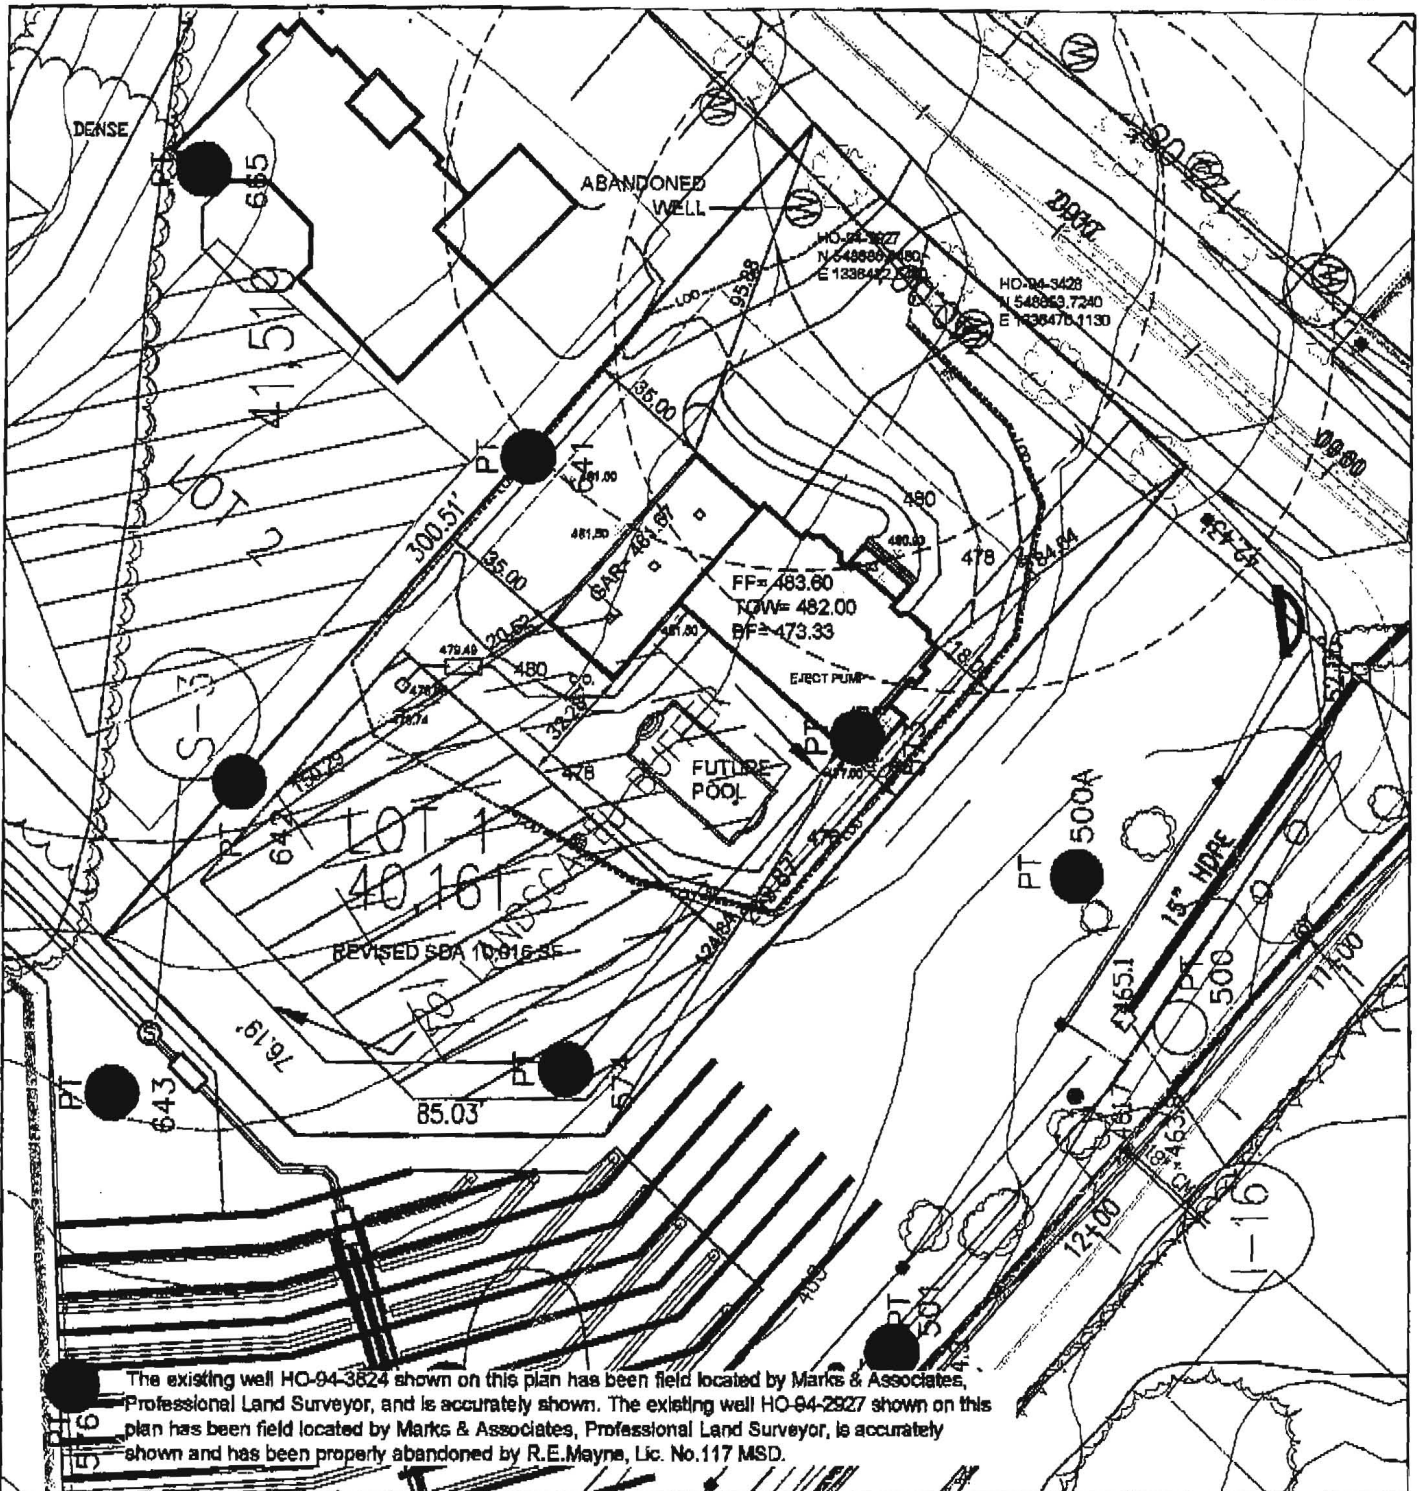

The existing well HO-94-3824 shown on this plan has been field located by Marks & Associates, Professional Land Surveyor, and is accurately shown. The existing well HO-94-2927 shown on this plan has been field located by Marks & Associates, Professional Land Surveyor, and is accurately shown and has been properly abandoned by R.E. Mayne, Lic. No. 117 MSD.

<p>TITLE PERCOLATION PLAT PLOT PLAN</p>		<p>OWNER/ BUILDER: Dale Thompson Builders, Inc. 6300 Woodside Court Suite A Columbia, MD 21046</p>	<p><u>PROPOSED ELEVATIONS:</u> BASEMENT SLAB: 473.33 TOP OF WALL: 482.00 FIRST SUBFLOOR: 483.00 INVERT OUT OF HOUSE: 478.30 INVERT INTO TANK: 478.80 INVERT OUT OF TANK: 478.30 INVERT INTO DISTRIBUTION BOX: 476.00 INVERT INTO TRENCHES: 475.50 GRADE AT SEPTIC TANK: 476.49 GRADE AT DISTRIBUTION BOX: 478.85 GRADE AT TRENCHES: 476.74 PAVING SPECIFICATIONS: 2" ASPHALT OVER 4" CR-6 OR 2.5" ASPHALT OVER 1.5" OVERLAY</p>
<p>DATE 7-24-2006 SCALE 1: 50</p>		<p>PROJECT NAME: SINGLE-FAMILY DWELLING PINDELL WOODS LOT 1 FULTON, HOWARD COUNTY MARYLAND 20729</p>	<p>APPROVED: FOR PRIVATE WATER AND PRIVATE SEWERAGE SYSTEM, LOT 1, PINDELL WOODS, FULTON, HOWARD COUNTY, MD. _____ HOWARD COUNTY HEALTH OFFICER _____ DATE</p>

SUCCESSORS AND ASSIGNS ALL EASEMENTS SHOWN ON THIS PLAN FOR WATER, SEWER, STORM DRAINAGE, OTHER PUBLIC UTILITIES AND FOREST CONSERVATION (DESIGNATED AS "FOREST CONSERVATION AREA"), LOCATED IN, ON, OVER AND THROUGH LOTS 1 THRU 47 AND PARCELS "A" THROUGH "F", ANY CONVEYANCES OF THE AFORESAID LOTS SHALL BE SUBJECT TO THE EASEMENTS HEREIN RESERVED, WHETHER OR NOT EXPRESSLY STATED IN THE DEED(S) CONVEYING SAID LOT(S). DEVELOPER SHALL EXECUTE AND DELIVER DEEDS FOR THE EASEMENTS HEREIN RESERVED TO HOWARD COUNTY, WITH A METES AND BOUNDS DESCRIPTION OF THE FOREST CONSERVATION AREA. UPON COMPLETION OF THE PUBLIC UTILITIES AND THEIR ACCEPTANCE BY HOWARD COUNTY, AND IN THE CASE OF FOREST CONSERVATION EASEMENT(S). UPON COMPLETION OF THE DEVELOPER'S OBLIGATIONS UNDER THE FOREST CONSERVATION INSTALLATION AND MAINTENANCE AGREEMENT EXECUTED BY DEVELOPER AND THE COUNTY, AND THE RELEASE OF DEVELOPER'S SURETY POSTED WITH SAID AGREEMENT, THE COUNTY SHALL ACCEPT THE EASEMENTS AND RECORD THE DEED(S) OF EASEMENT IN THE LAND RECORDS OF HOWARD COUNTY."

(AS SUPPLEMENTED AS FAR AS THEY RELATE TO THE MARKING OF THIS PLAT AND THE SETTING OF MARKERS, HAVE BEEN COMPLIED WITH.)


Dale Thompson 8-6-01
DALE THOMPSON, MEMBER OF MOUNT VIEW L.L.C. DATE

Clarence Carvell 8-6-01
CLARENCE CARVELL, OWNER DATE

Martha Carvell 8-6-01
MARTHA CARVELL, OWNER DATE

John C. Mellema 8-6-01
JOHN C. MELLEMA, SURVEYOR DATE

F-01-089

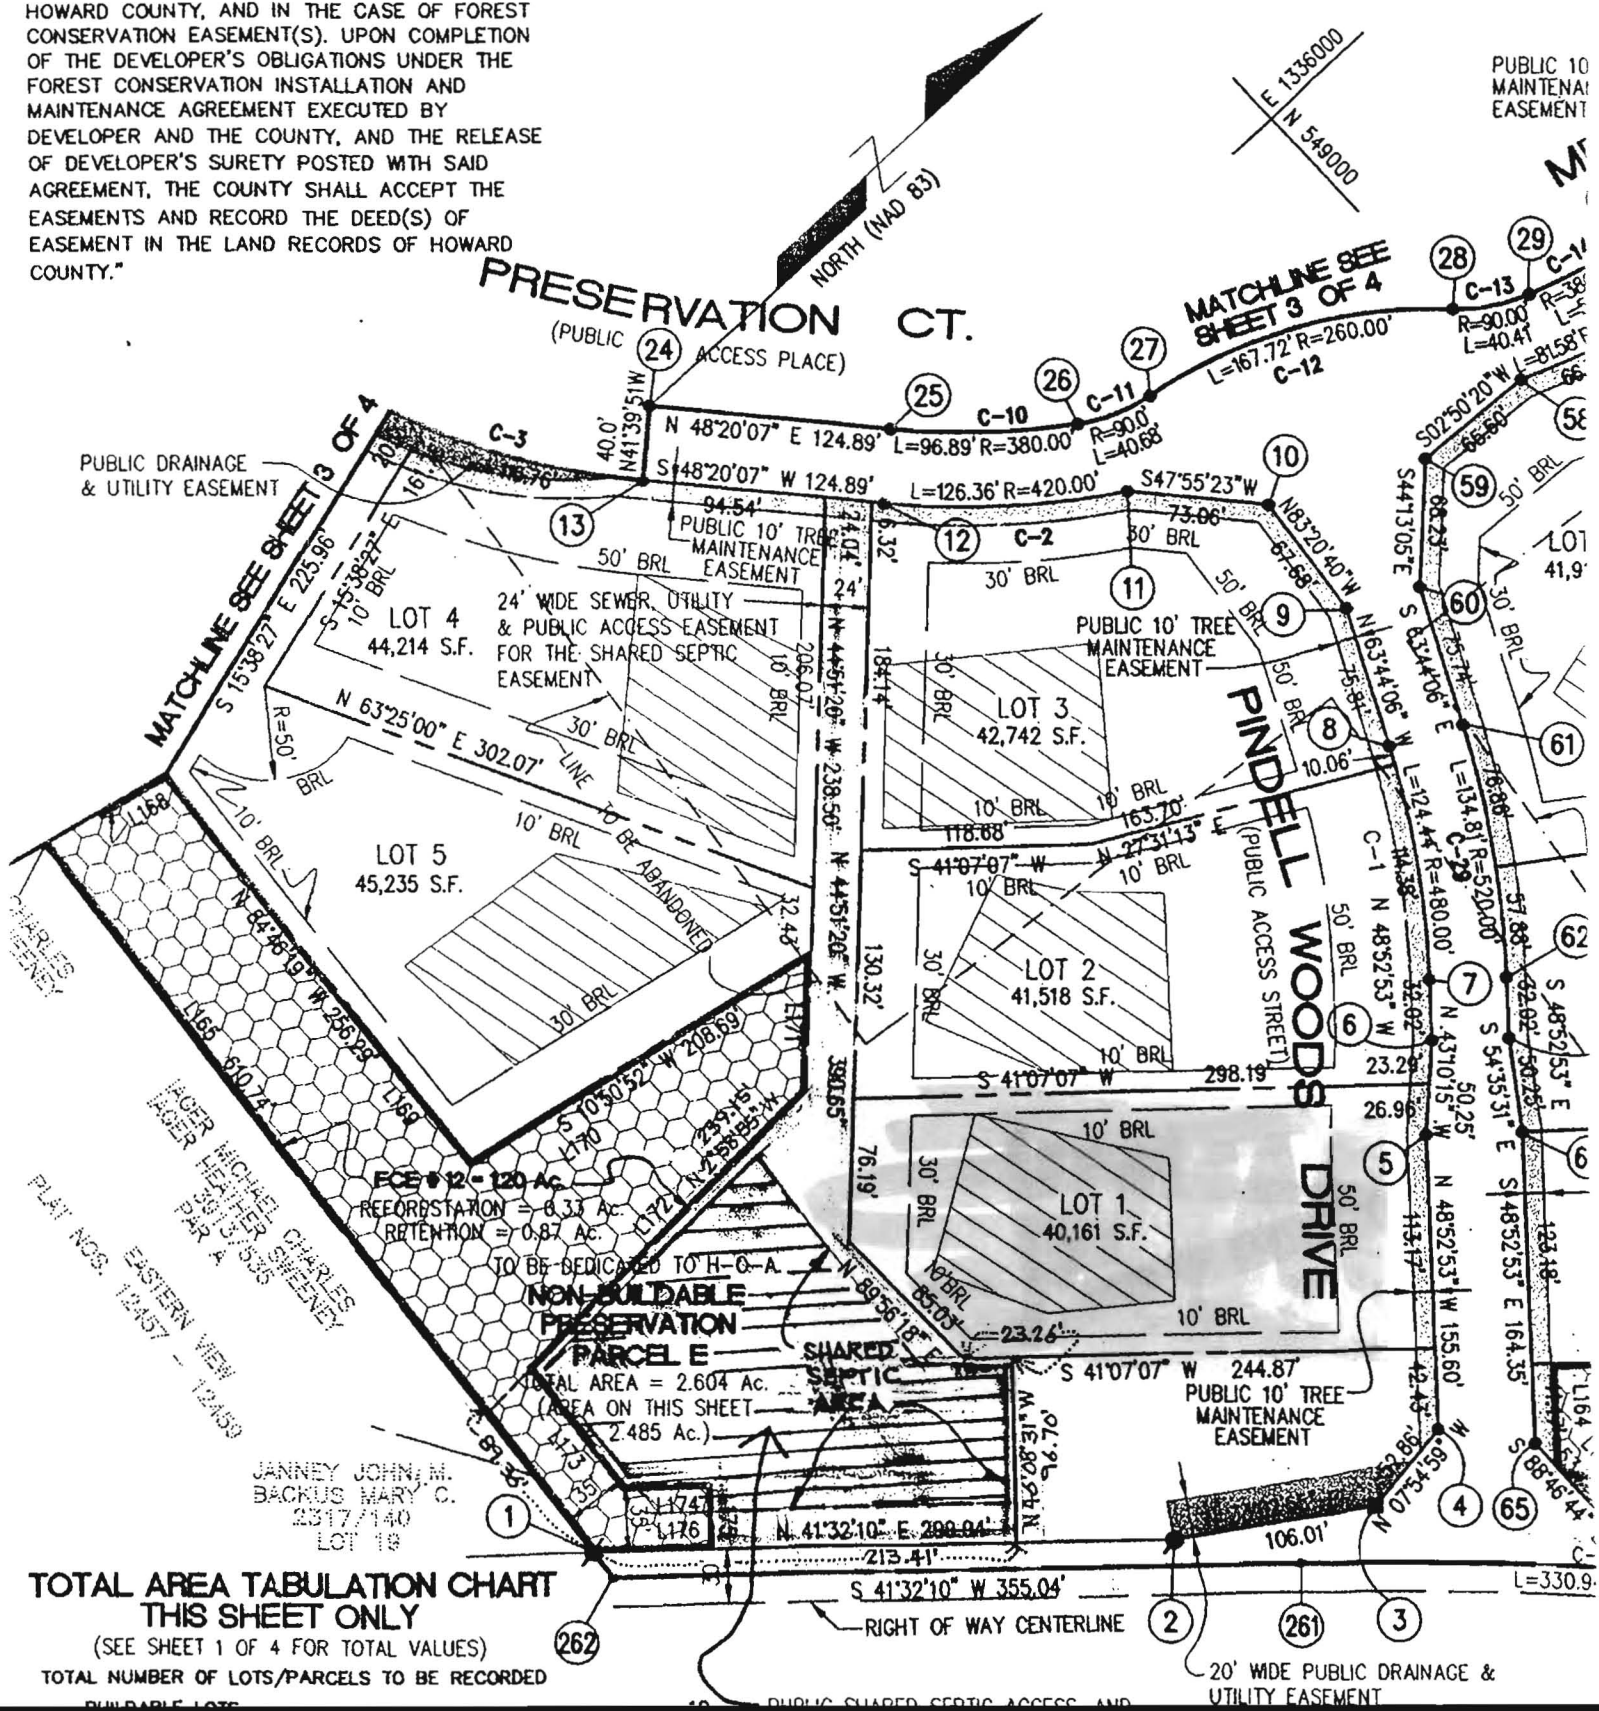

**TOTAL AREA TABULATION CHART
THIS SHEET ONLY**
(SEE SHEET 1 OF 4 FOR TOTAL VALUES)

TOTAL NUMBER OF LOTS/PARCELS TO BE RECORDED

TOTAL AREA OF BUILDABLE LOTS

TOTAL AREA OF NON-BUILDABLE PRESERVATION

TOTAL AREA OF PUBLIC SHARED SEPTIC ACCESS AND

TOTAL AREA OF 20' WIDE PUBLIC DRAINAGE & UTILITY EASEMENT

Bricker, Robert

From: Bricker, Robert
Sent: Thursday, May 10, 2012 2:55 PM
To: 'Pete@catalinapoolbuilders.com'
Subject: RE: Note contents for revised Perc Cert
Attachments: Plot Plan[1]_11603 Pindell Woods Drive.pdf; Perc Cert_11603 Pindell Woods.pdf

Attached is the subdivision Perc Cert showing topography, perc tests, septic reserve and well location on Lot 1. Also attached is the Plot Plan showing an adjustment in the septic reserve to accommodate a pool oriented parallel with the 'long' axis of the house. (I believe you have this Plot Plan content depicted on your proposal.) I cannot locate the As-Built (re: the septic system installation permit) you will have to submit a request to Juanita King, our person who handles PIA requests.

Please be advised that you can extend the septic reserve to 10 feet from the lot line. Also you will need to add two Alternate Well locations on the front of the property; they need to be spaced by 50 feet; setbacks are 15' from R-O-W, 10 feet from driveway, 30 feet from house, 100-feet from any septic tank or septic reserve area.

From: Pete@catalinapoolbuilders.com [mailto:Pete@catalinapoolbuilders.com]
Sent: Thursday, May 10, 2012 8:41 AM
To: Bricker, Robert
Subject: re: Note contents for revised Perc Cert

Robert,

This is the request for the percolation plat of Pindell Woods Lot 1.

I also faxed a request for an as built for the existing system.

Attached is what I had to work with to locate the pool and move a little septic area to the back. I could not get it in PDF form from the scanner but if you need it that way I will get it figured out.

I rotated the original to bring everything to scale to verify the distances of all the adjustments.

When I have all the paperwork does Margaret need an engineer for the revised sewage easement or does she just need to sign the form you furnished?

Thank you for all your help and let me know what I do from here.

Sincerely,


Pete,

Pete Mousaw
Pete@catalinapoolbuilders.com
410-647- POOL (7665)
Catalina Pool Builders LLC
836 Ritchie Hwy , Severna Park, Md, 21146

MARGARET KIM
 11603 PINDELL WOODS DR
 FULTON, MD, 20759


ROOT #
 DIST OS - 434769

SCALE 1" = 40' 0"

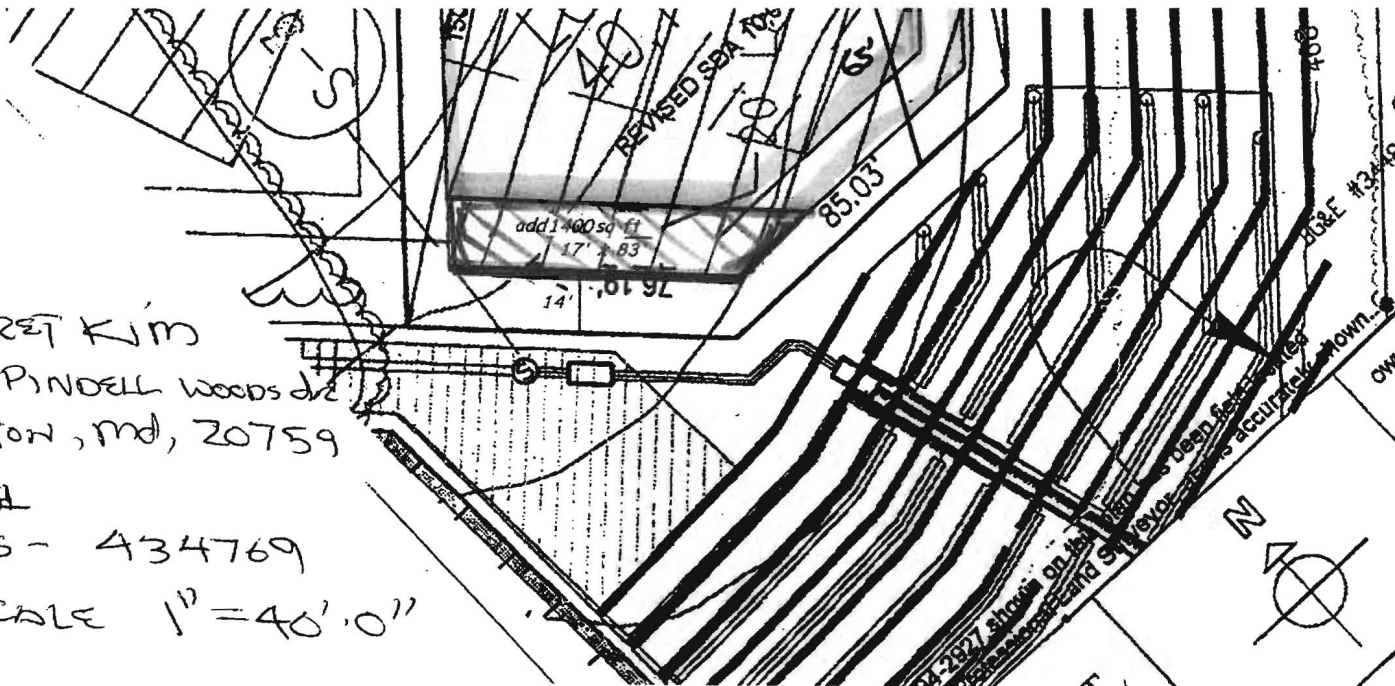

TITLE:
**PERCOLATION PLAT,
 PLOT PLAN**

DATE: 6-07-2006
SCALE: 1:40



OWNER/ BUILDER:
 Dale Thompson Builders, Inc.
 6300 Woodside Court
 Suite A
 Columbia, MD 21046


PROPOSED ELEVATIONS:

BASEMENT SLAB:	473.33
TOP OF WALL:	482.00
FIRST SUBFLOOR:	483.80
INVERT OUT OF HOUSE:	478.30
INVERT INTO TANK:	478.80
INVERT OUT OF TANK:	476.30
INVERT INTO DISTRIBUTION BOX:	478.00
INVERT INTO TRENCHES:	475.50
GRADE AT SEPTIC TANK:	479.49
GRADE AT DISTRIBUTION BOX:	478.85
GRADE AT TRENCHES:	478.74


PROJECT NAME:
 SINGLE-FAMILY DWELLING
 PINDELL WOODS
 LOT 1
 FULTON, HOWARD COUNTY
 MARYLAND 20759

APPROVED: FOR PRIVATE WATER AND PRIVATE SEWERAGE SYSTEM, LOT 1, PINDELL WOODS, FULTON, HOWARD COUNTY, MD.

PAVING SPECIFICATIONS:
 2" ASPHALT OVER 4" C.R. & G.

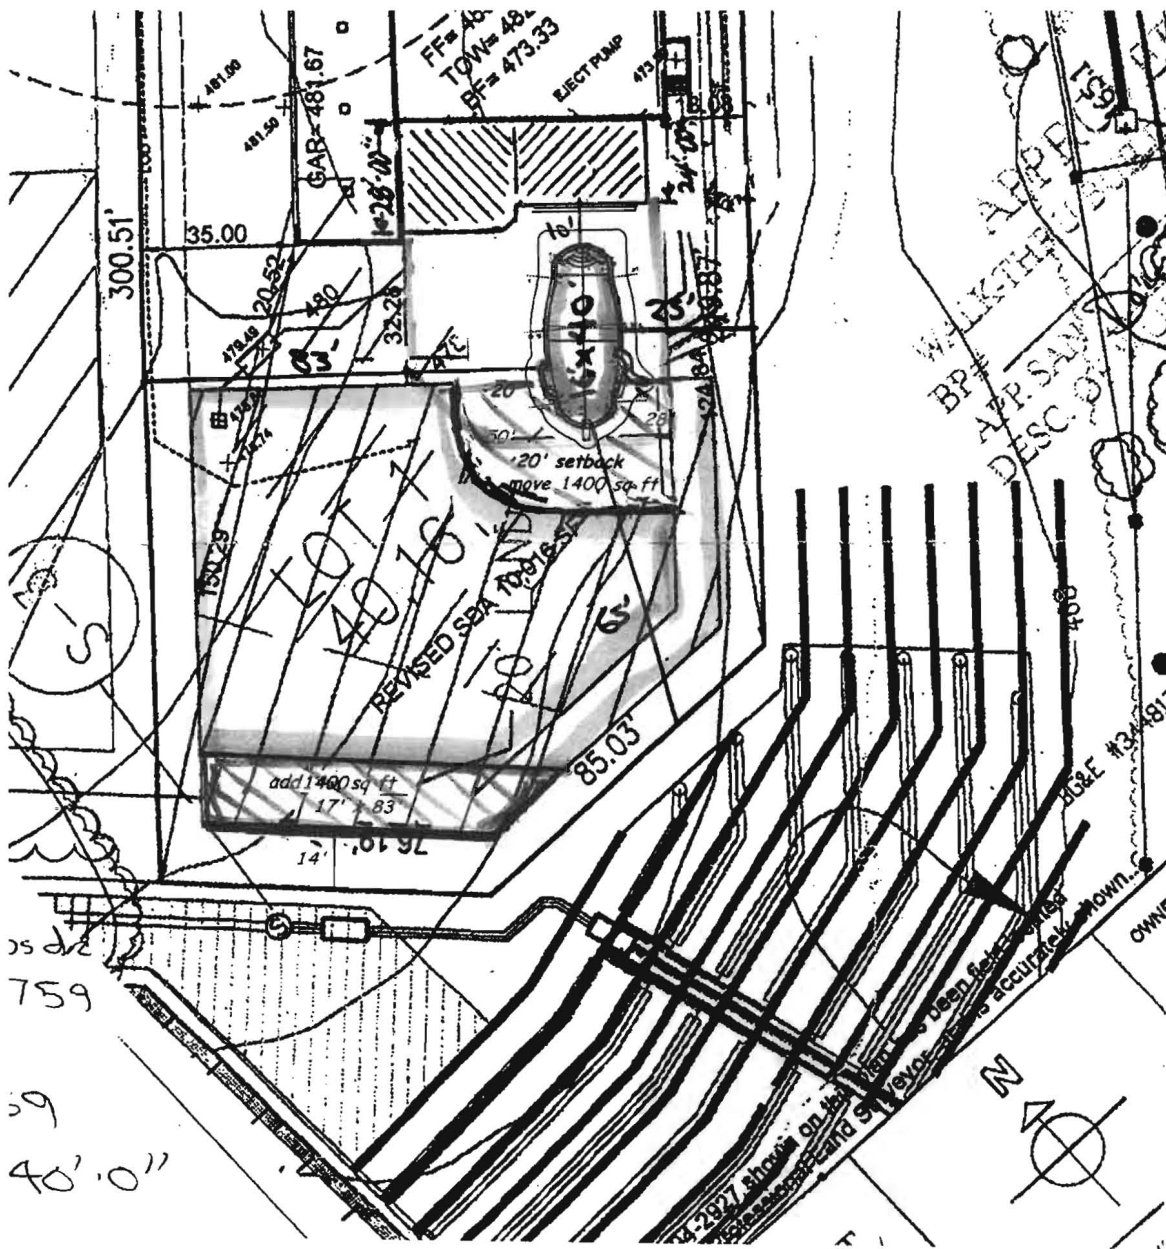


	<p>OWNER/ BUILDER: Dale Thompson Builders, Inc. 6300 Woodside Court Suite A Columbia, MD 21046</p>	<p>PROPOSED ELEVATIONS:</p> <table border="0"> <tr><td>BASEMENT SLAB:</td><td>473.33</td></tr> <tr><td>TOP OF WALL:</td><td>482.00</td></tr> <tr><td>FIRST SUBFLOOR:</td><td>483.80</td></tr> <tr><td colspan="2"> </td></tr> <tr><td>INVERT OUT OF HOUSE:</td><td>478.30</td></tr> <tr><td>INVERT INTO TANK:</td><td>478.80</td></tr> <tr><td>INVERT OUT OF TANK:</td><td>476.30</td></tr> <tr><td>INVERT INTO DISTRIBUTION BOX:</td><td>476.00</td></tr> <tr><td>INVERT INTO TRENCHES:</td><td>475.50</td></tr> <tr><td colspan="2"> </td></tr> <tr><td>GRADE AT SEPTIC TANK:</td><td>479.49</td></tr> <tr><td>GRADE AT DISTRIBUTION BOX:</td><td>478.85</td></tr> <tr><td>GRADE AT TRENCHES:</td><td>478.74</td></tr> </table> <p>PAVING SPECIFICATIONS: 2" ASPHALT OVER 4" C&G CG</p>	BASEMENT SLAB:	473.33	TOP OF WALL:	482.00	FIRST SUBFLOOR:	483.80			INVERT OUT OF HOUSE:	478.30	INVERT INTO TANK:	478.80	INVERT OUT OF TANK:	476.30	INVERT INTO DISTRIBUTION BOX:	476.00	INVERT INTO TRENCHES:	475.50			GRADE AT SEPTIC TANK:	479.49	GRADE AT DISTRIBUTION BOX:	478.85	GRADE AT TRENCHES:	478.74
BASEMENT SLAB:	473.33																											
TOP OF WALL:	482.00																											
FIRST SUBFLOOR:	483.80																											
INVERT OUT OF HOUSE:	478.30																											
INVERT INTO TANK:	478.80																											
INVERT OUT OF TANK:	476.30																											
INVERT INTO DISTRIBUTION BOX:	476.00																											
INVERT INTO TRENCHES:	475.50																											
GRADE AT SEPTIC TANK:	479.49																											
GRADE AT DISTRIBUTION BOX:	478.85																											
GRADE AT TRENCHES:	478.74																											
<p>MOVED: FOR PRIVATE WATER AND PRIVATE SEWERAGE SYSTEM, LOT 1, PINDELL RD, FULTON, HOWARD COUNTY, MD.</p>																												

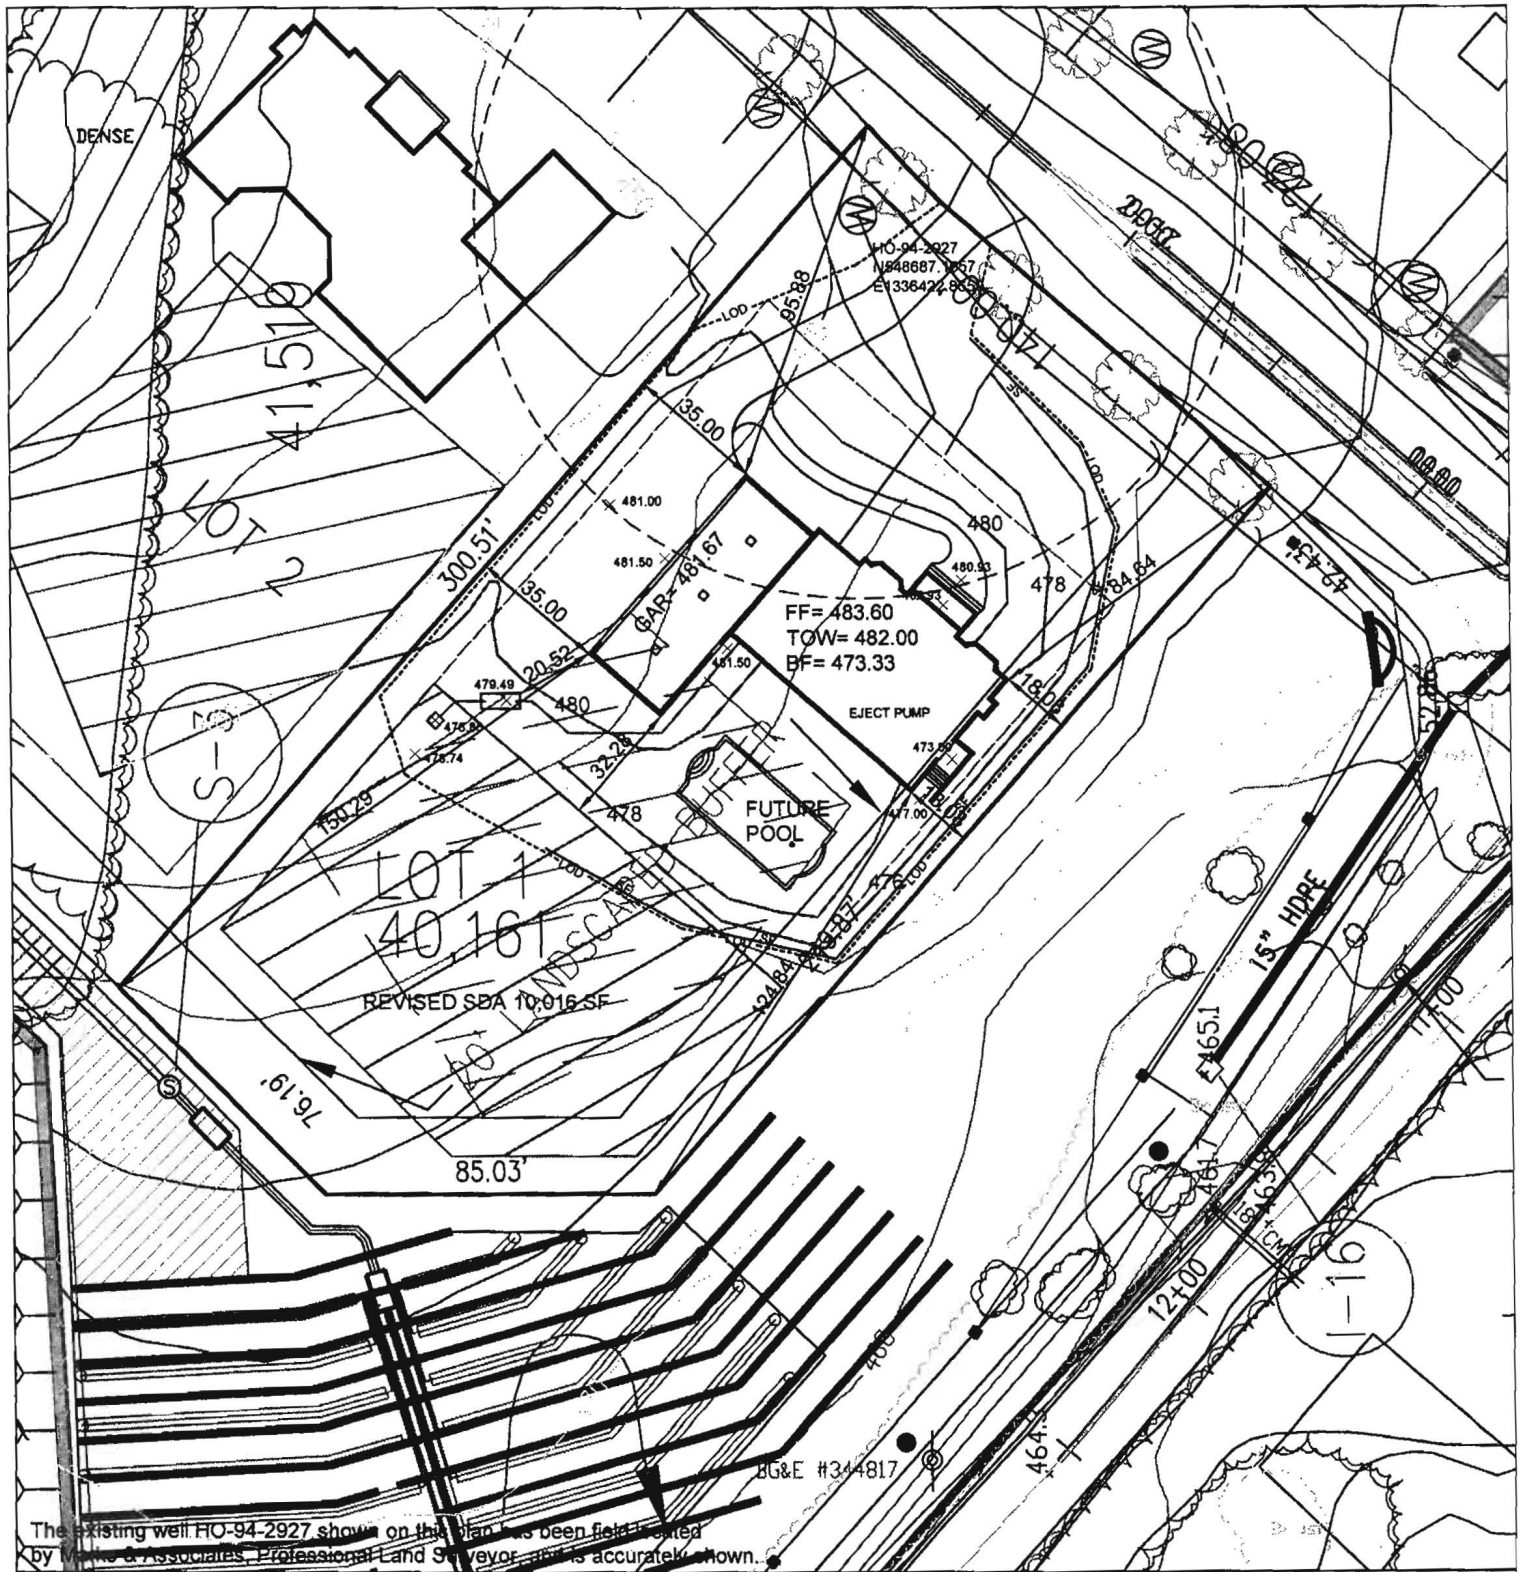

TITLE:
**PERCOLATION PLAT
 PLOT PLAN**

DATE: 6-07-2006
 SCALE: 1: 50



OWNER/ BUILDER:
 Dale Thompson Builders, Inc.
 6300 Woodside Court
 Suite A
 Columbia, MD 21046

PROPOSED ELEVATIONS:	
BASEMENT SLAB:	473.33
TOP OF WALL:	482.00
FIRST SUBFLOOR:	483.60
INVERT OUT OF HOUSE:	478.30
INVERT INTO TANK:	478.80
INVERT OUT OF TANK:	476.30
INVERT INTO DISTRIBUTION BOX:	478.00
INVERT INTO TRENCHES:	475.50
GRADE AT SEPTIC TANK:	479.49
GRADE AT DISTRIBUTION BOX:	478.85
GRADE AT TRENCHES:	478.74

PROJECT NAME:
 SINGLE-FAMILY DWELLING
 PINDELL WOODS
 LOT 1
 FULTON, HOWARD COUNTY
 MARYLAND 20759

APPROVED: FOR PRIVATE WATER AND PRIVATE SEWERAGE SYSTEM, LOT 1, PINDELL WOODS, FULTON, HOWARD COUNTY, MD.

 HOWARD COUNTY HEALTH OFFICER

DATE _____

PAVING SPECIFICATIONS:
 2" ASPHALT OVER 4" CR-6 OR
 2.5" ASPHALT OVER 1.5" OVERLAY

HOWARD COUNTY HEALTH DEPARTMENT
Completed Septic System

P 525631 A 518574

DATE 11/13/2006

LOCATION <u>11603 Pindell Woods Drive</u>	<u>APPLICATION</u>	
<u>Pindell Woods</u>	HOLD	()
	APPROVED	()
LOT <u>1</u>	REJECTED	()
APPLICANT _____	<u>INSTALLATION</u>	
OWNER <u>Dale Thompson Builders</u>	HOLD	()
PERMITTEE _____	APPROVED	()
	APPROVED	
HD-11	DATE <u>02/01/2007</u>	

CATALINA POOLS

F A X

836 Ritchie Highway # 8, Severna Park, MD 21146 CatalinaPoolBuilders.com

410-647-POOL

Fax 410-544-0555

^{PETE}
#info@CatalinaPoolBuilders.com

To	Howard County Health	From	PETE
Attention		# Pages	1 + cover
Fax #	410-313-2648	Date	5-9-12
Regarding	AS BUILTS for septic	Fax #	410-544-0555

COMMENTS


I am working with Mrs Kim to install an inground pool.

We will have to relocate on area of the septic reserve.

I need a copy of the As Built and any other information that you can help me with.

Thank you in advance for your help.

PK
Pete Mousaw,
I can come and pick them up if that will help you, just call me.



Bureau of Environmental Health
7178 Gateway Drive Columbia, MD 21046
(410) 313-2640 Fax (410) 313-2648
TDD (410) 313-2323 Toll Free 1-866-313-6300
website: www.hchealth.org

Peter Beilenson, M.D., M.P.H., Health Officer

Public Information Act Request Form

Property Information Requested:
Margaret & Victor Kim
Current Owner's Name
Pindell Woods incl A. BSB
Subdivision
11603 Pindell Woods dr
Property Address FULTON MD 20759
1 Lot # 0091 Tax Map 0274 Parcel

Applicant's Name: Catalina Pools Phone # Pete 443-852-9325

Address: 836 Ritchie Hwy - Suite 8 Severna Park, MD 21146

Select from the following records:

Well & Septic Program

- Percolation Results
Well Completion Report
Other (specify)

- X Septic Construction Plan (As built)
Complete Lot File

Food Protection Program

- Inspection Report - Food Facility Name:
List of food facilities
Other (Please explain):

Community Hygiene Program

- Complaint Investigation Reports Rabies Case Reports Pool Inspection Records
Registered Storage Tanks Well Water Sampling Other

Please indicate how you would like us to respond to your request:

- Regular Mail Fax: X Email: PETE@CatalinaPoolBuilders.com

I understand that I will be charged \$.60 per page copied. If staff time in record retrieval takes more than two(2) hours, then a fee of \$25.00 per hour after two (2) hours will be assessed. Also, I do understand that I will not be able to request any proprietary information enclosed in the file and all copies larger than 11"x17" may best be provided by the proprietor of the document. I also realize that it may take up to thirty (30) days to process this request.

Pete Mousaw
Applicant Signature

5-9-12
Date

FOR OFFICE USE ONLY
5/9/12 Date Received 5/11/12 Date Completed 2 # of Copies Made
Record Found Preparation Time Staff Initials

513646-15

closed

CATALINA POOLS

F A X

836 Ritchie Highway # 8, Severna Park, MD 21146 CatalinaPoolBuilders.com

410-647-POOL

Fax 410-544-0555

PETE

~~info~~@CatalinaPoolBuilders.com

To	Howard County Health	From	PETE 443-852-9325
Attention	JUANITA King	# Pages	1 + COVER 6.8.12
Fax #	410-313-2648	Date	5.9.12 5.15.12
Regarding	AS BUILTS for septic	Fax #	410-544-0555

~~6.8.12~~ JUANITA - I HAVE NOT HEARD FROM YOU
 CAN YOU PLEASE COMMENTS HELP ME. THE CUST
 I am working with Mrs King to install an inground pool.
 IS GETTING FRUSTRATED,
 Thank you
 PETE.


We will have to relocate on area of the
 Septic RESERVE.

I need a copy of the As Built and any other
 information that you can help me with.

Thank you in advance for your help

PS
 Pete Mousaw
 I can come and pick them up if that will
 help you, just call me.

~~5.15.12~~ CAN YOU PLEASE help me with
 THIS - CAN I pick these up on - 5.16 or 17.
 THANK YOU PETE.



Bureau of Environmental Health
 7178 Gateway Drive Columbia, MD 21046
 (410) 313-2640 Fax (410) 313-2648
 TDD (410) 313-2323 Toll Free 1-866-313-6300
 website: www.hchealth.org

Peter Beilenson, M.D., M.P.H., Health Officer

Public Information Act Request Form

Property Information Requested:
 Current Owner's Name: Margaret & Victor KIM Property Address: 11603 Pindellwoods dr
 Subdivision: Pindell Woods incl A. BSB Lot #: 1 Tax Map: 0091 Parcel: 0274
 City: FULTON MD - 20759

Applicant's Name: Catalina Pools Phone # Pete 443.852.9325

Address: 836 Ritchie Hwy - Suite 8 Severna Park, Md 21146

Select from the following records:

Well & Septic Program

- Percolation Results
- Well Completion Report
- Other (specify) _____
- Septic Construction Plan (As built)
- Complete Lot File

Food Protection Program

- Inspection Report - Food Facility Name: _____
- List of food facilities
- Other (Please explain): _____

Community Hygiene Program

- Complaint Investigation Reports
- Rabies Case Reports
- Pool Inspection Records
- Registered Storage Tanks
- Well Water Sampling
- Other

Please indicate how you would like us to respond to your request:

- Regular Mail
- Fax: _____
- Email: PESE@CatalinaPoolBuilders.com

I understand that I will be charged \$.60 per page copied. If staff time in record retrieval takes more than two(2) hours, then a fee of \$25.00 per hour after two (2) hours will be assessed. Also, I do understand that I will not be able to request any proprietary information enclosed in the file and all copies larger than 11"x17" may best be provided by the proprietor of the document. I also realize that it may take up to thirty (30) days to process this request.

Pete Mousaw
 Applicant Signature

5-9-12
 Date

FOR OFFICE USE ONLY

_____ Date Received	_____ Date Completed	_____ # of Copies Made
_____ Record Found	_____ Preparation Time	_____ Staff Initials
