

APPLICATION

SEWAGE DISPOSAL TESTING

MARYLAND STATE DEPARTMENT OF HEALTH

HOWARD COUNTY

ELLICOTT CITY

DISTRICT _____

DATE _____

A _____
P _____

TO: THE COUNTY HEALTH OFFICER
ELLICOTT CITY, MARYLAND

I, HEREBY, APPLY FOR THE NECESSARY TESTS IN ORDER TO CONSTRUCT (OR RECONSTRUCT) A SEWAGE DISPOSAL SYSTEM.

PROPERTY OWNER _____

ADDRESS _____ PHONE _____

PROPERTY LOCATION:

SUBDIVISION _____ LOT NO. _____

ROAD AND DESCRIPTION _____

OCCUPANT _____ PHONE _____

PERSON TO CONSTRUCT SYSTEM _____

ADDRESS _____ PHONE _____

SIZE OF LOT _____ TYPE BLDG. 3 bedrooms per building
NUMBER OF BEDROOMS

IF NOT SINGLE RESIDENCE DESCRIBE _____

SIGNATURE OF APPLICANT _____


APPROVED: De Monaghan FOR Dry W. 2 DATE 7/28/70

REJECTED BY _____ FOR _____ DATE _____
(KIND OF SYSTEM)

HOLD PENDING FURTHER TESTS _____ DATE _____

REASONS FOR REJECTION OR HOLDING _____

THIS IS NOT A PERMIT

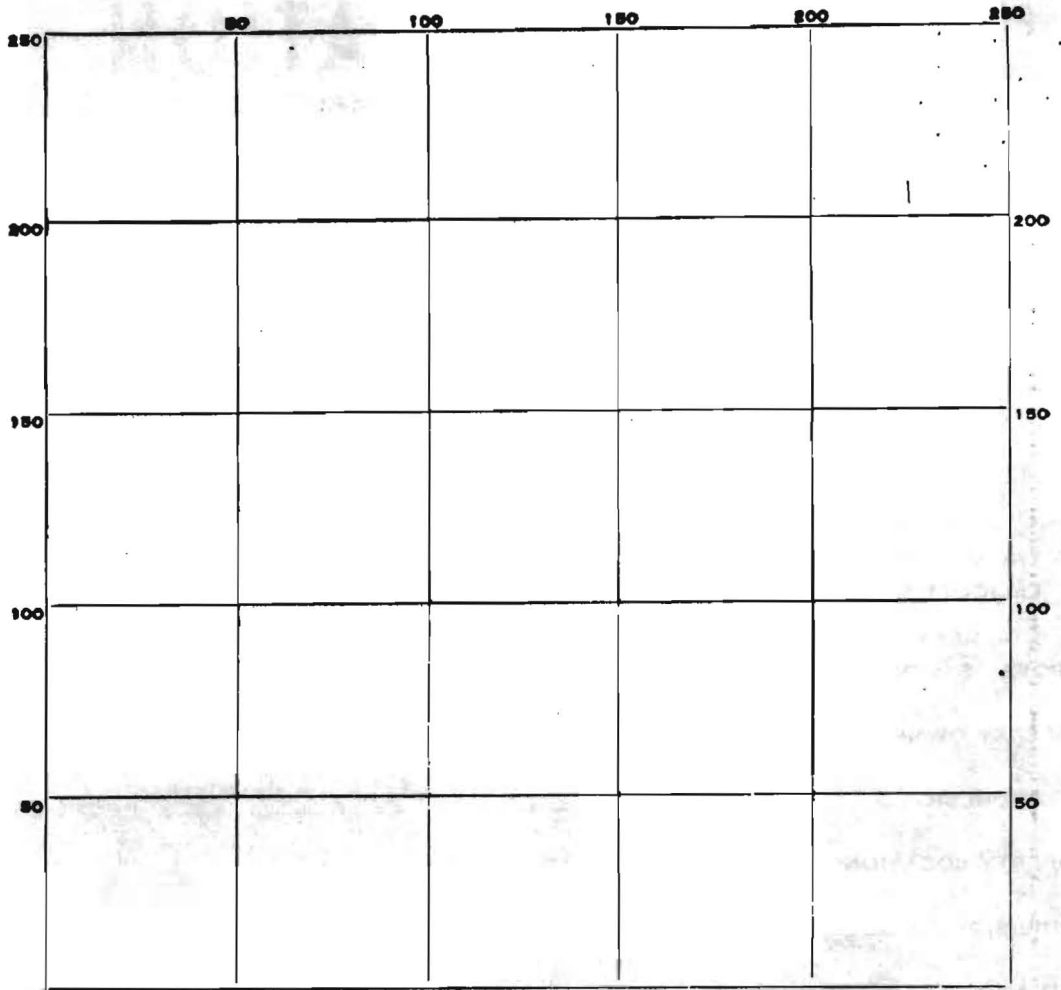

INDICATE NORTH. - NAME ADJOINING ROADWAY AS BASE LINE.

DATE	TEST NO.	DEPTH	PRE-WET		TEST - 1" DROP		TIME
			START	STOP	START	STOP	
7/28/70	1	12 1/2	9:39	9:42	9:49	10:08	20
	2	5 ft	9:40	9:42	9:42	started slow pr.	
	3	11 1/2	9:43	9:52	9:52	10:03	11 min
	4	5 ft	9:45	started with pen.			

SOIL AUGER FINDING best soil starts 5ft.

TESTED BY [Signature]

REMARKS [Signature]

Plot will be at site.

APPLICATION

A 15426

SEWAGE DISPOSAL TESTING

P _____

MARYLAND STATE DEPARTMENT OF HEALTH

HOWARD COUNTY

ELLICOTT CITY

DISTRICT 3

DATE 7/23/70

Received
7/28/70
9:30

Septic Tank - 1000 gal.

Dry Wells - 2 dry wells - dig each pit 10ft square. Set block + top in center of pits fill in rest of pits with gravel. Each Dry Well to have 7ft effective depth below the first 5ft of non absorbent gravel. Maximum depth for Dry Wells is 12 ft below original grade.

Place each Dry Well about 162 ft from front property line + with one Dry Well about 185 ft from right sideline - second dry well about 150 ft from right side line as seen when facing lot from Pfefferkorn Rd. Dry wells to be 30ft apart edge to edge + connected in series.

I, HEREBY, APPLY FOR THE NECESSARY TESTS IN ORDER TO CONSTRUCT (OR RECONSTRUCT) A SEWAGE DISPOSAL SYSTEM.

PROPERTY OWNER J. P. & K. O. Wigglesworth

ADDRESS 9408 Hughes Court, Adelphia, Md. PHONE 392-8264 - business
HE 4-5394 - home

PROPERTY LOCATION:

SUBDIVISION _____ LOT NO. _____

ROAD AND DESCRIPTION Pfefferkorn Rd. - off Rt. 32 - look for garage back on the lot
look for TATTRIE & LEVY SIGN

OCCUPANT _____ PHONE _____

PERSON TO CONSTRUCT SYSTEM _____

ADDRESS _____ PHONE _____

SIZE OF LOT 16,500 acres TYPE BLDG. 3 bedroom per Mr. Levy
24

Single Family (DWIlg.)

IF NOT SINGLE RESIDENCE DESCRIBE _____

SIGNATURE OF APPLICANT *[Signature]*

APPROVED BY *[Signature]* FOR Dry Wells - 2 DATE 7/28/70
(KIND OF SYSTEM)


REJECTED BY _____ FOR _____ DATE _____
(KIND OF SYSTEM)

HOLD PENDING FURTHER TESTS _____ DATE _____

REASONS FOR REJECTION OR HOLDING _____

PRINTED NAME AND JOB

THIS IS NOT A PERMIT

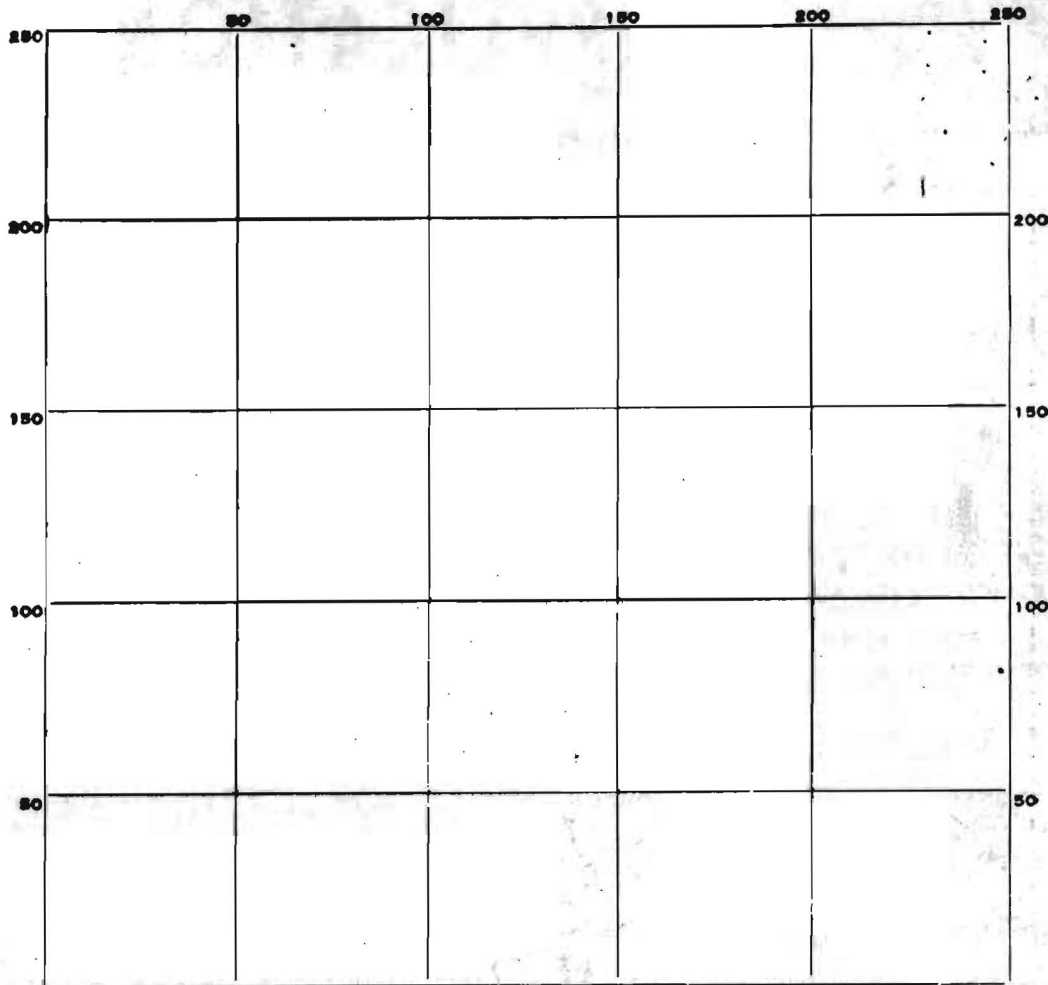

INDICATE NORTH. - NAME ADJOINING ROADWAY AS BASE LINE.

DATE	TEST NO.	DEPTH	PRE-WET		TEST - 1" DROP		TIME
			START	STOP	START	STOP	
7/2/77	1	1 1/2 ft	9:39	9:42	9:42	10:08	20
	2	5 ft	9:40	9:42	9:42	slight slump	
	3	11 1/2 ft	9:43	9:52	9:52	10:03	11 min
	4	5 ft	9:45	slight	slight	slight	

SOIL AUGER FINDING just soil start 5ft

TESTED BY [Signature]

REMARKS - See plot for test locations
absent
