

192
3.30

PERMIT

SEWAGE DISPOSAL SYSTEM

DEPARTMENT OF HEALTH AND MENTAL HYGIENE

P 48769

A REPAIR

DISTRICT _____

DATE 5/28/92

HOWARD COUNTY HEALTH DEPARTMENT

BUREAU OF ENVIRONMENTAL HEALTH
461-9933

TAX ID # 04-316495

DATE SYSTEM APPROVED _____

INDEXED

INSPECTOR _____

Robert R. Hopkins IS PERMITTED TO INSTALL _____ ALTER

ADDRESS 18805 Penn Shop Road, Mt. Airy, Maryland PHONE 831-7893

SUBDIVISION _____ LOT _____ ROAD 18805 Penn Shop Road

PROPERTY OWNER Shannon Hopkins

ADDRESS 18805 Penn Shop Road
Mt. Airy, Maryland 21771

SEPTIC TANK CAPACITY _____ GALLONS

NUMBER OF BEDROOMS _____

_____ SQUARE FEET PER BEDROOM

LINEAR FEET OF TRENCH REQUIRED _____

REPAIR - PURPOSE - Applicant proposes enlargement to residence potentially in conflict with of well and septic system. Percolation test required to establish sufficient area for long term septic capacity. Visual inspection of well and septic to determine if replacement would be required.

PLANS APPROVED BY _____ DATE _____

COVER NO WORK UNTIL INSPECTED AND APPROVED

NEITHER THE HOWARD COUNTY COUNCIL NOR THE HEALTH DEPARTMENT IS RESPONSIBLE FOR THE SUCCESSFUL OPERATION OF ANY SYSTEM

NOTE: CLEANOUT REQUIRED EVERY 70 FEET OF SEWER LINE AND/OR AT 90° SWEEPS IN LINES FROM HOUSE TO DRAIN FIELDS, 90° ELBOWS NOT ACCEPTABLE.

NOTE: ALL PARTS OF SEPTIC SYSTEMS (I.E. TANK, DISTRIBUTION BOX TRENCHES) TO BE 100 FEET FROM WELL (UNLESS OTHERWISE SPECIFICALLY AUTHORIZED)

NOTE: IF DEEP TRENCH(ES) ARE USED CALL FOR INSPECTION BEFORE AND AFTER PLACING GRAVEL IN TRENCH(ES)

NOTE: NO DRY WELL SHALL EXCEED 15 FOOT IN DIAMETER NO ABSORPTION TRENCH TO EXCEED 100 FEET IN LENGTH

NOTE: ALL PIPE FROM HOUSE TO SEPTIC TANK MUST BE CAST IRON OR SCHEDULE 35/40 PVC OR ABS

PERMIT VOID AFTER TWO YEARS

NOTE: INSTALL STAND PIPE ON SEPTIC TANK AND DRY WELL STAND PIPES MUST BE 6 INCHES IN DIAMETER CAST IRON, CONCRETE OR TERRA COTTA OR PVA OR ABS ACCEPTED. IF TOP OF SEPTIC TANK IS DEEPER THAN 3 FEET, MANHOLE TO GRADE REQUIRED.

NOTE: DISTRIBUTION BOXES MUST HAVE BAFFLES


BLDG. PERMIT SIGNED
AND RETURNED 6/24/92
Serial # 44776-addition

***INSTALLER IS RESPONSIBLE FOR OBTAINING FINAL APPROVAL ON THIS PERMIT**

HD-260(6-90)

*CALL 461-9933 FOR INSPECTION OF SEPTIC SYSTEM.

48769

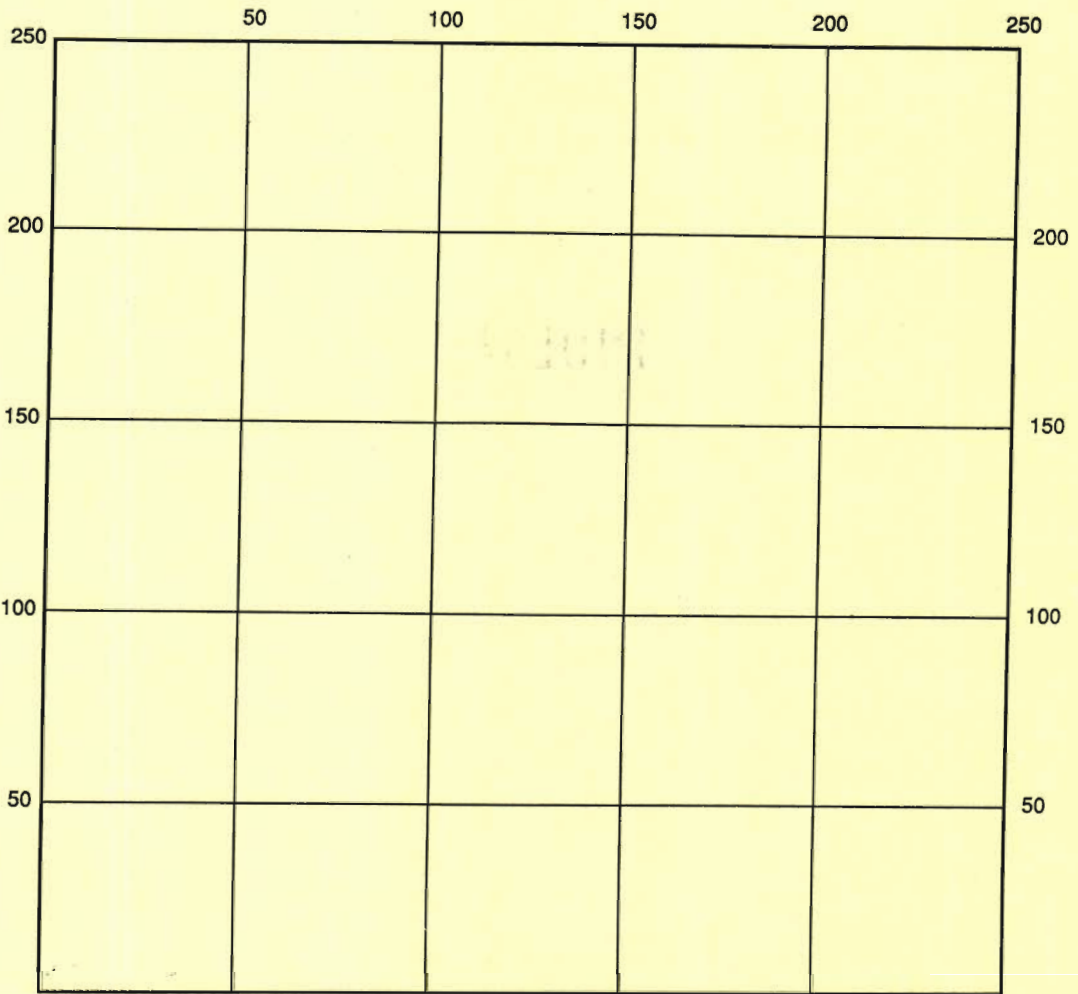

INDICATE NORTH - NAME ADJOINING ROADWAY AS BASE LINE

SEPTIC TANK LEVEL _____ CLEANOUTS _____

DISTRIBUTION BOX LEVEL _____

DRAIN FIELD/TITLE DEPTH _____ FT. TRENCH WIDTH _____ FT. INLET DEPTH _____ FT.

EFFECTIVE GRAVEL DEPTH _____ FT. TOTAL LENGTH _____ FT.

NUMBER OF TRENCHES _____ ONE SIDEWALL/BOTTOM AREA _____ SQ. FT.

DRYWALL INSIDE DIAMETER _____ FT. EFFECTIVE DEPTH BELOW INLET _____ FT.

ABSORBENT AREA _____ SQ. FT.

REMARKS: _____

DATE SYSTEM APPROVED _____ INSPECTOR _____

MEMO TO THE FILE:

March 29, 1993

RE: 18805 Penn Shop Road
Repair to Septic - Questionable
Receipt Number P48167

Mr. David Buechling called. He has been looking for septic (repair) records for this property. He feels that some septic work has been done without Health Department involvement.


According to Health notes, R. Pinkley did 2 perc tests on 5-18-92. He observed the existing septic tank 18.5 feet from the rear of the existing well, behind the house.

A repair permit was paid for on 5-28-92 but no permit was issued or work inspected.

Mr. Buechling feels a "new" septic tank is in place approximately 12 feet off the well behind the house.

David Buechling
831-5949
Prospective Buyer

JENodeau
Sanitarian



KERNAN

for Baltimore County Executive

9/23/86 - New septic
system, 4 yrs old,
This will be a
three (3) bedroom
house. JS


Phone No. H 829-12

Baltimore County Citizens for Kernan

Authority: Stephen Snyder, Treasurer





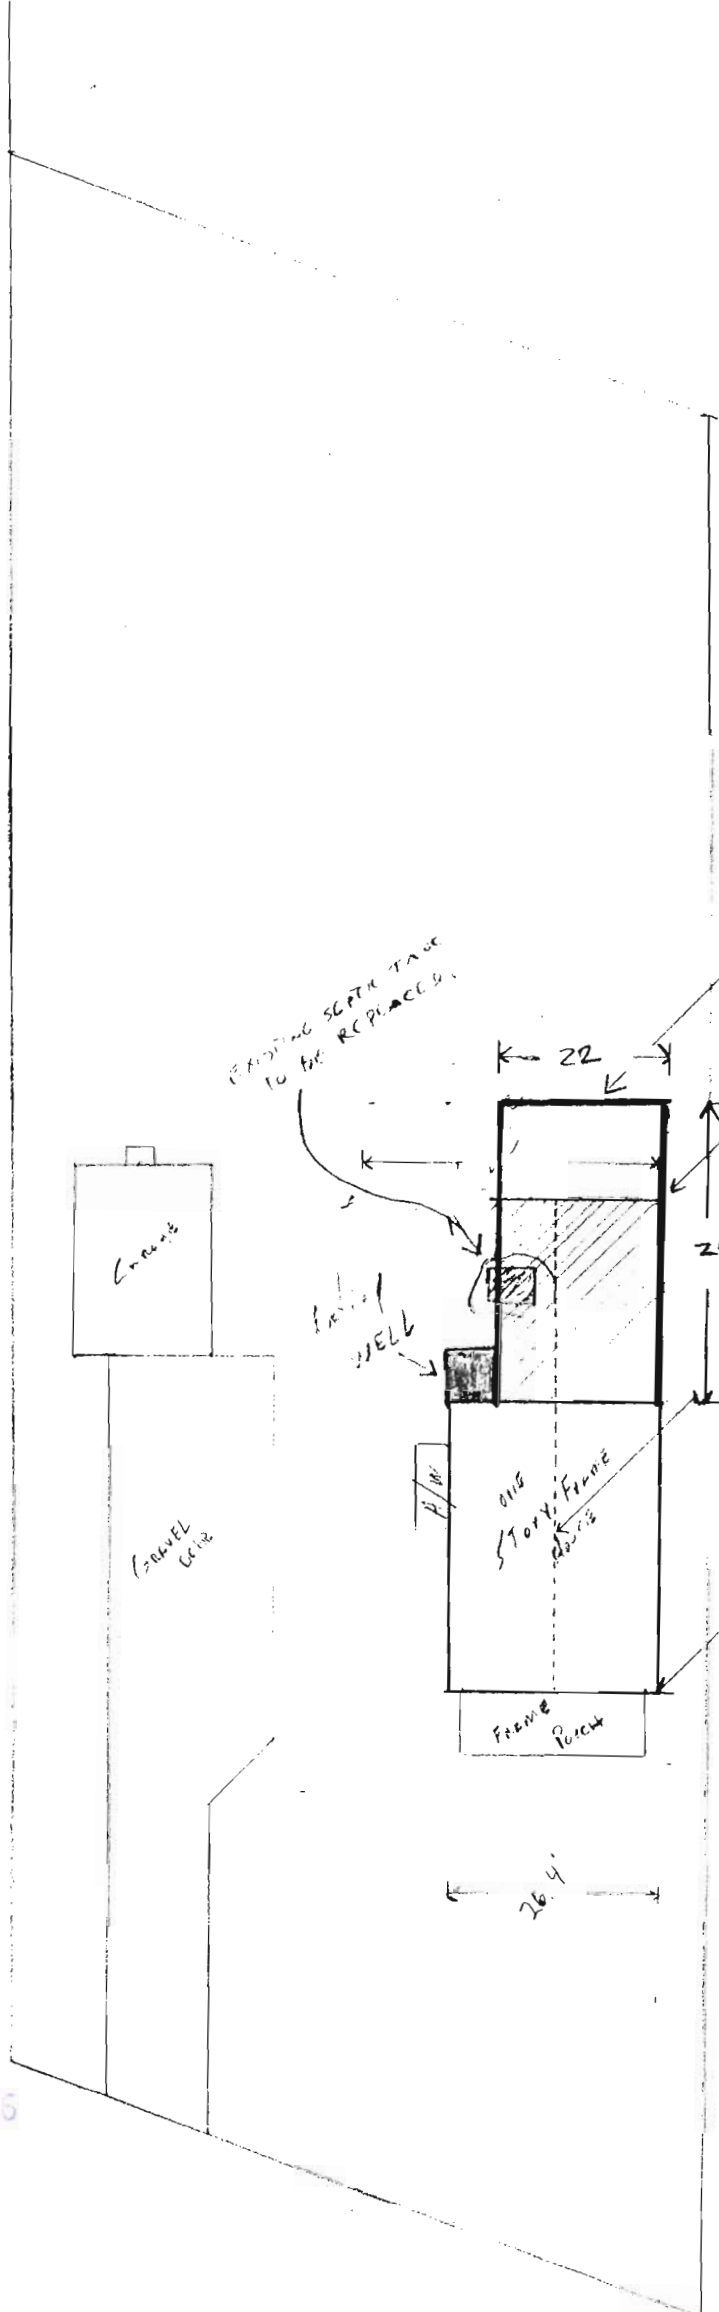

★ NEW Floor plan Agreement with

New wood frame Anchors

Match Existing Floor

Existing House

EXISTING SEPTIC TANK TO BE REPLACED

WELL

Cove

FRAME POCKET

NEW WOOD FRAME ANCHORS

FRAME POCKET

92 JUN 16 11 17:35

