

Bureau of Environmental Health
 8930 Stanford Boulevard, Columbia, MD 21045
 Main: 410-313-2640 | Fax: 410-313-2648
 TDD 410-313-2323 | Toll Free 1-866-313-6300
www.hchealth.org
 Facebook: www.facebook.com/hocohealth

Maura J. Rossman, M.D., Health Officer

RECEIPT DATE: 8-7-24 **ONSITE SEWAGE DISPOSAL SYSTEM** P 580713

APPROVAL DATE: 8/15/24 **PERMIT: REPAIR** A _____

PROPERTY ADDRESS: 12039 Patapsco Ridge Road, Marriottsville, MD 21104

SUBDIVISION: _____ LOT: P 57 TAX ID: 03-304450

CONTRACTOR: Freedom Septic Service EMAIL: christy@freedomseptic.com

CONTRACTOR ADDRESS: 580 Obrecht Road, Sykesville, MD 21784 PHONE: 410-795-5670

PROPERTY OWNER: Timothy & Erin Poandl EMAIL: _____

OWNER ADDRESS: 12039 Patapsco Ridge Road, Marriottsville, MD 21104 PHONE: 410-705-2947

SEPTIC TANK SIZE (GALLONS): Existing TANK MANUFACTURER: Existing

PUMP MODEL: N/A PUMP SIZE N/A PUMP TANK CAPACITY: N/A

DISTRIBUTION SYSTEM: GRAVITY PRESSURE DOSED BEDROOMS: 4 APPLICATION RATE: _____


TRENCHES:	LINEAR FEET REQUIRED: <u>104'</u>	INLET DEPTH: <u>2.5'</u>
	TRENCH WIDTH: <u>3'</u>	MAXIMUM BOTTOM DEPTH: <u>6'</u>
	MINIMUM SPACE BETWEEN TRENCHES: <u>9'-10'</u>	EFFECTIVE AREA BEGINNING DEPTH: <u>4'</u>
LOCATION:	SYSTEM STAKED BY INSTALLER AND VERIFIED BY APPROVING AUTHORITY DURING PRE-CONSTRUCTION INSPECTION.	
NOTES:	Install system per approved design plans	

ISSUED BY: S. Page ISSUE DATE: 8-7-24 EXPIRATION DATE: 8-7-25

- NOTE: CONTRACTOR MUST SCHEDULE A PRE-CONSTRUCTION INSPECTION PRIOR TO BEGINNING ANY INSTALLATION
- NOTE: CONTRACTOR MUST SCHEDULE AN INSPECTION AND GAIN APPROVAL OF ALL COMPONENTS PRIOR TO COVERING
- NOTE: STONE MUST BE APPROVED BY HEALTH DEPARTMENT AND GRAVEL TICKET MUST BE AVAILABLE FOR REVIEW.
- NOTE: WATERTIGHT TANKS REQUIRED
- NOTE: ALL PARTS OF SEPTIC SYSTEM SHALL BE AT LEAST 100 FEET DOWNGRAIENT FROM ANY WATER WELL
- NOTE: MANHOLE RISERS REQUIRED ON ALL SEPTIC TANKS AND PUMP CHAMBERS
- NOTE: AN ELECTRICAL PERMIT IS REQUIRED FOR INSTALLATION OF ANY ELECTRICAL COMPONENTS OF THE SYSTEM
- ELECTRICAL PERMIT ISSUED E N/A
- NOTE: MDE RECOMMENDS SEPTIC TANKS, BAT, AND OTHER PRETREATMENT UNITS BE PUMPED AT A FREQUENCY ADEQUATE TO ENSURE THAT SOLIDS ARE NOT DISCHARGED TO THE DISPOSAL AREA

**NEITHER THE HOWARD COUNTY COUNCIL NOR THE HEALTH DEPARTMENT IS RESPONSIBLE FOR THE SUCCESSFUL OPERATION OF ANY SYSTEM.
 PERMITTEE RESPONSIBLE FOR OBTAINING FINAL APPROVAL ON THIS PERMIT.
 CALL 410-313-1771 TO SCHEDULE INSPECTIONS.**

NOT TO SCALE

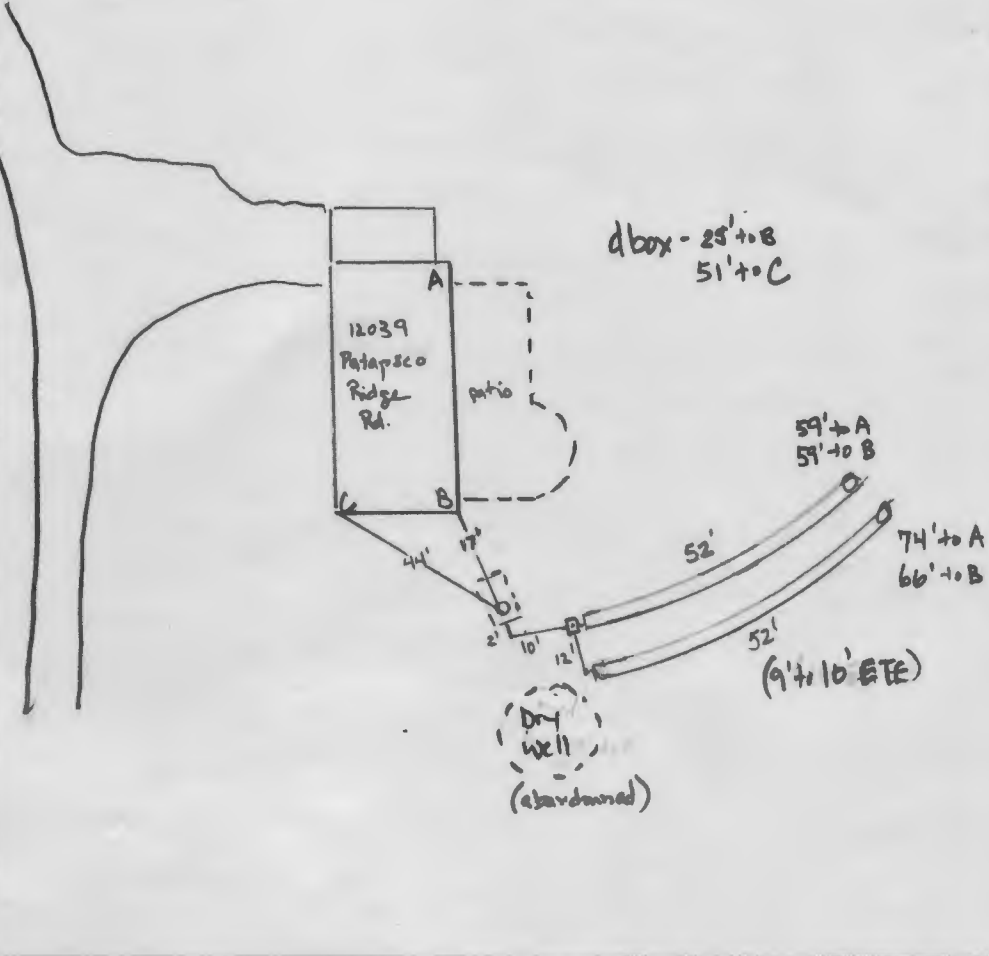

ROAD NAME

TRENCH/DRAINFIELD DATA

WIDTH	INLET	BOTTOM
3'	2.5'	6'
NUMBER OF TRENCHES		2
TOTAL LENGTH		104'
ABSORPTION AREA		312 sqft + sidewall
DISTRIBUTION BOX LEVEL		yes
DISTRIBUTION BOX BAFFLE		yes
DISTRIBUTION BOX PORT		yes

SEPTIC TANK DATA use

SEPTIC TANK 1 LEVEL	(existing)
MANUFACTURER	N/A
CAPACITY	1500? GAL
SEAM LOC	med
TANK LID DEPTH	8"
BAFFLES	Yes
BAFFLE FILTER	-
MANHOLE LOC	Rear
6" PORT LOC	none
WATERTIGHT TEST	OK
SLOTTED	no
DATE ON LID	N/A

PUMP/SEPTIC TANK LEVEL

MANUFACTURER	
CAPACITY	GAL
SEAM LOC	
TANK LID DEPTH	
BAFFLES	
BAFFLE FILTER	
MANHOLE LOC	
6" PORT LOC	
WATERTIGHT TEST	
SLOTTED	
DATE ON LID	

SEPTIC CONTRACTOR ONSITE INSTALLING SYTEM: Dan Farrow
SEPTIC CONTRACTOR ONSITE LICENSED WITH THE STATE OF MD YES/NO

PRE-CONSTRUCTION NOTES:
8/7/2024 Design plan approved (SP)

CONTROL PANEL DATA

CONTROL PANEL HEIGHT	(MIN 30")
INSPECTION DATE	
INSPECTION: PASS/FAIL (CIRCLE ONE)	

INSTALLATION NOTES:

8/14/24 - inspection w/ contractor onsite, backline out of the septic tank was installed, dbox & line to bottom trench completed - most of the bottom trench completed, contractor waiting on stone, stone used in the trench. So far looks ok, geo-textile fabric in place, observation port in place, ok to continue (w/ 8/15/24 - 2nd (top) trench completed, stone ok, fabric in place, observation port good, dbox levelers ok & the drywell was pumped out, collapsed, and fill in w/ dirt, ok to backfill, no new riser installed on septic tank (22)
(9'-10" between trenches)

FINAL INSPECTOR R. Zapport DATE OF APPROVAL 8/15/24

Septic repair design plan

Freedom Septic
2804 Liberty
Sikeston, MO
407-785-2947
Plan - Dan Farrow
performed

4890
Peppard - home owner
240-1150
of Peppards
12039 Peppard
Marionville, MO
loads #2 Stone
washed

Approved Septic System Plan
Howard County Health Department
S. Page
8/17/2024



3W
2.5 INLET
6 BOTTOM
10.5 TOTAL TRENCH
2 x 52



**Howard County
Health Department**

Bureau of Environmental Health

8930 Stanford Boulevard, Columbia, MD 21045

Main: 410-313-2640 | Fax: 410-313-2648

TDD 410-313-2323 | Toll Free 1-866-313-6300

www.hchealth.org

Facebook: www.facebook.com/hocohealth

Maura J. Rossman, M.D., Health Officer

RECEIPT DATE: _____ **ONSITE SEWAGE DISPOSAL SYSTEM** P _____

APPROVAL DATE: _____ **PERMIT: REPAIR** A _____

PROPERTY ADDRESS: 12039 Patapsco Ridge Road, Marriottsville, MD 21104

SUBDIVISION: _____ LOT: P 57 TAX ID: 03-304450

CONTRACTOR: Freedom Septic Service EMAIL: christy@freedomseptic.com

CONTRACTOR ADDRESS: 580 Obrecht Road, Sykesville, MD 21784 PHONE: 410-795-5670

PROPERTY OWNER: Timothy & Erin Poandl EMAIL: _____

OWNER ADDRESS: 12039 Patapsco Ridge Road, Marriotsville, MD 21104 PHONE:- 410-705-2947

SEPTIC TANK SIZE (GALLONS): Existing TANK MANUFACTURER: Existing

PUMP MODEL: N/A PUMP SIZE N/A PUMP TANK CAPACITY: N/A

DISTRIBUTION SYSTEM: GRAVITY PRESSURE DOSED BEDROOMS: 4 APPLICATION RATE: _____

TRENCHES:	LINEAR FEET REQUIRED: <u>104</u>	INLET DEPTH: <u>2.5</u>
	TRENCH WIDTH: <u>3</u>	MAXIMUM BOTTOM DEPTH: <u>6</u>
	MINIMUM SPACE BETWEEN TRENCHES: _____	EFFECTIVE AREA BEGINNING DEPTH: <u>4</u>
LOCATION:	SYSTEM STAKED BY INSTALLER AND VERIFIED BY APPROVING AUTHORITY DURING PRE-CONSTRUCTION INSPECTION.	
NOTES:	Install system per approved design plans	

ISSUED BY: S. Page ISSUE DATE: _____ EXPIRATION DATE: _____

NOTE: CONTRACTOR MUST SCHEDULE A PRE-CONSTRUCTION INSPECTION PRIOR TO BEGINNING ANY INSTALLATION

NOTE: CONTRACTOR MUST SCHEDULE AN INSPECTION AND GAIN APPROVAL OF ALL COMPONENTS PRIOR TO COVERING

NOTE: STONE MUST BE APPROVED BY HEALTH DEPARTMENT AND GRAVEL TICKET MUST BE AVAILABLE FOR REVIEW.

NOTE: WATERTIGHT TANKS REQUIRED

NOTE: ALL PARTS OF SEPTIC SYSTEM SHALL BE AT LEAST 100 FEET DOWNGRADIENT FROM ANY WATER WELL

NOTE: MANHOLE RISERS REQUIRED ON ALL SEPTIC TANKS AND PUMP CHAMBERS

NOTE: AN ELECTRICAL PERMIT IS REQUIRED FOR INSTALLATION OF ANY ELECTRICAL COMPONENTS OF THE SYSTEM


ELECTRICAL PERMIT ISSUED E N/A

NOTE: MDE RECOMMENDS SEPTIC TANKS, BAT, AND OTHER PRETREATMENT UNITS BE PUMPED AT A FREQUENCY ADEQUATE TO ENSURE THAT SOLIDS ARE NOT DISCHARGED TO THE DISPOSAL AREA

NEITHER THE HOWARD COUNTY COUNCIL NOR THE HEALTH DEPARTMENT IS RESPONSIBLE FOR THE SUCCESSFUL OPERATION OF ANY SYSTEM.

PERMITTEE RESPONSIBLE FOR OBTAINING FINAL APPROVAL ON THIS PERMIT.

CALL 410-313-1771 TO SCHEDULE INSPECTIONS.

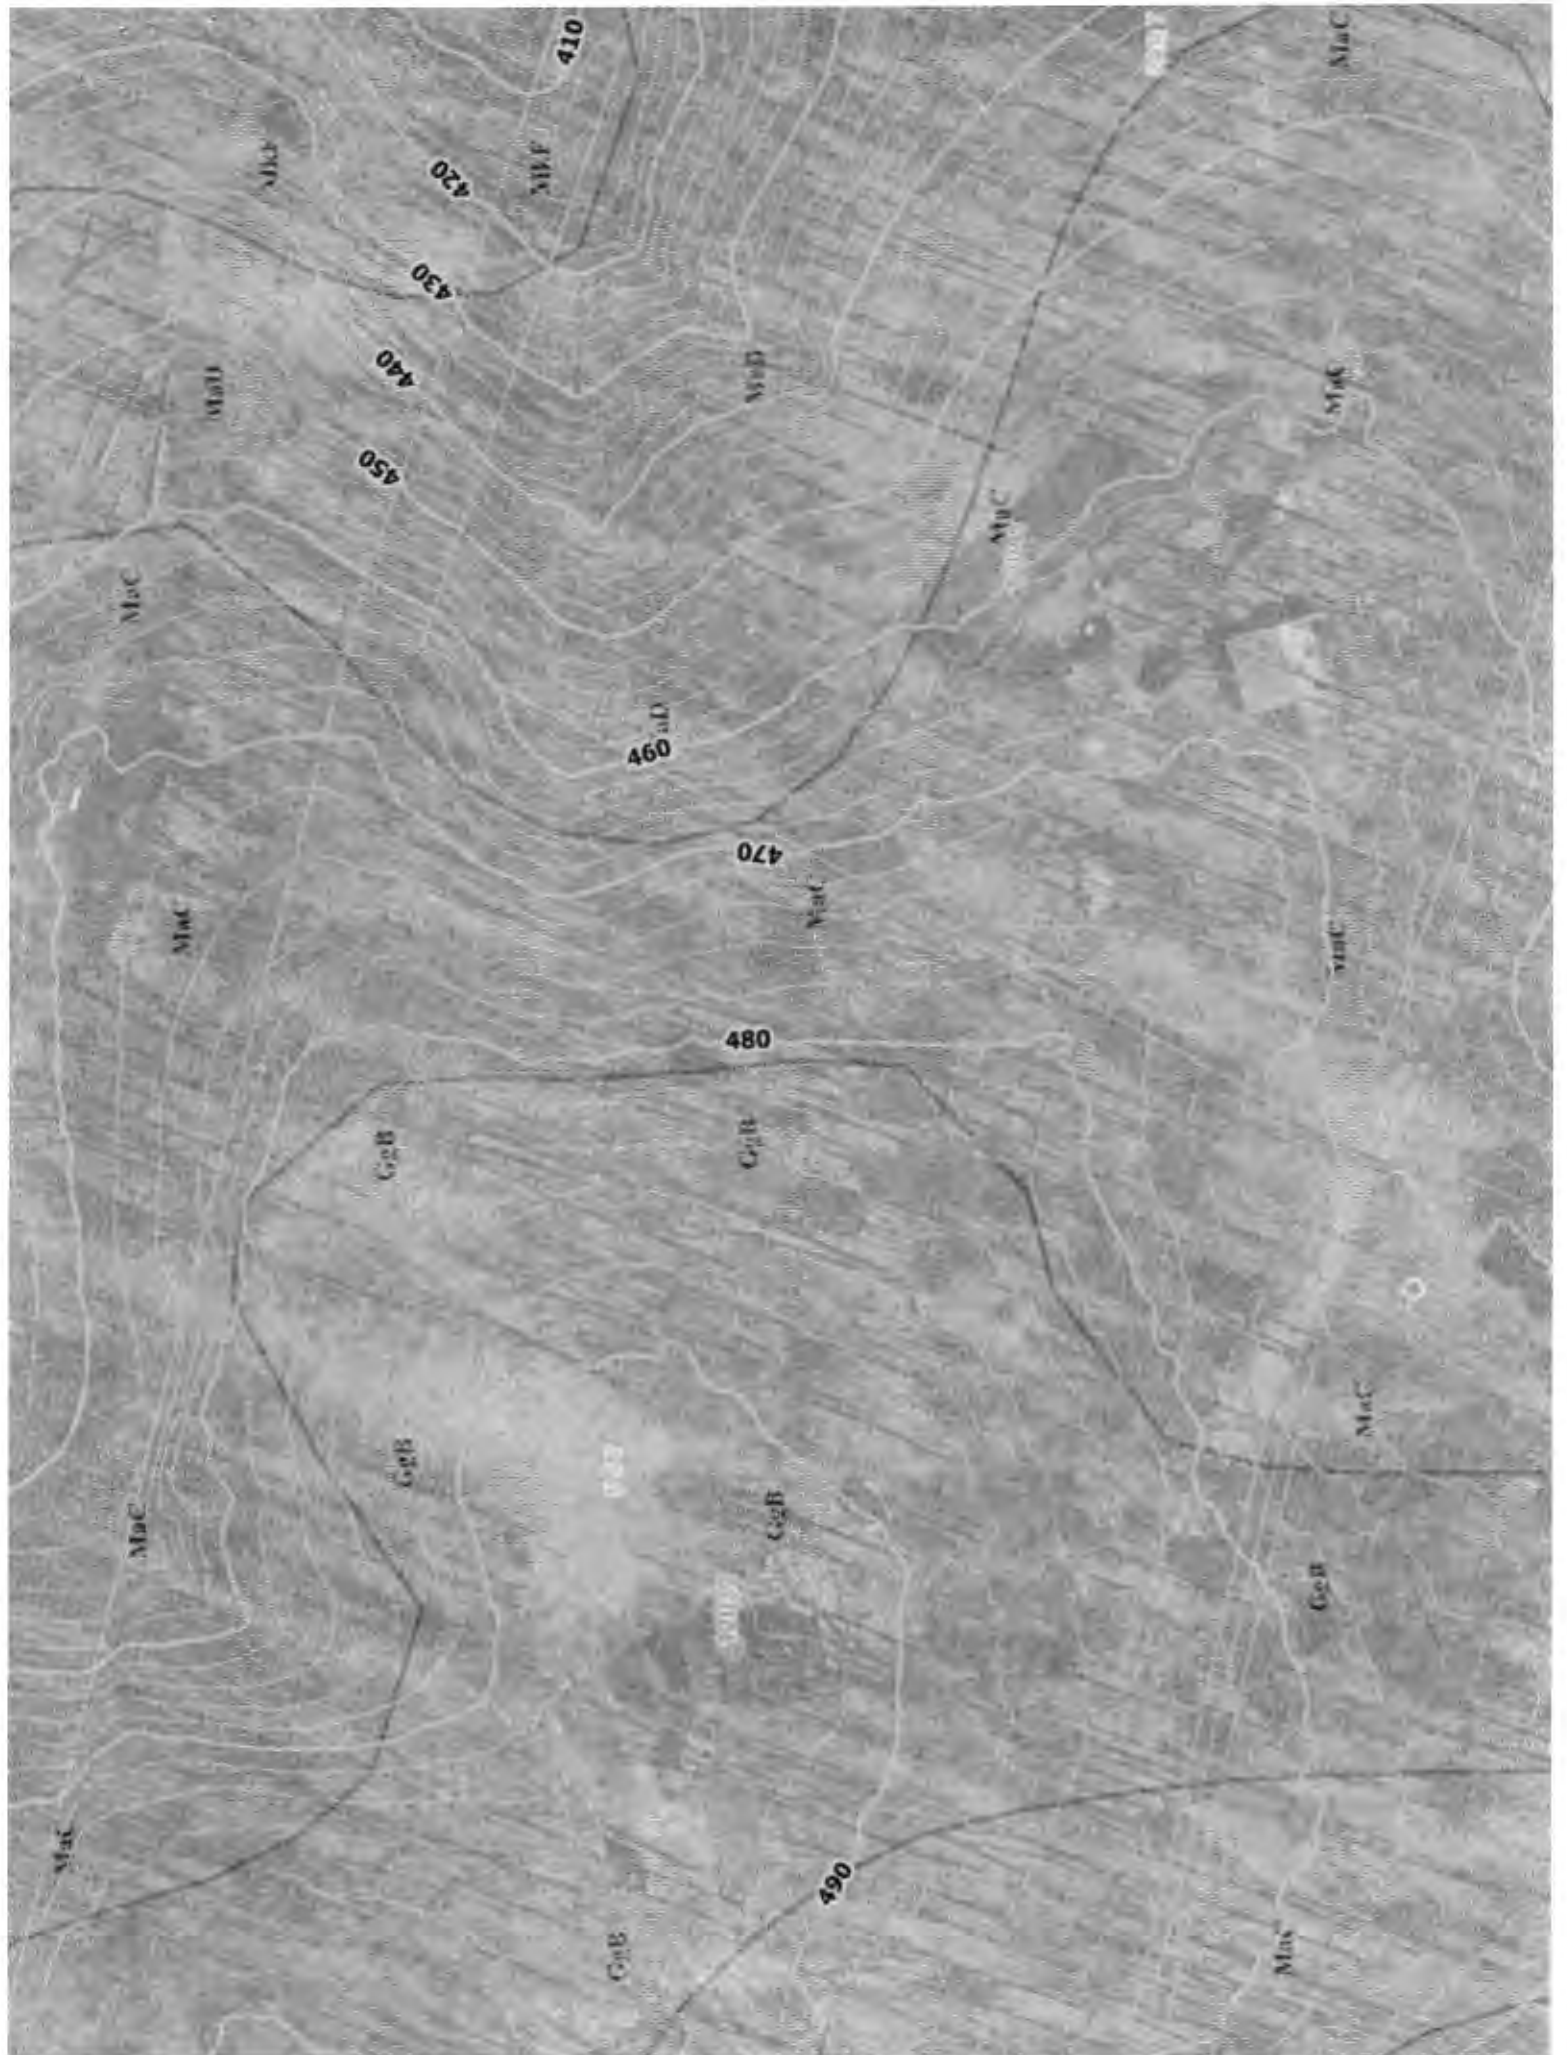

Transaction Code: BW0P0B723B12
Date: 08/07/2024 09:54:59 AM
Card Type: Visa
Card Number: xxxxxxxxxxxx9322
Authorization Code: 111111
Total Amount: \$265.00
Operator ID: SMARTIN
Cash Drawer ID :
Record: WS-SP-APP-24-00136
I agree to pay the above amount according to the Credit Card issuer agreement.
Sign Below:

Print Receipt

Cancel

Transaction Code: BW0P0B723B12
Date: 08/07/2024 09:54:59 AM
Card Type: Visa
Card Number: xxxxxxxxxxxx9322
Authorization Code: 111111
Total Amount: \$265.00
Operator ID: SMARTIN
Cash Drawer ID :
Record: WS-SP-APP-24-00136

I agree to pay the above amount according to the Credit Card issuer agreement.

Sign Below:

Print Receipt

Cancel

RECEIPT

Howard County, MD
HOWARD COUNTY HEALTH DEPARTMENT
ASCEND ONE BUILDING
Columbia, MD 21045
8930 STANFORD BLVD

Application: WS-SP-APP-24-00136
Application Type: EnvHealth/Well and Septic/Sewage Disposal System/Application
Address: 12039 PATAPSCO RIDGE RD, Marriottsville, 21104

Receipt No.	Ref Number	Amount Paid	Payment Date	Cashier ID	Received	Comments
10405		\$265.00	08/07/2024	SMARTIN		

Owner Info.:
POANDI TIMOTHY E
12039 PATAPSCO RIDGE RD
MARRIOTTSVILLE, MD 21104

Work Description:



HOWARD COUNTY HEALTH DEPARTMENT

86773

CODES

DATE
8 / 17 / 24

CASH
 CHECK
NO. 00

Received From

Freedom Septic

For

Septic Service - 12031 Palmyra Rd

Two hundred fifty dollars

Dollars

\$ 250.00

Received By

[Signature]

Approved Public System from
Howard County Health Department

104

104
