

Approved 6/26/24
-H.O.

Record Detail * (This section is required.)

Permit Type	Permit Number	Opened Date
Building/Residential/Misc/Deck	B24002141	06/10/2024
Description of Work		
SFD / CONSTRUCT A MULTI LEVEL 41 X 4 WALKWAY (DECK) ALONG SIDE OF HOUSE		

[check spelling](#)

Online BP.

gjs 6/26/24

Address * (This section is required.)

Search Reset Clear Get Parcel & Owner

Street #	Street Name	Street Type	
17015	FREDERICK	RD	
Unit Type	Unit #	X Coordinate	Y Coordinate
-Select-		-77.1072	39.34541
City	State	Zip Code	Primary
MOUNT AIRY	MD	21771	Yes

Parcel * (This section is required.)

Search Reset Clear Get Address & Owner

GIS ID *	Parcel	Parcel Area	Land Value	Improved Value	Exemption Value	Plan Area
917072	15	1.03	60300	505900	41780	RURAL
Legal Description						
LOT 7,8,9 []17015 FREDERICK RD []POPLAR HGTS						

[check spelling](#)

Block	Lot	Census Tract	Council Dist	Inspection Dist	Supervisor Dist	Map #	DAP Zone
	7 8 9	604001	5				
Plan Area	State Tax Id		Subdivision Name				
	1404316517						
Section	Area		Tax Map				
			7				
Grid	Zoning District		ADC Map				
7-2	RC-DEO		4691-C5				
SDP No.	Final Plan No.		WP File No.				
Record Plat No.	WS Contract No.		FDP No.		Primary		
3/026					Yes		
Owner Occupied	Year Built		Historic District				
<input type="radio"/> Yes <input type="radio"/> No	2017		<input type="radio"/> Yes <input checked="" type="radio"/> No				
Historic District Registry No.	Stat Area		Flood Plain				
	4-04		<input type="radio"/> Yes <input checked="" type="radio"/> No				
Building No							

Owner * (This section is required.)

Search Reset Clear

Name *
BETAN

Address Line 1
17015 FREDERICK RD


Address Line 2

Address Line 3

Submit

Cancel

10/07/17
11-15-289

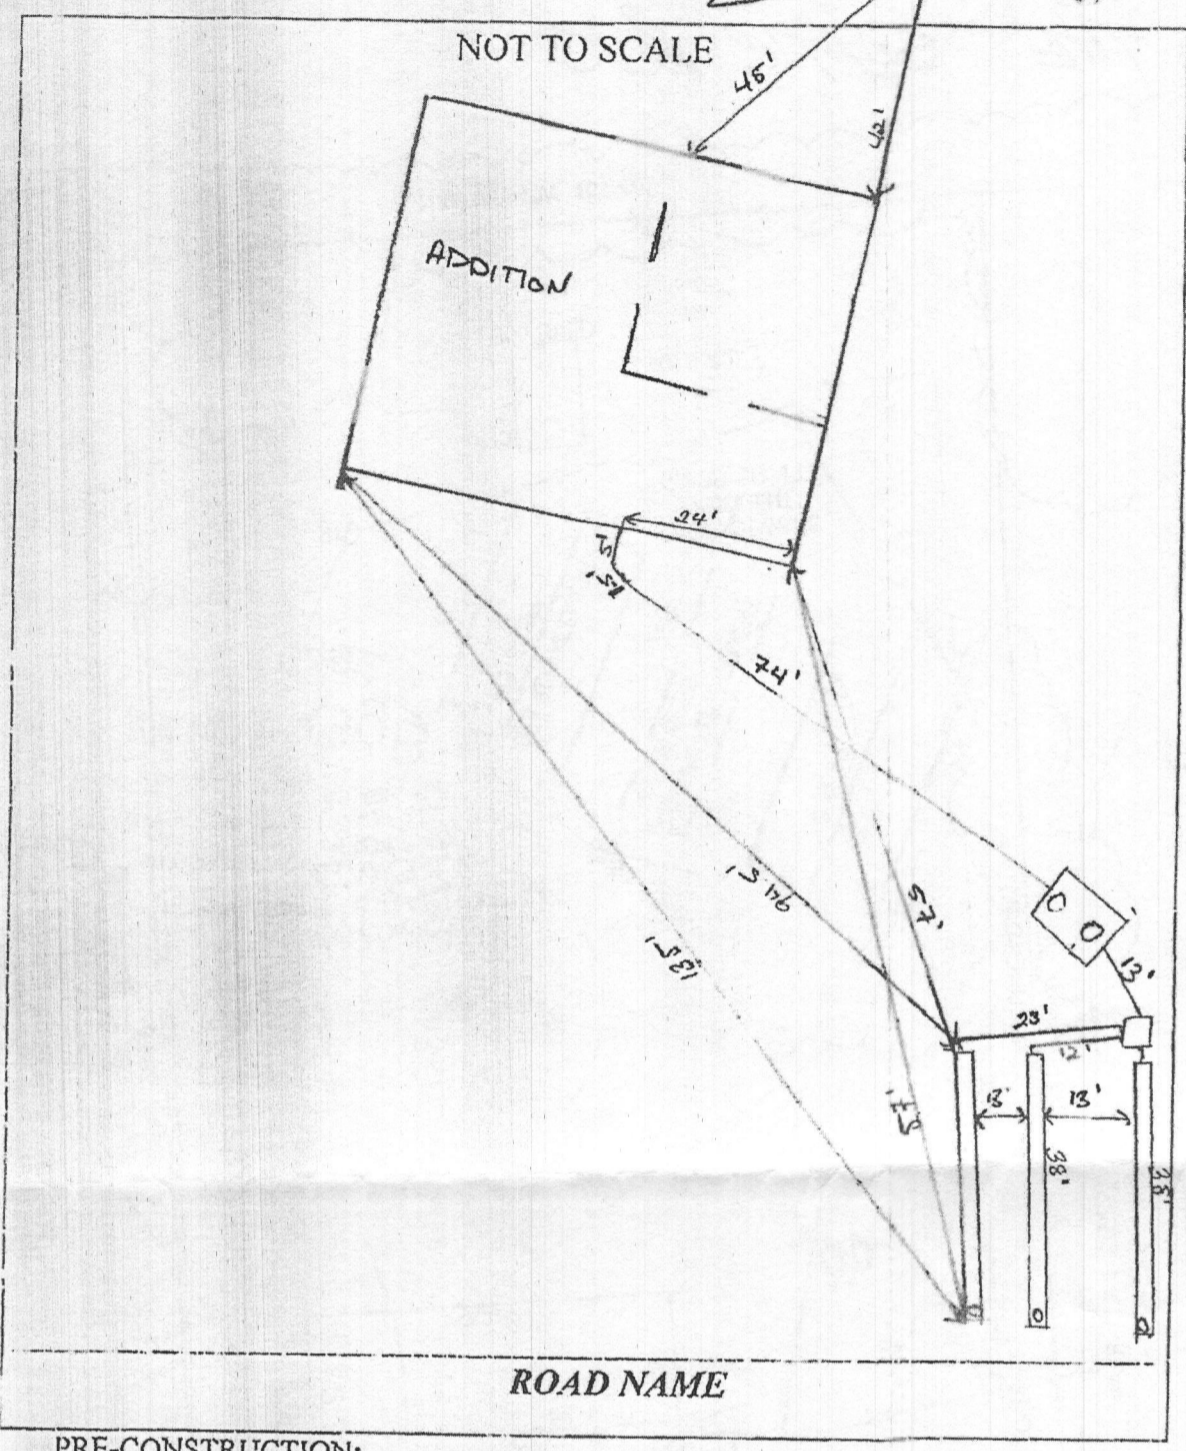

TRENCH/DRAINFIELD DATA		
WIDTH	INLET	BOTTOM
3'	4'	8'
NUMBER OF TRENCHES	3	
TOTAL LENGTH	114'	
ABSORPTION AREA	342 sq ft ^{side area}	
DISTRIBUTION BOX LEVEL	yes	
DISTRIBUTION BOX BAFFLE	yes	
DISTRIBUTION BOX PORT	yes	

SEPTIC TANK DATA	
SEPTIC TANK 1 LEVEL	
MANUFACTURER	Babylon
CAPACITY	1500 GAL
SEAM LOC	TOP
TANK LID DEPTH	15'
BAFFLES	yes
BAFFLE FILTER	N/A
MANHOLE LOC	Front/Rear
6" PORT LOC	yes
WATERTIGHT TEST	
SLOTTED	yes
DATE ON LID	01/07/2017
PUMP/SEPTIC TANK LEVEL	
MANUFACTURER	
CAPACITY	
SEAM LOC	
TANK LID DEPTH	
BAFFLES	
BAFFLE FILTER	
MANHOLE LOC	
6" PORT LOC	
WATERTIGHT TEST	
SLOTTED	
DATE ON LID	

PRE-CONSTRUCTION:
 2/6/17 Met Tom Seal on site for layout. 3 of 6 septic SDA corner stakes present. Shot corners and laid out 3x39 trenches. Tank will be 700 from well, 72' off house. Must have SDA corners restaked prior to installing trenches. (S) 2/7/17 on site with Mike Davis. Placed flags at trench ends and tank corners for owner to verify. Homeowner choosing not to have SDA restaked - trenches may extend out of SDA, but are on property. OK for contractor to proceed with install per Mike Davis. (S)

INSTALLATION:
 02/13/2016 On Site for completion of third trench. Captured measurements for the at-built. OK to backfill. (S)

FINAL INSPECTOR [Signature] DATE OF APPROVAL 02/14/2017

11/15/17
 24-054-00341-01-01
 2-10-17
