

1/19/89

PERMIT

P 43/85

SEWAGE DISPOSAL SYSTEM

A REPAIR

MARYLAND STATE DEPARTMENT OF HEALTH

DISTRICT _____

HOWARD COUNTY
BUREAU OF ENVIRONMENTAL HEALTH
461-9933

DATE 12/12/88

DATE SYSTEM APPROVED 1/20/89

INDEXED

INSPECTOR M. RIFKIN

ROY BAUMAN IS PERMITTED TO INSTALL _____ ALTER X

ADDRESS _____ PHONE _____

SUBDIVISION _____ ROAD Elibank Drive LOT _____

PROPERTY OWNER Belmont Conference Center
Elibank Drive

ADDRESS _____

IF GARBAGE GRINDER IS USED INCREASE SEPTIC TANK CAPACITY BY 50% AND ABSORPTION AREA BY 22%.

GARBAGE GRINDER? YES _____ NO _____

SEPTIC TANK CAPACITY _____ GALLONS NUMBER OF BEDROOMS _____

REPAIR - TO REPLACE FAILING DRYWELL - 5 BEDROOM HOUSE TO BE CONVERTED TO OVERNITE
ACCOMMODATIONS. NO KITCHEN FACILITIES. ok

INSTALL 75' TRENCH W/ 5' STONE COVER

PLANS APPROVED BY C. Williams DATE 12/09/88

COVER NO WORK UNTIL INSPECTED AND APPROVED

NEITHER THE HOWARD COUNTY COUNCIL NOR THE HEALTH DEPARTMENT IS RESPONSIBLE FOR THE SUCCESSFUL OPERATION OF ANY SYSTEM

NOTE: CLEANOUT REQUIRED EVERY 70 FEET OF SEWER LINE AND/OR AT 90° SWEEPS IN LINES FROM HOUSE TO DRAIN FIELDS

NOTE: ALL PARTS OF SEPTIC SYSTEMS (I.E. TANK, DISTRIBUTION BOX, TRENCHES) TO BE 100 FEET FROM WELL (UNLESS OTHERWISE SPECIFICALLY AUTHORIZED)

NOTE: IF DEEP TRENCHES ARE USED CALL FOR INSPECTION BEFORE AND AFTER PLACING GRAVEL IN TRENCHES

NOTE: NO DRY WELL SHALL EXCEED 15 FOOT IN DIAMETER NO ABSORPTION TRENCH TO EXCEED 100 FEET IN LENGTH

NOTE: ALL PIPE FROM HOUSE TO SEPTIC TANK MUST BE CAST IRON OR SCHEDULE 40 PVC OR ABS

PERMIT VOID AFTER TWO YEARS

NOTE: INSTALL STAND PIPE ON SEPTIC TANK AND DRY WELL. STAND PIPES MUST BE 6 INCHES IN DIAMETER. CAST IRON, CONCRETE OR TERRA COTTA OR PVC OR ABS ACCEPTED. IF TOP OF SEPTIC TANK IS DEEPER THAN 3 FEET, MANHOLE TO GRADE REQUIRED


NOTE: DISTRIBUTION BOXES MUST HAVE BAFFLES

***INSTALLER IS RESPONSIBLE FOR OBTAINING FINAL APPROVAL ON THIS PERMIT**

*CALL 461-9933 FOR INSPECTION OF SEPTIC SYSTEMS.

HD-260

43/85

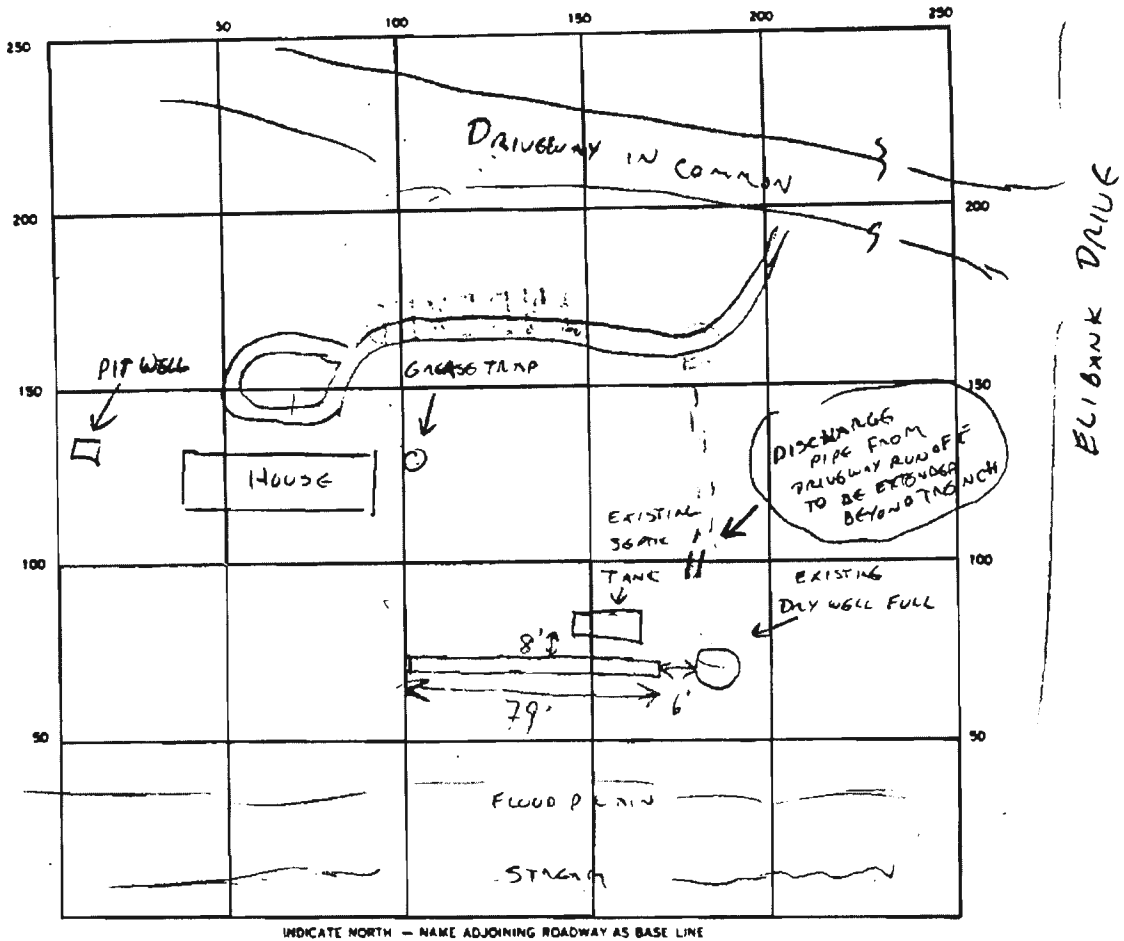

SEPTIC TANK LEVEL EXISTING CLEANOUTS EXISTING

DISTRIBUTION BOX LEVEL N/A

DRAIN FIELD/TILE FIELD DEPTH 8 FT TRENCH WIDTH 22 FT. INLET DEPTH 3 FT.

EFFECTIVE GRAVEL DEPTH 5 FT. TOTAL LENGTH 75 FT

NUMBER OF TRENCHES 1 ONE SIDEWALL AREA SQ. FT.

DRYWELL INSIDE DIAMETER Existing FT EFFECTIVE DEPTH BELOW INLET 5 FT

ABSORBENT AREA 375 SQ. FT.

REMARKS 12/20/88 TEST HOLE OK TO 13" INSTALL 75' TRENCH W/5' STONE

1/18/89 LAY-OUT DISCUSSED WITH NEW CONTRACTOR. C.W.

1/19/89 TRENCH DUG READY FOR STONE CONTINUE, FINAL TOMORROW 9-10 a.m MR

1/20/89 TRENCH OK TO COVER MR

DATE SYSTEM APPROVED 1/20/89 INSPECTOR M. E. Kim

HOWARD COUNTY

PERMIT APPLICATION

DEPARTMENT OF PUBLIC WORKS
BUREAU OF INSPECTIONS LICENSES & PERMITS
3430 COURT HOUSE DRIVE, ELLICOTT CITY, MARYLAND 21043

SERIAL NUMBER

0 301 1

APPLICATION
ONING #
BA 88-33-E

BUILDING ADDRESS (BLOCK NO., STREET, TOWN OR AREA)
6566 BELMONT WOODS RD
ELK RIDGE MD

GRADING/SEDIMENT CONTROL YES NO

DESCRIPTION OF WORK AUTHORIZED
CONVERT 3 CLOSETS INTO
A BATH RM.

LOT NO.	PARCEL NO.	SEC.	AREA	BLOCK NO.	LIBER	FOLIO
11A	P-21			19	111	1
SUB DIVISION	ZONE	ZONE MAP	ELEC. DIST.	CENSUS TR.		
11A	R-20	32	1	6C11		

OWNER'S NAME AND ADDRESS
AMERICAN CHEMICAL SOCIETY
1155 16TH ST NW
WASHINGTON DC 20036

OCCUPANT'S NAME AND ADDRESS
T/ BELMONT CONFERENCE CENTER
1/4 6555 BELMONT WOODS RD 21221

ARCHITECT OR ENGINEER'S NAME AND ADDRESS
SAME

CONTRACTOR'S NAME AND ADDRESS
SAME

EXISTING USE
RESIDENCE

PROPOSED USE
5 BED RMS
FOR 5 GUESTS

EST. CONSTRUCTION COST
\$3,000

LICENSE NUMBER
PERMIT FEE

W/S CODE

FOR OFFICE USE ONLY

DISTANCE IN FEET FROM R/W LINE TO FRONT BUILDING LINE

SIDE YARD
(DISTANCE IN FEET FROM SIDE BLDG. LINE TO SIDE PROPERTY LINE)
DISTANCE IN FEET FROM SIDE STREET R/W LINE

TO SIDE BUILDING LINE
DISTANCE IN FEET, REAR YD. REQUIRING SET

BACK CONDITIONS (IF ANY) (CORNER LOT ONLY)

Checks payable to DIRECTOR OF FINANCE OF HOWARD COUNTY

CAUTION

To begin construction before a permit placard has been issued and displayed on the job is a violation of the law.
Use and occupancy permit must be applied for two weeks before it will be issued.

IMPORTANT: PLEASE SHOW ZIP CODES AND AREA CODES WHEREVER REQUIRED.

LP-69
Revised

SIZE OF BLDG.	FRONT	DEPTH	HEIGHT
36' x 25 1/2'	36	25 1/2	2 1/2

TYPE OF BLDG.	AREA	VOLUME	ROOF
B. ROOMS			SLATE
ROOMS			4
BATHS			2
FIREPLACES			

FOOTINGS	FOUNDATION	S. WALLS
CONCRETE	SILOVE	BRICK

UTILITIES					
WATER	WELL	SEWER	SEPTIC	GAS	ELECTRICITY
					AC

I have carefully examined and read this application and know the same is true and correct, and that in doing this work, all provisions of Howard County Ordinances and the State Laws of Maryland will be complied with, whether specified or not; and I will notify the Bureau of Inspections, and Permit twenty-four hours in advance when I am ready for the inspections called for elsewhere in this application; and that no work will be covered up until such inspections have been completed with.

Signature: *Elmer...*
TITLE: *...*
DATE: *1/17/89*

FUNCTION	DATE	SIGNATURE APPROVAL
ZONING/PLANNING		
SHA		
SEDIMENT/GRADING		
BUILDING OFFICIAL		
WATER & SEWER		
HEALTH DEPT.	6/20/89	<i>Craig...</i>
FIRE PROTECTION		
STORM WATER MGM.		

Distribution of Copies:
White - Building Official
Green - Planning & Zoning

Yellow - Engineering
Pink - Health Dept.
Gold - S.H.A.

Fyock Septic Service, Inc.

P.O. Box 89
Glenelg, MD 21737
(410) 988-9270

CERTIFICATION OF SEPTIC SYSTEM

Property 6550 Belmont Woods
Elkridge, MD 21075

Buyers

Sellers

CLEAN OUTS EXPOSED

YES / NO

BAFFLES INTACT

YES / NO

WATER LEVEL IN SEPTIC TANK

HIGH / NORMAL / LOW

WATER LEVEL IN DRYWELL

HIGH / NORMAL / LOW / NA

TOILETS FLUSH PROPERLY

YES / NO

SYSTEM WORKING PROPERLY AT THIS TIME

YES / NO

PASSED / FAILED

COMMENTS

System was fine, had no issues at all.

Service Driver



Don Martini

Date

4/22

Permit #

4/19

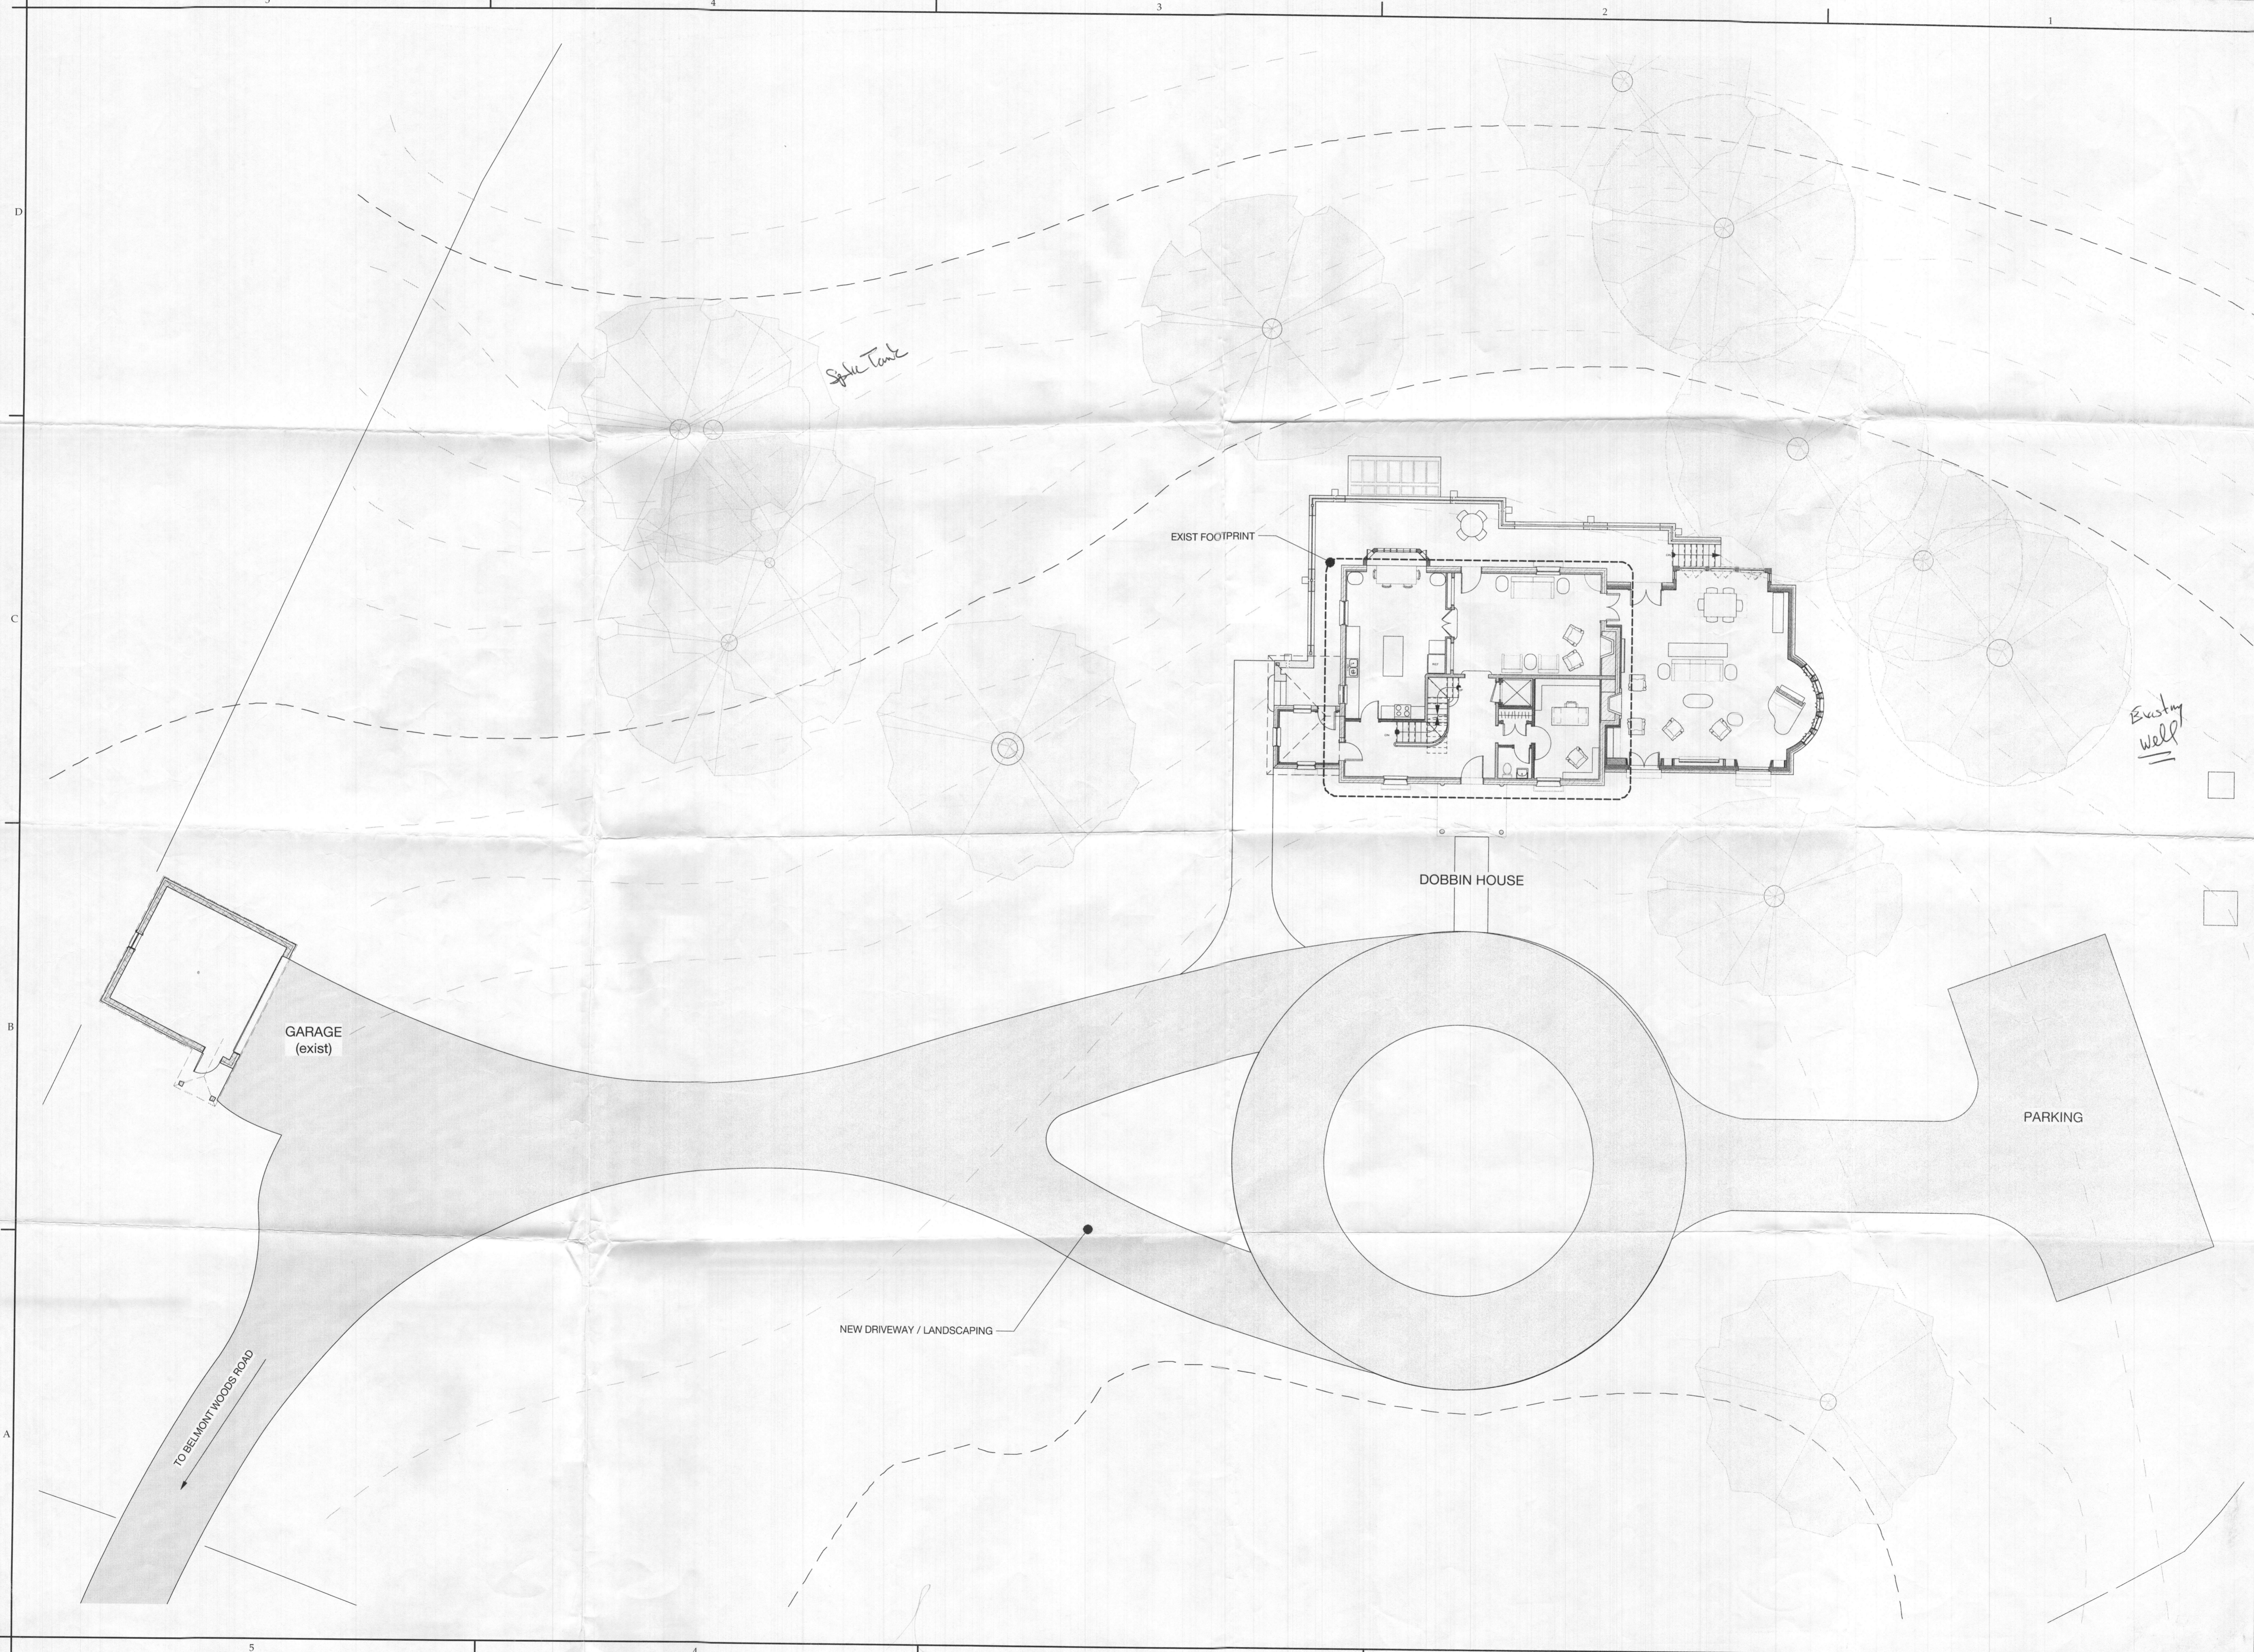

WILLIAM SLOAN ASSOCIATES
ARCHITECTS
331 MAIN STREET WINCHESTER, MA 01890

Issues / Revisions

No.	Date	Notes
-----	------	-------

Project Manager	CS
Reviewed By	CS
Checked By	CS
Drawn By	JW / KR
Designed By	CS
Date	08/24/15
Drawing Title	

SITE
PLAN

Scale 3/32" = 1'-0"

Drawing No.

A100
