

8/23/94  
Anytime

# PERMIT

## SEWAGE DISPOSAL SYSTEM

### DEPARTMENT OF HEALTH AND MENTAL HYGIENE

02-194-279

P 50215  
A 18068  
A REPAIR

DISTRICT 2nd

DATE 08/12/94

#### HOWARD COUNTY HEALTH DEPARTMENT

BUREAU OF ENVIRONMENTAL HEALTH

~~XXXXXXXX~~ 313-2640

DATE SYSTEM APPROVED 8/23/94

INSPECTOR Am

INDEXED

Vince Marino P & H, Inc.

IS PERMITTED TO INSTALL ALTER X

ADDRESS 2608 Hoffman Mill Road, Hampstead, Maryland 21074 PHONE 410-876-1928

SUBDIVISION \_\_\_\_\_ LOT \_\_\_\_\_ ROAD 3574 Church Road

PROPERTY OWNER George Bayless

ADDRESS 3574 Church Road  
Ellicott City, Maryland 21043

SEPTIC TANK CAPACITY \_\_\_\_\_ GALLONS

NUMBER OF BEDROOMS \_\_\_\_\_

SQUARE FEET PER BEDROOM \_\_\_\_\_

LINEAR FEET OF TRENCH REQUIRED \_\_\_\_\_

REPAIR - PURPOSE - TO ALLOW AN ADDITIONAL CONNECTION TO THE EXISTING SEPTIC SYSTEM.

Call for inspection when ground is opened so sanitarian can relocation of pipes from the house and the new addition to the septic tank. 08/12/94

PLANS APPROVED BY \_\_\_\_\_ DATE \_\_\_\_\_

COVER NO WORK UNTIL INSPECTED AND APPROVED

NEITHER THE HOWARD COUNTY COUNCIL NOR THE HEALTH DEPARTMENT IS RESPONSIBLE FOR THE SUCCESSFUL OPERATION OF ANY SYSTEM

NOTE: CLEANOUT REQUIRED EVERY 70 FEET OF SEWER LINE AND/OR AT 90° SWEEPS IN LINES FROM HOUSE TO DRAIN FIELDS, 90° ELBOWS NOT ACCEPTABLE.

NOTE: ALL PARTS OF SEPTIC SYSTEMS (I.E. TANK, DISTRIBUTION BOX TRENCHES) TO BE 100 FEET FROM WELL (UNLESS OTHERWISE SPECIFICALLY AUTHORIZED)

NOTE: IF DEEP TRENCH(ES) ARE USED CALL FOR INSPECTION BEFORE AND AFTER PLACING GRAVEL IN TRENCH(ES)

NOTE: NO DRY WELL SHALL EXCEED 15 FOOT IN DIAMETER NO ABSORPTION TRENCH TO EXCEED 100 FEET IN LENGTH

NOTE: ALL PIPE FROM HOUSE TO SEPTIC TANK MUST BE CAST IRON OR SCHEDULE 35/40 PVC OR ABS


PERMIT VOID AFTER TWO YEARS

NOTE: INSTALL STAND PIPE ON SEPTIC TANK AND DRY WELL STAND PIPES MUST BE 6 INCHES IN DIAMETER CAST IRON. CONCRETE OR TERRA COTTA OR PVA OR ABS ACCEPTED. IF TOP OF SEPTIC TANK IS DEEPER THAN 3 FEET. MANHOLE TO GRADE REQUIRED.

NOTE: DISTRIBUTION BOXES MUST HAVE BAFFLES

**\*INSTALLER IS RESPONSIBLE FOR OBTAINING FINAL APPROVAL ON THIS PERMIT**

50215

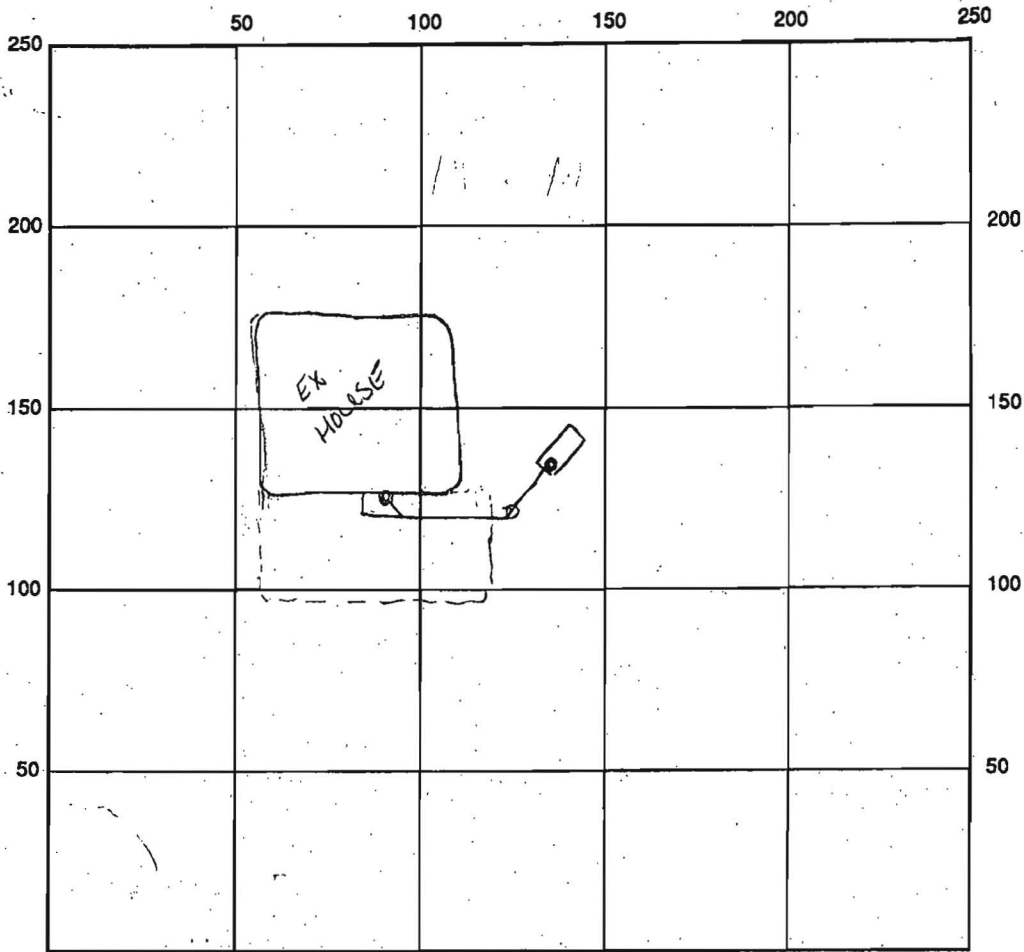

INDICATE NORTH - NAME ADJOINING ROADWAY AS BASE LINE

SEPTIC TANK LEVEL \_\_\_\_\_ CLEANOUTS \_\_\_\_\_

DISTRIBUTION BOX LEVEL \_\_\_\_\_

DRAIN FIELD/TITLE DEPTH \_\_\_\_\_ FT. TRENCH WIDTH \_\_\_\_\_ FT. INLET DEPTH \_\_\_\_\_ FT.

EFFECTIVE GRAVEL DEPTH \_\_\_\_\_ FT. TOTAL LENGTH \_\_\_\_\_ FT.

NUMBER OF TRENCHES \_\_\_\_\_ ONE SIDEWALL/BOTTOM AREA \_\_\_\_\_ SQ. FT.

DRYWALL INSIDE DIAMETER \_\_\_\_\_ FT. EFFECTIVE DEPTH BELOW INLET \_\_\_\_\_ FT.


ABSORBENT AREA \_\_\_\_\_ SQ. FT.

REMARKS: 8/23/94 Cast iron pipe replaced w/ PVC. Cleanout provided outside the proposed addition 10' to cover drum cover

DATE SYSTEM APPROVED 8/23/94 INSPECTOR Amy McMillen

7/26/94

- Well probably in basement
- call owner to confirm
- what work has been done?  
cast iron to PVC

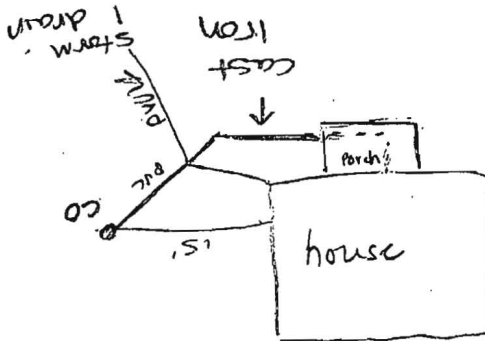

94 JUL 21 PM 2:46

RECEIVED  
HOWARD COUNTY  
HEALTH DEPT.



**VINCE MARINO  
PLUMBING AND HEATING, INC.**

2608 HOFFMAN MILL ROAD  
HAMPSTEAD, MARYLAND 21074

(410) 876-1928

(410) 876-7883

(410) 876-2719 FAX

JULY 28, 1994

AMY L. McMILLEN  
BUREAU OF ENVIRONMENTAL HEALTH  
3525-H ELLICOTT MILLS DRIVE  
ELLICOTT CITY, MD 21043

BAYLESS RESIDENCE, 3574 CHURCH ROAD, ELLICOTT CITY, MD 21043  
465-3483

ALL EXISTING CAST IRON UNDERGROUND SANITARY WASTE LINES WHICH  
EXITS OUT OF EXISTING HOUSE WILL BE COMPLETELY REPLACED WITH  
PVC SCHEDULE 40 PLASTIC PIPE UNDER NEW ADDITION LOCATION AND  
PLUMBER WILL CONNECT ONTO EXISTING PVC PLASTIC DRAIN LINE AT  
NEW SEPTIC TANK WHICH WAS INSTALLED ABOUT 30 DAYS AGO.  
ALL UNDERGROUND DRAIN LINES WILL HAVE 4" OF GRAVEL AROUND  
DIAMETER OF PIPE.

SINCERELY,

VINCE MARINO

*Vince Marino*

CC: M.B. DELP
